

DOCKETED	
Docket Number:	23-OPT-02C
Project Title:	Darden Clean Energy - Compliance
TN #:	271492
Document Title:	Monthly Compliance Report No #13
Description:	DCEP Monthly Compliance Report for June reporting month
Filer:	Eric Schaad
Organization:	Rincon
Submitter Role:	Applicant Consultant
Submission Date:	7/15/2026 5:17:36 PM
Docketed Date:	7/16/2026



Darden Clean Energy Project (23-OPT-02C)

Monthly Compliance Report No. 13,
Reporting Period: June 2026

prepared by

IP Darden I, LLC

IP Darden II, LLC

IP Darden III, LLC

IP Darden IV, LLC

c/o Intersect Power, LLC

9450 SW Gemini Drive, PMB #68743

Beaverton, Oregon 97008

prepared with the assistance of

Rincon Consultants, Inc.

7080 North Whitney Avenue, Suite 101

Fresno, California 93720

July 2026



Table of Contents

1	Introduction.....	1
2	Key Events	2
2.1	Master Key Events List	2
3	Monthly Compliance Report Required Documents	3
4	Reporting Period Updates	6
4.1	Key Construction Events	6
4.1.1	Harlan (BAAH) Switchyard	6
4.1.2	Darden I through IV Photovoltaic-BESS (PVB) Site and Gen-tie	6
4.2	Other Governmental Agency Filings and Submittals	8
4.3	Additions to Onsite Compliance File	9
4.4	Conditions of Certification Updates.....	9
4.4.1	Biological Resources	9
4.4.2	Compliance Conditions and Compliance Monitoring Plan	11
4.4.3	Cultural and Tribal Cultural Resources	12
4.4.4	Facility Design	12
4.4.5	Visual Resources	12
4.5	Two-Month Look-Ahead	13
4.6	Project Incidents and Corrective Actions.....	13

Tables

Table 1	Key Events List.....	2
Table 2	Monthly Compliance Report Submittal Requirements	3
Table 3	Current progress toward major construction tasks is as follows.....	6
Table 4	DCEP Progress Tracker	7

Appendices

Appendix A	Master WEAP Training Attendance List – June 2026
Appendix B	June 2026 - Daily Monitoring Summary Table
Appendix C	Harlan Switching Station Compliance Report – June 2026
Appendix D	COM-5 COC Tracking Table
Appendix E	DCBO Approval of Drainage Structures, Grading Plan, Erosion and Sediment Control Plan, Soils Report (CIVIL-1)
Appendix F	DCBO Approval of Electrical Design Package and Studies (ELEC-1)
Appendix G	DCBO Approval of Structural Package Revision (STRUC-1)
Appendix H	Darden Equipment List – June 2026 (SWITCH-GHG-01 / AQ-SC-5)
Appendix I	Darden Hazardous Waste Manifest (SWITCH WASTE-1)
Appendix J	Darden Safety Report (Worker Safety-3)
Appendix K	DCBO Approval of Minor Revisions to IFC Gen Tie Design Package (TSE-4)
Appendix L	DCBO Approval of Solar Canopy Plans
Appendix M	Department of Parks and Recreation Archaeological Reports

This page intentionally left blank.

1 Introduction

The Darden Clean Energy Project (DCEP) is a 1,150 MW solar photovoltaic (PV) facility, a 4,600 MW-hour battery energy storage system (BESS), a step-up substation, a generation-intertie line, and a switchyard on approximately 9,500 acres in western Fresno County, California.

Provided by California AB 205, the California Energy Commission (CEC) has the statutory authority to certify solar photovoltaic, and other facilities, for construction and operation in lieu of any permit, certificate, or similar document required by a state, local, or regional agency, or federal agency, to the extent permitted by federal law, for those facilities, that Opt-in to a thorough review process by CEC staff. DCEP was certified for construction and operation by the CEC on June 11, 2025. Pursuant to the Conditions of Certification (COCs) identified in the CEC's Staff Assessment and Final Order certified on June 12, 2025, and published to the project's docket (23-OPT-02), this is the Monthly Compliance Report (MCR) to the CEC's Compliance Project Manager (CPM). This MCR will include details of recent or upcoming submittals to the CPM, Delegate Chief Building Official (DCBO), and/or other relevant authorities, as required by the COCs.

Project construction activities at the Breaker-and-a-Half (BAAH) in June included ongoing civil activities and construction of switchyard structural features (Section 4.1). Biological resources were monitored daily in June, and archaeological and paleontological monitors were on site for 23 days. Two Environmentally Sensitive Area (ESA) buffers are designated at the BAAH, one associated with a red-tailed hawk (*Buteo jamaicensis*) nest located in a transmission tower west of the project site, and the other associated with a house finch (*Haemorrhous mexicanus*) nest in a piece of equipment near the construction office trailer (Section 3, Table 2). Worker Environmental Awareness Program (WEAP) training is ongoing as needed and is provided in person via the recorded WEAP (Appendix A). The summary table for June WEAP attendance and the cumulative tally of staff participation in the WEAP training are included in Appendix A. The summary table of daily monitoring activities is provided as Appendix B.

Project construction activities at the Darden PV/BESS project site in June included continuing work on the 12kV scope, as well as gen-tie, substation, civil, and solar construction activities (Section 4.1). Full-time biological monitoring has been implemented for work occurring within reduced buffers. Biological and archaeological monitoring occurred daily, and paleontological monitoring was conducted as needed throughout June (Appendix B). The CEC approved "batch" Buffer Reduction Requests (BRR) for Swainson's hawk on June 22, and for burrowing owl and general nesting birds on June 25, which apply to all existing and future nests on the project site through the 2026 nesting season. Environmentally Sensitive Areas are demarcated throughout the project site, including seven ESAs for Swainson's hawk nesting, ESAs for burrowing owl, including the Area 3 and Area 15 protected berm locations, and numerous ESAs for common birds, including mourning dove, lesser nighthawk, killdeer, red-tailed hawk, northern harrier, barn owl, great horned owl, American kestrel, Say's phoebe, western kingbird, loggerhead shrike, common raven, horned lark, northern mockingbird, red-wing blackbird, and western meadow lark. To date, 48 buffer reductions have been authorized by the CEC and are implemented in the field, of which 15 were authorized in June. WEAP training has been provided in-person via the recorded WEAP. The summary table for June WEAP attendance and the cumulative tally of staff participation in the WEAP training are included in Appendix A.

2 Key Events

Project: Darden Clean Energy Project

Docket Number: 23-OPT-02C

Compliance Project Manager: Joseph Douglas

2.1 Master Key Events List

Table 1 Key Events List

Event Description	Date
Certification Date	6/12/2025
Finalize Land Sale Transaction	10/15/2025
On-line Date	3/31/2028
Site Activities	
LNTP Issued for BAAH	10/24/2025
Start Site Mobilization/Construction (Harlan Switchyard only)	10/29/2025
Began staking Limits of Disturbance (COC BIO-7)	10/31/2025
CEC Approval for Pre-seeding Activities Issued	11/25/2025
Start Site Assessment/Pre-construction/Pre-seeding	12/1/2025
Start Site Mobilization/Construction (Darden)	2/1/2026
12kV Line Installations for Office Trailer Complex	3/13/2026
Begin Driving Steel Foundations	3/31/2026
Begin Installation of Major Equipment	4/13/2026
First Start/Energizing of PV Array or BESS	4/22/2027
Obtain Building Occupation Permit	5/19/2028
Start Commercial Operation	3/31/2028
Complete All Construction	3/24/2028
Transmission Line Activities	
Gen-tie Route Tree Clearing	12/8/2025
Start Transmission Line Construction	4/13/2026
Complete Transmission Line Construction	3/24/2027
Synchronization with Grid and Interconnection	4/22/2027

3 Monthly Compliance Report Required Documents

Table 2 provides a list of documents and information required to be submitted with each Monthly Compliance Report.

Table 2 Monthly Compliance Report Submittal Requirements

COC Number	Document or Description	Location in MCR
AQ-SC-3	Fugitive Dust Control	Mortenson has continued to conduct trainings, provide available resources, monitor site conditions, and implement dust control measures (such as use of water trucks for non-stabilized/seeded ground) as required by AQ-SC-3 and WS-11.
BIO-5, PAL-5, CUL-3, SWITCH CUL-3	Master WEAP Training Attendance List	Appendix A
BIO-2	Summary of daily monitoring activities	Appendix B
BIO-6, CUL-4, PAL-6, SWITCH CUL-4	Implementation of BRMIMP Measures, survey results, construction activities monitored, non-compliance incidents and resolutions, species observed, and sensitive paleontological or cultural resources observed.	Appendix B Biological, archaeological, and paleontological monitoring of construction activities occurred throughout the month, including where nest buffer reductions have been authorized by the CEC. Construction activities within reduced buffer areas included civil and solar scopes, and vegetation management. Refer to <i>Section 4.6 Project Incidents and Corrective Actions</i> for details regarding ESA buffer encroachments that occurred in June.
BIO-7	General Impact Avoidance Measures	During all work activities, monitors ensured avoidance measures were implemented on site, including maintaining all construction activities and staging within LODs, ensuring BMPs are in place and maintained, inspecting trenches/holes for appropriate ramping/covering, capping or covering staged pipes and other materials, containing and removing trash, ensuring ESA buffers were avoided, maintaining speed limits, ensuring dust plumes were avoided, and implementing SWPPP procedures as needed during storm events. See Section 4.4.2 for submittals and approvals under COC BIO-7. On May 18, 2026, a request for authorization to use a non-toxic hydraulic mulch soil binder was submitted to the CPM and was approved on May 21, 2026.
BIO-8	Nesting Bird Avoidance and Minimization Measure	Daily nesting bird sweeps are conducted ahead of work in areas where nesting is known or likely (e.g., presence of ground vegetation and gravel, adjacent to trees). Nests of the following species have been identified: mourning dove, lesser nighthawk, killdeer, red-tailed hawk, northern harrier, barn owl, great horned owl, American kestrel, Say's phoebe, western kingbird, loggerhead shrike, common raven, horned lark, northern mockingbird, red-wing blackbird, and western meadow lark.

COC Number	Document or Description	Location in MCR
		Refer to <i>Section 4.4, Conditions of Certification Updates</i> , for details on buffer reduction requests authorized by the CPM in June.
BIO-10	Swainson's Hawk Impact Avoidance, Minimization, and Mitigation Measures for Take	Eight pairs of SWHA have been documented nesting on the project site, including a new nest (along South Butte Avenue) reported to the CEC on 6/12/2026. Two SWHA nests have been unsuccessful to date: one along Sonoma Ave, outside the project site, adjacent to a residential/commercial area and a bus stop, and one adjacent to a great horned owl nest. Refer to <i>Section 4.4 Conditions of Certification Updates</i> for details regarding buffer reduction requests authorized by the CPM in June.
BIO-12	BUOW Plan	Refer to <i>Section 4.4 Conditions of Certification Updates</i> for details regarding buffer reduction requests authorized by the CPM in June.
CIVIL-1	DCBO Approval of Drainage Structures, Grading Plan, Erosion and Sediment Control Plan, Soils Report	Appendix E
COM-5	Compliance Matrix	Appendix D
COM-6	June MCR	Section 2, Table 1 Key Events List
	Harlan Switching Station Compliance Report June 2026	Appendix C; Page 3
CUL-5	Unanticipated Discovery of Cultural or Tribal Cultural Resources	Appendix M
ELEC-1	DCBO Approval of Electrical Design Package and Studies	Appendix F
GEN-2	Harlan Switching Station Compliance Report June 2026	Appendix C; Page 5
	June MCR	Section 4.1.2, Table 4 DCEP Schedule Progress Tracker
STRUC-1	DCBO Approval of Structural Package Revision	Appendix G
SWITCH-AQ-1 / AQ-SC-4	Harlan Switching Station Compliance Report June 2026	Appendix C; Page 17
SWITCH-GHG-1 / AQ-SC-5	Harlan Switching Station Compliance Report June 2026	Appendix C; Page 19
	Darden – PVB	Appendix H

COC Number	Document or Description	Location in MCR
	Equipment List	
TRANS -2	Darden – PVB Hazardous Waste Manifest	Appendix I
TSE-4	Transmission System Engineering	Appendix K
WATER-6	Harlan Switching Station Compliance Report June 2026	Appendix C; Page 21
	Darden – PVB	The Darden Clean Energy Project has used a total of 14,656,300 gallons of water for the month of June
Worker Safety-3	Harlan Switching Station Compliance Report June 2026	Appendix C (Includes NOISE-02, Worker Safety-11, and SWITCH HAZ-02); Page 22
	Darden – PVB Safety Report	Appendix J

4 Reporting Period Updates

The following updates are for the Reporting Period of June 1 through 30.

4.1 Key Construction Events

4.1.1 Harlan (BAAH) Switchyard

The Harlan (BAAH) Switchyard is currently under active construction, and the following activities occurred in June:

- Conduit excavation and trenching
- Continued drilling and pouring of foundations
- Installation and completion of structural fill and the retention basin
- MPAC building currently undergoing wiring activities
- Above-grade electrical work including steel erection and the installation of hard bus and insulators
- Microwave tower foundations are poured

Table 3 Current progress toward major construction tasks is as follows

Task	Status
Site preparation BMPs	100% complete
Stripping organics across site	100% complete
Pad over-excavation	100% complete
Pad cut / fill / compaction	95% complete
Access road installation	100% complete
Foundation Survey	100% complete
MPAC Foundation	100% complete
Cut in road/add base rock	60% complete
Installation of Rip Rap	80% complete
Foundation Installation	77% complete
MPAC Building Installation	67% complete
MPAC Internal Wiring	35% complete
Conduit Installation	45% complete
Steel Erection	76% complete
Insulator Installation	25% complete
Bus Installation	10% complete

The summary of WEAP training attendance is provided in Appendix A. Biological resources were monitored daily in June, and archaeological and paleontological monitors were on site for 23 days (Appendix B).

4.1.2 Darden I through IV Photovoltaic-BESS (PVB) Site and Gen-tie

Activities conducted in June consisted of:

- **12kV:** Trenching work concluded in the month of June, as the entire 12kV trench layout was completed in mid-June. There is still some outstanding pad mount transformer installation/termination work to be performed; however, most of the work that can be done has been completed at this time.

- **Gen-Tie:** The month of June marked the start of the foundations scope. The crews have completed foundations (minus structures affected by ESA buffers) all the way from structure 80 to 54. The crews have poured 24 foundations (roughly 25% of total piers).
- **Substation:** To date, 2 cap banks, 24 circuit breaker foundations and 64 piers have been successfully poured in Darden III and Darden IV of the substation. The foundation and pedestal for the HICO Main Power Transformer (MPT) in Darden III have also been completed. Additionally, the team has installed over 75 conduit runs throughout the substation.
- **Civil:** During the month of June, the Civil SOW advanced in Darden I & II access roads, basins, perimeter control, and laydown yards, and inverter apron subgrades commenced.
- **Solar:** Receiving of electrical material, piles, tracker material and modules for Darden III and IV. Site – buildout of area 12 laydown yard. DIII – Site fencing install, MV home run and skid to skid installation, distribution and install of inverter/priority and racking piles, receiving and placement of tracker material, inverter subgrade (excavation, conduit install, DC wire install, slurry and backfill), LBD box install, tracker material distribution, torque tube distribution, tracker final assembly, module offload and distribution, module installation and support, harness installation, messenger wire install, LBD 750kcmil terminations, junction box install and MV splicing. DIV – Site fencing install, MV home run and skid to skid installation, distribution and install of inverter/priority piles and racking piles, receiving and placement of tracker material, inverter subgrade (excavation, conduit install, DC wire install, slurry and backfill), tracker material distribution, torque tube distribution, tracker final assembly, module offload and distribution, module installation and support, LBD box install and 750kcmil terminations, junction box install and MV splicing.

The summary of WEAP training attendance is provided in Appendix A. Biological and archaeological monitoring occurred daily, and paleontological monitoring was conducted as needed throughout June (Appendix B).

Table 4 DCEP Progress Tracker

Task Name	UOM	Percent complete
External Access Roads - Pioneering	LF	97%
External Access Roads - Subgrade Preparation	LF	95%
External Access Roads - Aggregate Placed	LF	88%
Internal Access Roads - Pioneering	LF	89%
Internal Access Roads - Subgrade Preparation	LF	89%
Internal Access Roads - Aggregate Placed	LF	78%
Laydown Yards - Aggregate Placed	LF	99%
BMPs - Perimeter Control	HR	74%
BMPs - Diversion Berms	LF	51%
Detention Basin Install	EA	46%
Substation Pad	LF	100%
BESS (DAR I & II) Pad	EA	100%
BESS (DAR III & IV) Pad	EA	100%
Gen-Tie ROW Clearing	EA	100%
12kV - Trenching	LF	100%
12kV - Cable Install	LF	100%
12kV - Pole Install	EA	100%
Equipment Setting	EA	65%

Darden Clean Energy Project (23-OPT-02C)

Foundation Surveying	EA	100%
ROW Clearing	EA	100%
Drilling/Excavation Completed	EA	14%
Engineered Fill Installed	EA	25%
Rebar Completed	EA	11%
Concrete Pour	EA	10%
Backfilling	EA	3%
Below Grade Conduit	LF	15%
Install - Piles	EA	18%
Racking/Tracker Assembly	EA	6%
Module Rails Install	EA	6%
Install - Drive Motors	EA	12%
Install - Modules	EA	2%
Harness Install	EA	1%
MV Terminations	EA	1%
MV Plowing	EA	1%
MV Sectionalizing Cabinets	EA	46%
Inverter Station Subgrade	EA	19%
Combiner Box Raceway & Box Installation	EA	8%
Combiner Box Terminations		1%
Priority Pile Install	EA	75%
Aux Control Panel (ACP) Pile Install	EA	50%
MV Bullhorn Install	EA	56%
FNE Conduit Install	LF	50%
Ground Grid Install	EA	40%
Production Piles	EA	14%
FNE Rack prefab	EA	13%
Common Trench Excavation	EA	18%
MV Bullhorn Prefab	EA	18%
Priority Pile Install	EA	75%
ACP Pile Install	EA	50%
MV Bullhorn Install	EA	56%

4.2 Other Governmental Agency Filings and Submittals

Coordination is ongoing with Fresno County Staff, San Joaquin Valley Air Pollution Control District staff, and Fresno County Fire Protection District, as needed, regarding applicable filings and permits needed.

- No filings were submitted to Other Agencies for Harlan in the month of June.
- Filings for the Darden PVB site include:
 - Encroachment Permits:
 - Directional & Site Signage – Issued
 - Primary Construction Entrances – Issued
 - Covers street sweeping operations
 - Road Improvements – Issued

- School Bus Stop Encroachment – Issued
- Gen-Tie Entrances – Issued
- Mowing Signage – Issued
- SWPPP/NOI – Issued
- I-5 Encroachment – Issued
- DCBO Approval of Solar Canopy Plans (Appendix L)

4.3 Additions to Onsite Compliance File

The following are additions to the on-site compliance file for the DCEP:

- NOISE-02: Noise Pollution Training Log
- Worker Safety-03: General Site Safety Inspection & Certification
- Worker Safety-11: Valley Fever Training Log; Air Quality Monitoring & Inspections

4.4 Conditions of Certification Updates

This section summarizes only the significant updates to the status of compliance for each COC, categorized by technical resource area. Minor updates and progress comments are included in Appendix D, Compliance Matrix.

4.4.1 Biological Resources

BIO-1: Designated Biologist Selection

If a Designated Biologist needs to be replaced, the specified information regarding the proposed replacement must be submitted to the CPM at least ten working days prior to the termination or release of the preceding Designated Biologist.

- Resumes were submitted to the CEC on 6/5/2026, 6/12/2026, and on 6/26/2026 for authorization of additional designated biologists.

BIO-2: Designated Biologist Duties

The Designated Biologist shall submit in the MCRs to the CPM copies of all written reports and summaries that document construction activities that have the potential to affect biological resources. The Designated Biologist's written records will be made available for the CPM's inspection on request at any time during normal business hours.

- Refer to *Section 4.6 Project Incidents and Corrective Actions* for details regarding ESA buffer encroachments that occurred in June.

BIO-3: Biological Monitor Selection

If additional biological monitors are needed during construction or for species specific surveys, the specified information shall be submitted to the CPM for approval at least 10 days prior to their first day of monitoring activities.

- Additional resumes submitted to CEC on 6/5/2026 and 6/26/2026 to aid in support of increased levels of construction and nesting activity.

BIO-8: Nesting Bird Avoidance and Minimization Measure and Tricolored Blackbird Avoidance and Minimization Measures

Pre-construction nest surveys shall be conducted if pre-construction site mobilization or construction shall initiate during the breeding season, from February 1 through September 15.

- 5) Any nest buffer reduction would require full-time monitoring if reduced from the levels identified in the approved NBMP.
- Nine buffer reduction requests were authorized by the CPM in June for general nesting birds, including a “batch” BRR approved on June 25 that applies to all existing and future nests on the project site through the 2026 nesting season.

In addition to buffer reduction approvals, the CEC approved the following four amendments to previously approved buffer reduction requests:

- A request for modification of an approved GHOW nest ESA buffer reduction (approved by CEC on 3/27/2026, and subsequent BRR amendment approved on 5/14/2026) was submitted to CEC on 6/4/2026, which would allow for increased levels of construction within the reduced ESA buffer. The CEC approved the buffer reduction on 6/9/2026.
- A request for modification of a HOFI nest ESA buffer was submitted to CEC on 6/4/2026.
- A request for modification of an approved GHOW nest ESA buffer reduction (approved by CEC on 3/4/2026) was submitted to CEC on 6/15/2026, which would allow for increased levels of construction within the reduced ESA buffer.

BIO-10: Swainson’s Hawk Impact Avoidance, Minimization, and Mitigation Measures

Item 4: Swainson’s Hawk Nest Buffers. Except for limited vehicle access as prescribed below, the project owner and Designated Biologist(s) shall ensure that no project activities occur within 100 feet of a Swainson’s hawk nest during the nesting season (February 15 through September 15). The 100-foot no disturbance buffer shall not be reduced or otherwise modified without prior written CPM approval. Worker foot traffic, water and restroom facilities, employee break areas (permanent or temporary), and worker vehicle parking is prohibited within 1,000 feet of any Swainson’s hawk nest without prior written CPM approval.

- Three buffer reductions were approved by the CEC in June for SWHA buffers, including a “batch” BRR approved on June 22 that applies to all existing and future SWHA nests on the project site through the 2026 nesting season.

In addition to buffer reduction approvals for SWHA nests, the CEC approved the following three amendments to previously approved buffer reduction requests:

- A notification was sent to the CPM on 6/12/2026 regarding identification of an active SWHA nest along South Butte Avenue at the eastern edge of the project boundary, including confirmation that buffers and monitoring will be initiated.
- A request for modification of an approved SWHA nest ESA buffer reduction (approved by CEC on 5/26/2026) was submitted to CEC on 6/15/2026, which would allow for increased levels of construction within the reduced ESA buffer.

- A request for modification of an approved SWHA nest ESA buffer reduction (approved by CEC on 5/18/2026) was submitted to CEC on 6/15/2026, which would allow for increased levels of construction within the reduced ESA buffer.

BIO-12: Burrowing Owl Impact Avoidance, Minimization, and Take Mitigation Measures

The project owner shall implement the following measures to avoid, minimize and offset impacts to breeding and foraging burrowing owls during construction and operation, and decommissioning:

6e) If the Designated Biologist determines that specific project activities are not likely to affect the burrowing owl using known or nesting burrowing owl burrows due to the nature of the specific project activities and/or due to objects or topography that might reduce potential noise disturbance and obstruct view of the project activities from the nest, then the Designated Biologist may email a written request to the CPM to reduce the buffer distance with documented observational data (Buffer Reduction Request).

- Three BRRs were approved by the CEC for BUOW in June, including a “batch” BRR approved on June 25 that applies to all existing and future SWHA nests on the project site through the 2026 nesting season.
- A notification was sent to the CPM on 6/3/2026 regarding identification of a fourth occupied BUOW nest at the complex associated with 5/22/2026 Buffer Reduction Request, which was previously approved by the CEC on 5/28/2026; the CEC responded on 6/5/2026 that the presence of a fourth burrow does not alter the protective measures in the approved BRR, and that the DB is encouraged to consider additional hay bale visual barrier installation as necessary.
- A notification was sent to the CPM on 6/15/2026 regarding identification of a fifth occupied BUOW nest located at the complex associated with the 5/22/2026 Buffer Reduction Request and 6/3/2026 amendment, including confirmation that the same previously approved buffers and visual barriers would be implemented for the new occupied burrow. The CEC responded on 6/16/2026 that the presence of a fifth burrow does not alter the protective measures in the approved BRR, and that the DB is encouraged to consider additional hay bale visual barrier installation as necessary.

4.4.2 Compliance Conditions and Compliance Monitoring Plan

COM-5: Compliance Matrix

The project owner is required to submit a compliance matrix to the CPM with each MCR and ACR.

- Refer to Appendix D, Compliance Matrix.

COM-6: Monthly Compliance Report

During pre-construction, construction, or closure, the project owner or authorized agent shall submit an electronic searchable version of the MCR to the CPM within 10 business days after the end of each reporting month.

- This MCR is being submitted in accordance with COM-6.

4.4.3 Cultural and Tribal Cultural Resources

CUL-5: Unanticipated Discovery of Tribal or Cultural Resources

Should there be an unanticipated discovery of cultural or tribal cultural resources, the CRS shall comply with state law and any provisions described in the CTCRMMP. The CRS shall notify CEC within 24 hours of the discovery and invite CEC's participation in the resolution of the find.

- Notification of unanticipated cultural resource (archaeological isolate) identification and proposed prescriptive treatment submitted to CEC on 6/3/2026. Approval of prescriptive treatment received from CEC on 6/3/2026.
- Notification of unanticipated cultural resource (archaeological site) identification and proposed treatment submitted to CEC on 6/4/2026. CEC archaeologist recommended CPM approve of the proposed treatment on 6/4/2026.

4.4.4 Facility Design

CIVIL-1: Drainage Structures, Grading Plan, Erosion and Sediment Control Plan, Soils Report

In the next MCR following the DCBO's approval, the project owner shall submit a written statement certifying that the documents have been approved by the DCBO.

- DCBO approval received on 6/8/2026 (Appendix E).

ELEC-1: Electrical Design Package and Studies

The project owner shall include in this submittal a copy of the signed and stamped statement from the responsible electrical engineer attesting compliance with the applicable LORS and shall send the CPM a copy of the transmittal letter in the next MCR.

- DCBO approval received on 6/16/2026 (Appendix F).

STRUC-1: Final Design Plans, Specification and Calculations

The project owner shall submit to the CPM, in the next MCR, a copy of a statement from the DCBO that the proposed structural plans, specifications, and calculations have been approved and comply with the requirements set forth in applicable engineering LORS.

- DCBO approval received on 6/5/2026 (Appendix G).

4.4.5 Visual Resources

VIS-1: Exterior Surface Coating, Color, Finish, and Materials Plan

a. The project owner shall submit an exterior surface coating, color, finish and materials plan to the CPM for approval and simultaneously to the Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase coating, color,

finish and materials with a vendor. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM.

b. If the CPM determines that the exterior surface coating, color, finish, and materials plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM.

- Submitted updated details pertaining to exterior paint coating for the Tesla OMI for Darden PV/BESS to CEC on 6/26/2026.

4.5 Two-Month Look-Ahead

Over the next two months, the following compliance activities are scheduled, and the project owner will make the following compliance filings, as needed:

- BIO-8: Nesting Bird Preconstruction Surveys, as needed, depending on work schedule and ongoing site disturbance. Surveys will be performed according to COC BIO-8(2) – ongoing
- BIO-10: Swainson's Hawk Preconstruction Nesting Survey – ongoing
- CBA-02: Progress Reports regarding the implementation of the Darden Project Local Investment Program
- CIVIL-04: Final Grading Plans, and the responsible civil engineer's signed statement that the installation of the facilities and all erosion control measures were completed in accordance with the final approved combined grading plans, and that the facilities are adequate for their intended purposes.
- COM-09: CEC annually adjusted compliance fee
- ELEC-1: Final Plant Design and Calculations
- STRUC-1: Final Plant Design, Specifications, and Calculations for substations, BESS, and O&M buildings
- WORKER SAFETY-9: Fire Protection System Specifications and Drawings

4.6 Project Incidents and Corrective Actions

No safety incidents occurred, and no safety-related corrective actions were required in June 2026.

Notification of two ESA buffer encroachments that occurred on 6/3/2026 (American Kestrel nest located outside of project boundaries adjacent to a commercial building) and 6/4/2026 (western kingbird nest along S. Yuba Avenue) was submitted to CEC on 6/4/2026. The CEC responded on 6/9/2026 with a request for anticipated ESA Sensitivity Awareness training content; details regarding the ESA-focused training were submitted to CEC on 6/12/2026, which include: installing prominent, highly visible ESA signage along roadways where traffic barriers are infeasible, and installation of prominent T-post and high-visibility rope where solid barriers can be used. Additionally, the project owner and contractor are collaborating on an ESA Sensitivity Awareness training to reinforce the WEAP training and to be administered to personnel during site orientation training prior to any work being performed.

Notification of a barn owl nest ESA buffer encroachment that occurred on 6/12/2026 was submitted to CEC on 6/12/2026. Corrective actions taken include altering the type of ESA staking to provide a greater level of physical blockage and adding extra signage for heightened visibility. Additionally, the project owner and contractor have committed to providing additional ESA Sensitivity Awareness training that

will be held for current employees on 6/16/26 and included during the EPC's First Day First Hour Orientation for new employees.

Notification of a SWHA nest ESA buffer encroachment that occurred on 6/15/2026 was submitted to CEC on 6/16/2026. Corrective actions taken include having dedicated traffic control personnel stationed at the main site entrance until all deliveries have been completed for the day.

Notification of a western kingbird nest ESA buffer encroachment that occurred on 6/18/2026 was submitted to CEC on 6/19/2026. Corrective actions taken include enhancing the visibility and delineation of ESA boundaries across the project site, particularly in areas such as this where public roads intersect with ESA areas. This includes supplementing existing barriers with items such as rope, extra flagging, extra signage, and traffic cones (this was implemented at the western kingbird buffer immediately after the ESA encroachment was notified to the contractor team). These actions are being implemented to strengthen environmental controls, improve site awareness, and ensure the continued protection of sensitive resources in full compliance with CEC requirements. In the event specific individuals are identified as responsible for ESA encroachments, the contractor's Action Evaluation Model will be enacted to ensure appropriate corrective actions are taken.

Notification of a SWHA nest ESA buffer encroachment that occurred on Saturday, 6/20/2026, was submitted to CEC on 6/22/2026. Corrective actions taken include holding a dedicated meeting (already occurred) to discuss the contractor's needs for laydown yard access and dedicated entry points when work is scheduled in other project areas, to ensure that proper biological monitoring coverage is planned. Additionally, the contractor's Action Evaluation Model will be enacted to ensure appropriate corrective actions are taken.

This page intentionally left blank.

Appendix A

Master WEAP Training Attendance List – June 2026

WEAP Training Attendance Master List

Total WEAP trainees for reporting month (June):	296
Total WEAP trainees for DCEP:	802

Date	Project Phase	Full Name	Company	Training Administered
6/1/2026	Darden PV/BESS	Jordan Bermudez	Mortenson	ENV/SWPPP; Bio; CR; PAL
		Aaron Slover	Mortenson	
		Hugo Romo	Mortenson	
		Erik Perez	Mortenson	
		Derrick Juarez	Mortenson	
		Thomas Moncton	Mortenson	
		Nicholas Jorge	Mortenson	
		Leelan Sewell	Mortenson	
		Jason Murrell	Mortenson	
		Adam Ortega	Mortenson	
		Aaron Palomera	Mortenson	
		Antonio Ayon	Mortenson	
		Angel Alonso	Mortenson	
		Dallas Sanchez	Mortenson	
		Jose A. Gomez	Mortenson	
		Ruben Gonzalez	Mortenson	
		Jesus Lopez	Mortenson	
		Joel Estrada	Mortenson	
		Jake Garcia	Mortenson	
		Michael Figueroa	Mortenson	
		Ricardo Figueroa	Mortenson	
		Angel Lopez	Mortenson	
		Jaylin Hill	Mortenson	
		Jose Rios	Mortenson	
		Samuel Gomez	Mortenson	
		Bryan Rosas	Mortenson	
		David Mcbath	Mortenson	
		Josue Pimental	Mortenson	
		Aristeo Ceruantes	Mortenson	
		Alvis Guzman	Mortenson	
		Gibta Lopez	Mortenson	
		Johnny Mendez	Mortenson	
		Arthur Gentel	Mortenson	

Date	Project Phase	Full Name	Company	Training Administered
		Reme Hernandez	Mortenson	
		Albert Richardson	Mortenson	
		Jonathan Richmond	Mortenson	
		Jonathan Rojas	Mortenson	
		Erick Martinez	Mortenson	
		Jaylin Hill	Mortenson	
		Brian Miranda	Mortenson	
		Robert Volker	Mortenson	
		Ethan Ibbs	Mortenson	
		Armando Melendrez	Mortenson	
		Angel Rodriguez	Mortenson	
		German Angel	Mortenson	
		Alejandro Martinez	Mortenson	
		Jose E. Lucas	Mortenson	
		Eleazar Vasquez	Mortenson	
		Jamey Guillermo	Mortenson	
		Nicholas Luna	Mortenson	
		Raul Jimenez-Tostado	Mortenson	
		Eric Gonzalez-Marcial	Mortenson	
		Michael Snell	Mortenson	
		Jarrett Sparks	Mortenson	
		Abel Perez	Mortenson	
		Benjamin Santiago	Mortenson	
		Alexander Almendarez	Mortenson	
		Mogelio DeLaTorre	Mortenson	
		Jose Palacios	Mortenson	
		Gerardo Ortega-Lamas	Mortenson	
		Edwin Martinez	Mortenson	
		Christian Basulto	Mortenson	
		Mark Stover	Mortenson	
		Joseph Cooper	Mortenson	
		Niko Baca	Mortenson	
		Ruben Vasquez	Mortenson	
		Francisco Lamas	Mortenson	
		Antonio Hernandez	Mortenson	
		Favian Moreno	Mortenson	
		Freddy Medina	Mortenson	
		Anthony Cuen	Mortenson	
		Blake Perry	Rincon/Summit West	

Date	Project Phase	Full Name	Company	Training Administered
6/1/2026 - 6/5/2026	BAAH/Access	Noah Howard	Mortenson	ENV/SWPPP; Bio; CR; PAL
		Andrew Mantoya	Dacon	
		Blake Vandevort	GTS	
		Justin Elliott	GTS	
		Stanislav Tinden	Dacon	
		Samson S.	GTS	
		Miriam Dominguez	ABB	
		Joseph Cavazes	Dacon	
6/8/2026	Darden PV/BESS	Genaro Gaytan	Not Provided	ENV/SWPPP; Bio; CR; PAL
		Miguel Palma	Not Provided	
		Zachrey Polston	Profoam	
		Aldelio Daza Vera	Not Provided	
		Luis Alvarez	Not Provided	
		Adrian Jimenez	Not Provided	
		Alexsis Gomez	Not Provided	
		Ernesto Sifuentes	Not Provided	
		Manuel Gomez	Not Provided	
		Derek Aguilar	Not Provided	
		Ana Ortuno	Not Provided	
		Daniel Williams	Not Provided	
		Moises Raiz Jr.	Not Provided	
		Fernando Diaz	Not Provided	
		Pedro Guzman	Not Provided	
		Ricky Heath	Not Provided	
		William Gale	Not Provided	
		Juan Jimenez	Not Provided	
		Felix Ponce	Not Provided	
		David Simerez	Not Provided	
		Marco Urrea-Zarala	Not Provided	
		Caleb Thiele	Not Provided	
		Roberto Olmedo	Not Provided	
		Yuri Yanovsky	Not Provided	
		She Simms	Not Provided	
		Nick Zandes	Not Provided	
		Robert Ackerman	Not Provided	
		Victor Abel Villa	Not Provided	
		Carlos Guererro	Mortenson	
		Jake Haase	Mortenson	
		Cervando Sanchez	Mortenson	

Date	Project Phase	Full Name	Company	Training Administered
		Shannon Furtado	Mortenson	
		Jose Molinero	Mortenson	
		Kristopher Gareca	Mortenson	
		Cody Cosca	Mortenson	
		Frank Raiz	Mortenson	
		Efrain Raiz	Mortenson	
		Steven Mello	Mortenson	
		John Young	Mortenson	
		Corry Harper	Mortenson	
		Adam Tapia	Mortenson	
		Earl Frierra-Jackson	Mortenson	
		Ricardo Rodriguez	Mortenson	
		Edgar Centos	Mortenson	
		Jeremiah Reddick	Mortenson	
		Scott Lawson	Mortenson	
		Michael Paz	Mortenson	
		Anthony Veliz	Mortenson	
		David Salazar	Mortenson	
		Miguel DeLaCruz	Mortenson	
		Kurtis Batey	Mortenson	
6/10/2026	Darden PV/BESS	Katerina Alexis-Konstentiniadis	Rincon	ENV/SWPPP; Bio; CR; PAL
		Sarah Hignojuz	IBEW	
		Reyes Soto	IW	
		Daniel Rule	Mortenson	
		Jose Rojas II	Mortenson	
		Cory Newsome	IBEW	
		William Kelly Nichols	Mortenson	
		Carlos Rodriguez	Mortenson	
		Aaron Sanchez	Mortenson	
		Benjamin Garcia	IW	
		Orlando Lindholm	IW	
		Sebastian Molinero	IW	
		Raymond Abina	IW	
		Noel Garza	IW	
		Rey Del Rexi	JIW	
		Jason Sanders	IBEW	
		Steven Correia	Mortenson	
		Nathaniel Harris	IW	
		Brian Verduzco	IW	

Date	Project Phase	Full Name	Company	Training Administered
6/17/2026		Frank Errecalde	IBEW	
		Adrian Arredondo	PTC	
		Jakell Tomlin	IBEW	
		Juan Villa	Mortenson	
		Isan Mendoza	IBEW	
		Gustavo Arreola	IBEW	
		Carlos Perez	Mortenson	
		Mariano Rodriguez	Mortenson	
		Fabian Torres	Mortenson	
		Jonathan Suggs	IBEW	ENV/SWPPP; Bio; CR; PAL
	Darden PV/BESS	Brian Gasca	Local 294	
		Isabel Barajas	IBEW	
		Antonio Miranda	JIW 155	
		Joan Carillo Cruz	IBEW 100	
		Janiah Sanders	IBEW 100	
		Gerardo Felix	IBEW 100	
		Omar Cortes	IBEW 100	
		Johnny Mararicia	Local 3	
		Marcos Angelo Reyna	IBEW 100	
		Pablo Moreno	IBEW 100	
		Isaiah Barajas	IBEW 100	
		Abraham Moreno	Local 220	
		Torie Wyatt	IBEW 100	
		Alejandro Ochoa	IBEW 100	
		Anthony Mascorro	IBEW 100	
		Diego Carlos Preciado	IW 155	
		George Rios Rodriguez	IBEW	
		Kyle McIntosh	JIW 155	
		Rodriguez Carlos	JIW 155	
		Miguel Perez	Local 294	
		Francisco Javier Vargas	Local 294	
		Maria Elena Malagon Gomez	Local 294	
		Leticia Rodriguez	Local 294	
		Jorge Hernandez	JIW 155	
		Adan Mariscal	IBEW 100	
		Demojiah Williams	IBEW 100	
		J. Sacramento Mendoza	JIW 155	
		Trevaun Price	IBEW 100	
		Joshua Angelo	IBEW	

Date	Project Phase	Full Name	Company	Training Administered
		Douglas Smith	IBEW	
		Rande Ferguson	WC3	
		Charles Gibbons	Rincon	
		Bobby Luangrath	Bancroft	
		Isaac Kreger	Rincon	
		Michael Hahn	Optics Bio	
		Kinur Amador	IBEW	
6/18/2026	Darden PV/BESS	Jeffrey Holland	Bancroft CS	ENV/SWPPP; Bio; CR; PAL
6/22/2026	Darden PV/BESS	Juan H. Martinez	Mortenson	ENV/SWPPP; Bio; CR; PAL
		Robert Parks	Mortenson	
		Rene Mireles	Mortenson	
		Luis Reyes	Mortenson	
		Domanic Gonzales	Mortenson	
		Eran Mcces	Mortenson	
		Samuel Jean	Mortenson	
		Robert Leon	Mortenson	
		Octavio Mara	Mortenson	
		Julio Paredes	Mortenson	
		Carl Conley Jr.	Mortenson	
		Erick Rosiles	Mortenson	
		Jose H Garcia Romero	Mortenson	
		Ernesto Ayala Dominguez	Mortenson	
		Francisco Gutierrez	Mortenson	
		Gabriel Sanchera	Mortenson	
		Gerardo Mejia Jr.	Mortenson	
		Javier Navaro	Mortenson	
		Decova Sneed	Mortenson	
		Pablo T. Siordia	Mortenson	
		Mark Hotler	Mortenson	
		Fidel Ivan Gandara	Mortenson	
		Anthony Morales	Mortenson	
		Nhajee Rayshon McCoy	Mortenson	
		Jimmy D. Lewis	Mortenson	
		Justin Darby	Mortenson	
		Everjoy Solimau	Mortenson	
		Eddie Marquis R. Malvo	Mortenson	
		Rebecca Murillo	Mortenson	
		Scott M. Hiebert	Union Hydroseed	

Date	Project Phase	Full Name	Company	Training Administered
6/24/2026	Darden PV/BESS	Adrian Almarez	Union Hydroseed	ENV/SWPPP; Bio; CR; PAL
		Raymond Mayberry	ISS	
		Justin Burbett	Mortenson 100	
		Chastity Junes	Mortenson 100	
		Rayshauna Tapia	Mortenson Local 100	
		Gary Jones	Mortenson Local 100	
		Edward Sanchez	Mortenson Local 100	
		Joseph Diaz	Mortenson	
		Jose Hernandez	Local 100	
		Joe Dalisay	Mortenson	
		Simon Aguilar	Mortenson	
		Erik Gonzalez	Mortenson	
		Edward Alvarado	Mortenson	
		Joseph Uriarte	Mortenson	
		Osbaldo Beltran	Mortenson	
		Damian Sandoval	Mortenson Local 100	
		Christian Castro	Mortenson	
		Anthony Garcia	Mortenson	
		Jesse Aleman	Mortenson	
		Carlos Olvera	Mortenson	
		John Aguilar	Mortenson	
		Carlos Ruiz	Rain for Rent	
		Julio Ramirez	Rain for Rent	
		Phillip Reyes	Rain for Rent	
		Christian Hinojosa	Rain for Rent	
		Sammy Cruz	294 Local	
		Nicacio	Morrinson	
		Tyler Pilman	Morrinson	
		Manuel Martinez	Mortenson	
		Caterina Ontiveros	Mortenson	
		Daniel Guizar	Mortenson	
		Davial A. Lopez	Mortenson	
		Demetrius Bailey	Mortenson	
		Alonzo Robinson	Local 100	
		Keenan McKinney	Mortenson	
		Brandi McKinney	Mortenson	
		Sebastian Ybarra	Mortenson	
		Arturo Aguilar	Mortenson	
		Miguel Reynosa	Mortenson	

Date	Project Phase	Full Name	Company	Training Administered
		Juan Rios	Mortenson	
		Katie Arredando	Mortenson	
		Bryson Crawford	Man	
		Adolfo Lopez Sandoval	Man	
		Jose Ochoa	Man	
		Alfonso Rena	Mortenson	
		Mario Riojas	Mortenson	
		Romero Dominguez	Mortenson	
		Carlos Arias	Mortenson	
		Joseph Santellano	Mortenson	
		Miguel Ulloa	Man	
		Jorge Ramos	Mortenson	
		Azis Salcido	Mortenson	
		Brian Gomez	Mortenson	
		Andrew Sullivan	Profoam	
6/29/2026	Darden PV/BESS	Eduardo Corona	Summit West	ENV/SWPPP; Bio; CR; PAL
		Erwin Sandbu	Summit West	
		Noah Herrera	Wilson	
		Lues Jumar	Wilson	
		Chase Farris	Wilson	
		Joel Figueroa	Wilson	
		Jose Rocha	Wilson	
		Ayden Rocha	Wilson	
		Cameron Demaranuille	Optics Bio	
		Ellery Charleton	Artemis Enviro.	
		Rory Gallagher	Wilson	
		Cody Hurt	Bancroft	
		Elijah Montoya	Wilson	
		Andrew Holbrook	The Quality Firm	
		Angel Fuentes	OccumedX	

Appendix B

June 2026 - Daily Monitoring Summary Table

Daily Monitoring Records Summary for the Darden Clean Energy Project – June 2026

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
1	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Moving materials, drilling, bulldozing, excavating, moving materials, and installing rebar BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end-of-day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None observed	None to report
	PVB/Gen-tie: Amy Plesetz (SWHA/BUOW DB) Amy Trexler (BUOW DB) Caleb Yakel (SWHA/BUOW DB) Emily Smith (BM) Erwin Sandhu (BM) Gerardo Morales (BM) Jack Quinzon (BM) Jorge Rodriguez (BM) Kevin Gugerty (BUOW DB) Michael Schwanhausser (GDB) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Julier (GDB) Rachael Iverson (BM) Rachel Clark (SWHA/BUOW DB) Reggie Borntrager (BM) Reilly Miller (BM) Rob Weber (BM) Ruby Sainz (BM) Samantha Love (GDB) Shannon Morris (BUOW DB) Susie Garcia (BUOW DB)	PVB/Gen-tie: Construction activities: BESS PAD install, excavation and electrical work at Laydown Yard/Substation, installing torque tubes onto array piles (using telehandlers and manual labor), MV PLOW work (including trenching, excavating, and wire placement inside trenches), pile driving, and received deliveries of solar equipment (i.e., wooden crates, metal beams, piles) offloading and staging these materials from the semi-trucks using telehandlers, preliminary trenching, excavating, and delivery of wire spools to the work area, geo-grid install in area 11, laydown yard and road construction in area 14 and basin berm construction in area 16, drone surveys, road grading, berm installation, dust mitigation BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; assisted drone pilot, end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Timothy Gaffney (BUOW DB) Andrew Vasquez (PRM) Cristian Martinez (CRM) Sierra Bennaton (CRM) Viviana Navarro (CRM) Darren Putty (CRM) Jake Farhar (PRM)			
2	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Digging, moving materials, bulldozing, grading, dust control BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end-of-day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Abra Schlotz (BM) Amy Plesetz (SWHA/BUOW DB) Amy Trexler (BUOW DB) Caleb Yakel (SWHA/BUOW DB) Emily Smith (BM) Erwin Sandhu (BM) Jack Quinzon (BM) Jorge Rodriguez (BM) Kevin Gugerty (BUOW DB) Michael Schwanhausser (GDB) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Fager (SWHA/BUOW DB) Nick Julier (GDB) Rachael Iverson (BM) Rachel Clark (SWHA/BUOW DB)	PVB/Gen-tie: Construction activities: Drilling to place cages in drill holes, excavating and trenching to place conduit and backfilling, hauling dirt and equipment, road grading, and berm work, dust suppression, BESS PAD install, excavation and electrical, installing torque tubes onto array piles (using telehandlers and manual labor), conducting MV Plow work (including trenching, excavating, and wire placement inside trenches), pile driving, and deliveries of solar equipment (i.e., wooden crates, metal beams, piles) and offloading and staging materials using telehandlers. BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep; made observations at Den 222 in Area 16 (Darden II) during construction activities. CRM activities: monitored daily construction activities; Tachi Yokut Tribal member monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Reggie Borntrager (BM) Reilly Miller (BM) Rob Weber (BM) Samantha Love (GDB) Shannon Morris (BUOW DB) Timothy Gaffney (BUOW DB) Cristian Martinez (CRM) Sierra Bennaton (CRM) Viviana Navarro (CRM) Darren Putty (CRM) Iveen Barrios (NAM) Andrew Vasquez (PRM) Jake Farhar (PRM)			
3	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Moving materials, drilling, bulldozing, excavating, pouring cement, and installing rebar, drilling through 8ft pad into original soil level, placement of steel pylons, cement pouring, soil movement, ground flattening, dust abatement with water BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end-of-day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	N/A	None to report
	PVB/Gen-tie: Nick Julier (GDB) Caleb Yakel (SWHA/BUOW DB) Abra Schlottz (BM) Allie Sennett (SWHA/BUOW DB) Amy Trexler (BUOW DB) Brittany Gummo (SWHA/BUOW DB) David Wappler (SWHA/BUOW DB)	PVB/Gen-tie: Construction activities: Diatomaceous earth (DE) application in Area 8, drilling/foundation work, trenching/backfilling, staging along adjacent gen tie, and rebar work, hauling dirt, road grading, haul trucks, and berm work, staging of equipment at structure 62 area, trenching and conduit installation, excavations for pads, wood box installations, excavation of battery path, MV plow and directional boring, staging material along northern road of Area 3, BESS Pad 1/2/3/4 excavation of trenches, installation of conduit and wiring, backfilling trenches, pile driving, ESA staking adjustments, road building, clearing salt bush by dozer, OLT, Solar	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern harrier, SSC	ESA Buffer encroachment reported to CEC on 06/04/2026, see Section 4.6

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Emma Kirschten (BM)	Array Grading, Drilling activities at tower 80 within the gen-tie ROW, Subgrade of Road 508		
	Gerardo Morales (BM)			
	Jack Quinzon (BM)			
	Jessica Lotts (BM)	BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep; made observations at Dens 220, 221, and 222 in Area 16 (Darden II) during construction activities.		
	Jorge Rodriguez (BM)			
	Katherine Phillips (GDB)			
	Kevin Gugerty (BUOW DB)	CRM activities: monitored daily construction activities; Tachi Yokut Tribal member monitored daily construction activities		
	Krista Suderman (BM)			
	Michael Schwanhausser (GDB)			
	Moses Lopez (BM)	PRM activities: monitored daily construction activities		
	Nathalie Treminio (GDB)			
	Nick Fager (SWHA/BUOW DB)			
	Onkar Singh (BUOW DB)			
	Rachael Iverson (BM)			
	Rachel Clark (SWHA/BUOW DB)			
	Reggie Borntrager (BM)			
	Rob Weber (BM)			
	Ruby Sainz (BM)			
	Sam Wasserman (BM)			
	Samantha Love (GDB)			
	Sarah Jacobsen (GDB)			
	Sarah Vasquez (BUOW DB)			
	Shannon Morris (BUOW DB)			
	Susie Garcia (BUOW DB)			
	Timothy Gaffney (BUOW DB)			
	Cristian Martinez (CRM)			
	Sierra Bennaton (CRM)			
	Viviana Navarro (CRM)			
	Darren Putty (CRM)			
	Iveen Barrios (NAM)			
	Andrew Vasquez (PRM)			
	Jake Farhar (PRM)			

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
4	BAAH: Jackie Dougherty (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Pouring concrete, drilling, deliveries, installing rock, and digging BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	N/A	None to report
	PVB/Gen-tie: Amy Trexler (BUOW DB) Blaine Grant (BUOW DB) Brittany Gummo (SWHA/BUOW DB) Daniel Hall (BUOW DB) David Wappler (SWHA/BUOW DB) Erwin Sandhu (BM) Gerardo Morales (BM) Jack Quinzon (BM) Jackie Dougherty (BM) Jessica Lotts (BM) Jorge Rodriguez (BM) Krista Suderman (BM) Michael Schwanhausser (GDB) Nick Fager (SWHA/BUOW DB) Oliver Scott (BM) Rachael Iverson (BM) Reilly Miller (BM) Sam Wasserman (BM) Sarah Jacobsen (GDB) Sarah Vasquez (BUOW DB) Susan Carlton (BUOW DB) Cristian Martinez (CRM) Sierra Bennaton (CRM)	PVB/Gen-tie: Construction activities: Road 508 subgrade, MV Plow, trenching, scraper and pile install, Trenching/excavation, shoring install, cable installation, other earthwork, backfill, gen-tie foundation drilling, and material staging/transport, Excavation of trenches. Installation of conduit and wiring. Backfilling trenches, pile driving, aggregate base deliveries for new access roads, compacting and subgrading aggregate, installation of basins, material offload, module distribution, pile distribution, support distribution, pipe cap install, wire install, conduit backfill, material and equipment staging and equipment maintenance, including forklifts, skid steers, semi-trucks, utility trucks, excavators, pile drivers, backhoe, and multiple water trucks. Directional boring, backfill, compaction of battery path and transformer, continued conduit installation and placement of cat banks, ESA staking. BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities; Tachi Yokut Tribal member monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Loggerhead shrike, SSC; Northern harrier, SSC	ESA Buffer encroachment reported to CEC on 06/04/2026, see Section 4.6

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Viviana Navarro (CRM) Darren Putty (CRM) Iveen Barrios (NAM) Nichole Escalon (NAM) Andrew Vasquez (PRM) Breahna Fogg (PRM)			
5	BAAH: Jackie Dougherty (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Installation of pylon cement bases, installation of bottom of pylons, dirt movement to fill in pad, relocation of pylons from staging area, dust abatement with water trucks BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Abra Schlotz (BM) Allie Sennett (SWHA/BUOW DB) Amy Trexler (BUOW DB) Blaine Grant (BUOW DB) Brittany Gummo (SWHA/BUOW DB) Daniel Hall (BUOW DB) David Wappler (SWHA/BUOW DB) Erwin Sandhu (BM) Gerardo Morales (BM) Jack Quinzon (BM) Jackie Dougherty (BM) Jessica Lotts (BM) Jorge Rodriguez (BM) Landy Figueroa (GDB)	PVB/Gen-tie: Construction activities: Installation of conduit and wiring, back filling trenches, excavation of trenches, pile driving, perimeter berm and basin 1 work, MV plow, staging materials, trenching, installation of conduit and wiring, back filling trenches, excavation of trenches, pile driving, delivering aggregate, drilling at structure 79, drilling at structure 78, excavation of 12kV trench, rebar work, directional boring, civil road work, trenching/excavation, shoring install, cable installation, earthwork, backfill, gen-tie foundation drilling and concrete pouring, and material staging/transport, plow crew laying conduit, material staging in the north laydown yard, boring, solar array installation in area 3, drone surveys BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST	The contractor was notified of uncontained trash on the project site. Trash was cleaned up, placed in a sealed trash container, and removed from the site at the end of the day.

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Michael Schwanhausser (GDB) Oliver Scott (BM) Onkar Singh (BUOW DB) Rachael Iverson (BM) Sam Wasserman (BM) Sarah Jacobsen (GDB) Sarah Vasquez (BUOW DB) Susan Carlton (BUOW DB) Cristian Martinez (CRM) Sierra Bennaton (CRM) Viviana Navarro (CRM) Darren Putty (CRM) Andrew Vasquez (PRM) Jake Farhar (PRM)			
6	BAAH: Gerardo Morales (BM)	BAAH: Construction activities: Cement pouring and conduit installation BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep	None	None to report
	PVB/Gen-tie: Jessica Lotts (BM) Erwin Sandhu (BM) Oliver Scott (BM) Reilly Miller (BM) Jessica Lotts (BM) Lily Arteaga (CRM) Andrew Vasquez (PRM) Jake Farhar (PRM)	PVB/Gen-tie: Construction activities: Drilling, cement pouring, conduit installation, dust suppressant spray, ingress and egress of cement trucks, deliveries, and crew traffic BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Swainson's hawk, ST; Northern harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
8	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	Construction activities: Bulldozing, moving materials, digging, placing rebar, grading, and dust control BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Alex Aylard (GDB) Amy Plesetz (BUOW DB) Asha Pluton (BM) Bryant Reynolds (BUOW DB/GDB) Caleb Yakel (SWHA/BUOW DB) Cameron Reid (GDB) Gerardo Morales (BM) Joey Medina (BUOW DB) Katherine Phillips (GDB) Kevin Gugerty (BUOW DB) Landy Figueroa (GDB) Lauren Salazar (BM) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Julier (GDB) Rachel Clark (SWHA/BUOW DB) Rainey Davis (BUOW DB) Rebekah Shannon (BM) Rob Weber (BM) Samantha Love (GDB) Shannon Morris (BUOW DB/GDB) Timothy Gaffney (BUOW DB) Tina Tran (BM) Nick Fager (SWHA/BUOW DB) Cristian Martinez (CRM)	PVB/Gen-tie: Construction activities: Equipment staging, grading, compacting, staking removal and adding stakes to ESAs, MV spool testing, pile driving in Darden 1, trenching/Excavation with heavy equipment in Darden 2, road grading, drilling, conduit installation, concrete casing removal, excavations, rolling, preparing gravel pad for water truck station and traffic on adjacent roads BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep; made observations at Dens 220, 221, and 222 in Area 16 (Darden II) during construction activities. CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Swainson's hawk, ST; Northern harrier, SSC; Loggerhead shrike, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Chris Chambers (CRM) Leon Bach (CRM) Viviana Navarro (CRM) Andrew Vasquez (PRM) Jake Farhar (PRM)			
9	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Digging, moving materials, bulldozing, pouring cement, grading, dust control BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	N/A	None to report
	PVB/Gen-tie: Alex Aylard (GDB) Amy Plesetz (BUOW DB) Asha Pluton (BM) Brittany Gummo (SWHA/BUOW DB) Bryant Reynolds (BUOW DB/GDB) Caleb Yakel (SWHA/BUOW DB) Cameron Reid (GDB) Jack Quinzon (BM) Kevin Gugerty (BUOW DB) Krista Suderman (BM) Landy Figueroa (GDB) Lauren Salazar (BM)	PVB/Gen-tie: Construction activities: Staking removal for ESA, pile install, conduit installation, equipment delivery, backfill, FNR racks, mowing, discing and frequent water trucks passing over areas along eastern border and southern portion of Area 16, dozers creating berm, scrapers moving dirt, ground excavation for utilities installment, approximately 250ft from nest location, subgrade/strip and buildout basins, working on roads 206-208, 12kv trenching and backfilling, rebar yard, and gen tie drilling/cement pouring, grading and compacting, boring crew conducting work within SWHA buffer overlapping Areas 11 and 14, MV Plow work (including trenching, excavating, and wire placement inside trenches) BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species; Swainson's hawk, ST	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Lukas Capatosto (BM) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Fager (SWHA/BUOW DB) Rainey Davis (BUOW DB) Rob Weber (BM) Samantha Love (GDB) Sarah Vasquez (BUOW DB) Shannon Morris (BUOW DB/GDB) Timothy Gaffney (BUOW DB) Tina Tran (BM) Cristian Martinez (CRM) Chris Chambers (CRM) Leon Bach (CRM) Viviana Navarro (CRM) Andrew Vasquez (PRM) Jake Farhar (PRM)			
10	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Digging, moving materials, bulldozing, pouring cement, grading, drilling, dust control BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	PVB/Gen-tie: Joey Medina (BUOW DB) Allie Sennett (SWHA/BUOW DB) Asha Pluton (BM) Brittany Gummo (SWHA/BUOW DB) Bryant Reynolds (BUOW DB/GDB) Caleb Yakel (SWHA/BUOW DB) Cameron Reid (GDB) David Wappler (SWHA/BUOW DB) Gerardo Morales (BM) Jack Quinzon (BM) Jessica Lotts (BM) Kevin Gugerty (BUOW DB) Krista Suderman (BM) Landy Figueroa (GDB) Lauren Salazar (BM) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Fager (SWHA/BUOW DB) Nick Julier (GDB) Onkar Singh (BUOW DB/GDB) Rachel Clark (SWHA/BUOW DB) Rainey Davis (BUOW DB) Reggie Borntrager (BM) Rob Weber (BM) Sam Wasserman (BM) Samantha Love (GDB) Sarah Jacobsen (GDB) Sarah Vasquez (BUOW DB) Shannon Morris (BUOW, DB/GDB) Tina Tran (BM)	PVB/Gen-tie: Construction activities: Basin 1 perimeter berm on North side of Area 2, module/ array install in Area 3, boring crew conducting work within SWHA buffer overlapping Areas 11 and 14, trenching, backfill, trenching/backfilling around substation area, grading and compacting road, staging equipment, watering down project roads, installing horizontal pipes on I beams, MV plow, surveying, continued backfill and compaction of transformer, continued conduit installation and backfill, continued pier drilling and concrete pours of cat pads, excavation of trenches, installation of conduit and wiring, backfilling trenches, subgrade/strip and buildout basins, work on road 208, jack and bore BM activities: conducted pre-activity sweep of project site; assisted drone flight; monitored daily construction activities; monitoring of burrowing owl dens; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Swainson's hawk, ST; Loggerhead shrike, SSC; Northern harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Whitney Vickers (BM) Cristian Martinez (CRM) Chris Chambers (CRM) Leon Bach (CRM) Viviana Navarro (CRM) Jake Farhar (PRM) Katerina Alexis-Konstantinidis (PRM)			
11	BAAH: Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Excavating trenches, pouring concrete, installing breaker boxes, staging equipment BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Gerardo Morales (BM) Katherine Phillips (GDB) Blaine Grant (BUOW DB) Whitney Vickers (BM) Jack Quinzon (BM) Lukas Capatosto (BM) Erwin Sandhu (BM) Lauren Salazar (BM) Cameron Reid (GDB) Sarah Vasquez (BUOW DB) David Wappler (SWHA/BUOW DB) Sarah Jacobsen (GDB) Landy Figueroa (GDB)	PVB/Gen-tie: Construction activities: Grading, compacting, ESA staking, MV plow, directional boring, civil road work, installation of no entrance and slow down signs for oncoming vehicles, pulling of stakes in numerous nesting sites by 1000ft and installing buffers, placement of ESA stakes for delineation, trenching and excavation, shoring install, cable installation, earthwork, backfill, gen-tie foundation drilling, cement pouring, material staging, transport, continued backfilling of 12kV trenches and conduit install, module/pile install, staging materials, deliveries, drone work, Survey staking, ESA staking, directional boring, grading and compacting at well #3, undergrounding cable with plough and trencher machine BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities; Tachi Yokut Tribal member monitored daily construction activities PRM activities: monitored daily construction activities	Swainson's hawk, ST; Burrowing owl, candidate species; Northern Harrier SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Craig O'Neill (BUOW DB) Tina Tran (BM) Sam Wasserman (BM) Reggie Borntrager (BM) Onkar Singh (BUOW DB/GDB) Allie Sennett (SWHA/BUOW DB) Jessica Lotts (BM) Cristian Martinez (CRM) Chris Chambers (CRM) Leon Bach (CRM) Viviana Navarro (CRM) Iveen Barrios (NAM) Jake Farhar (PRM) Katerina Alexis-Konstantinidis (PRM)			
12	BAAH: Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Backfilling trenches, drilling pylon foundation holes, placing rocks on downslope of the BAAH, installing pylons, fill material deliveries, staging equipment BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Alex Aylard (GDB) Allie Sennett (SWHA/BUOW DB) Blaine Grant (BUOW DB) Cameron Reid (GDB) Craig O'Neill (BUOW DB) David Wappler (SWHA/BUOW DB) Erwin Sandhu (BM) Gerardo Morales (BM)	PVB/Gen-tie: Construction activities: Road 302 topsoil stripping, tracker and pile installation, grading, watering, removing and compacting dirt in basins, boring work on the east side of Area 11, installation of MV bullhorns, installation of MV racks, backfill of trenches, general site maintenance, MV plow, directional boring, civil road work, transformer excavation, cat path excavation, conduit installation and backfill, setting forms for battery pads and piers for cement pours and continued drilling holes for pier structures, trenching, excavation, shoring install, cable installation, earthwork, backfilling, and material staging/transport as well as grading and compacting at well #3	Swainson's hawk, ST; Burrowing owl, candidate species; Northern Harrier SSC	ESA Buffer encroachment reported to CEC on 06/12/2026, see Section 4.6.

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Graham Biddy (SWHA/BUOW DB) Jack Quinzon (BM) Jessica Lotts (BM) Katherine Phillips (GDB) Lauren Salazar (BM) Nicole Carpenter (BM) Onkar Singh (BUOW DB/GDB) Rachel Clark (SWHA/BUOW DB) Reggie Borntrager (BM) Sam Wasserman (BM) Sarah Jacobsen (GDB) Sarah Vasquez (BUOW DB) Tina Tran (BM) Cristian Martinez (CRM) Chris Chambers (CRM) Leon Bach (CRM) Viviana Navarro (CRM) Iveen Barrios (NAM) Jake Farhar (PRM) Katerina Alexis-Konstantinidis (PRM)	BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities; Tachi Yokut Tribal member monitored daily construction activities PRM activities: monitored daily construction activities		
13	BAAH: Gerardo Morales (BM)	BAAH: Construction activities: Cement pouring, backfill, foundation work BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep	Swainson's hawk, ST	None to report
	PVB/Gen-tie: Alana Garza (SWHA/BUOW DB) Bryant Reynolds (BUOW DB/GDB) David Wappler (SWHA/BUOW DB) Gerardo Morales (BM)	PVB/Gen-tie: Construction activities: Continued excavation and backfilling for conduit installation, continued compacting cat path, continued setting of forms BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; ESA maintenance; assisted drone pilot; end of day clearance sweep; monitoring of burrowing owl dens	Swainson's hawk, ST; Northern Harrier SSC; Loggerhead shrike, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Jessica Lotts (BM) Lauren Salazar (BM) Chris Chambers (CRM) Jake Farhar (PRM)	CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities		
15	BAAH: Destiny Beltran (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Bulldozing, moving materials, digging, pouring cement, grading, and dust control BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Amy Plesetz (BUOW DB) Andrew Alba (GDB) Blake Perry (BM) Caleb Yakel (SWHA/BUOW DB) Danielle Simmons (BM) Eric Cercedes (BM) Gerardo Morales (BM) Jace Pearson (BM) Jack Quinzon (BM) Jorge Rodriguez (BM) Lauren Salazar (BM) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Fager (SWHA/BUOW DB) Nick Julier (GDB) Nikki Caravelli (BM) Oliver Scott (BM) Rachael Iverson (BM) Rachel Clark (SWHA/BUOW DB)	PVB/Gen-tie: Construction activities: MV plowing and other excavations, hydroseeding Plowing/trenching, excavation for inverters, deliveries, staging materials Subgrade/strip and buildout basins 2.1 and 2.2 Pouring concrete into drilled holes, drilling fresh holes and inspecting contents, laying rebar and moving materials on north end of area, framing for concrete pads, laying piping for conduits, Subgrade road rolling/tamping down excavated piping, handwork on cement pours, dust suppression, delivering aggregate to lay down as base for construction of new access road Rebar work, excavation backfilling, pile installation, trenching, electrical MV, gutter buildup and prefab, FNE racks, bullhorns conducted MV Plow work (excavating, installing wire in trenches), pile driving, torque tube installation, offloading and staging of delivered materials (piles, wooden crates), module installation, and general site clean-up (i.e., disposing of wooden and metal debris into designated dumpster bins), rebar work at laydown yard in substation, fabrication of rebar cages BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species; Swainson's hawk, ST; Northern Harrier SSC; Loggerhead shrike, SSC	ESA Buffer encroachment reported to CEC on 06/16/2026, see Section 4.6

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Reilly Miller (BM) Rob Weber (BM) Ruby Sainz (BM) Samantha Love (GDB) Shannon Morris (BUOW DB/GDB) Susie Garcia (BUOW DB) Timothy Gaffney (BUOW DB) Tina Tran (BM) Katherine Phillips (GDB) Sean Herman (BM) Cristian Martinez (CRM) Chris Chambers (CRM) Kayci Owen (CRM) Viviana Navarro (CRM) Jake Farhar (PRM) Katerina Alexis-Konstantinidis (PRM)			
16	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Backfill, trenching BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	N/A	None to report
	PVB/Gen-tie: Adrienne Calistri-Yeh (GDB) Amy Plesetz (BUOW DB) Brandon Dunnahoo (BM) Caleb Yakel (SWHA/BUOW DB) Camille Troncone (GDB) Connor Adams (BM)	PVB/Gen-tie: Construction activities: Aggregate base and dirt deliveries for the creation of mew access road and laydown yard, subgrading and rolling aggregate for compaction, plowing, hay install, staging material, trenching, backfill, mv pit, pile install, mowing in Area 13, digging/backfilling trenches, placing and installing metal posts, installing cables, dust suppression, hydroseeding, solar panel installation, pier drilling, framing concrete pads, conduit install, grading with skid steer, excavation with heavy equipment, relocating available materials next to ESAs, hand work placing and cutting	Burrowing owl, candidate species; Swainson's hawk, ST; Northern Harrier SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Danielle Simmons (BM)	rebar for cement pour, tube installation, installed torque tubes onto array		
	Eric Cercedes (BM)	piles (using telehandlers and manual labor)		
	Jace Pearson (BM)	BM activities: conducted pre-activity sweep of project site; monitored		
	Jorge Rodriguez (BM)	daily construction activities; end of day clearance sweep		
	Katherine Phillips (GDB)	CRM activities: monitored daily construction activities; Tachi Yokut Tribal		
	Lauren Salazar (BM)	member monitored daily construction activities		
	Moses Lopez (BM)	PRM activities: monitored daily construction activities		
	Nathalie Treminio (GDB)			
	Nick Fager (SWHA/BUOW DB)			
	Nikki Caravelli (BM)			
	Oliver Scott (BM)			
	Rachael Iverson (BM)			
	Rachel Clark (SWHA/BUOW DB)			
	Reilly Miller (BM)			
	Rob Weber (BM)			
	Ruby Sainz (BM)			
	Samantha Love (GDB)			
	Sarah Vasquez (BUOW DB)			
	Sean Herman (BM)			
	Shannon Morris (BUOW DB/GDB)			
	Summer Mersereau (BM)			
	Susie Garcia (BUOW DB)			
	Timothy Gaffney (BUOW DB)			
	Tina Tran (BM)			
	William Ryan (GDB)			
	Cristian Martinez (CRM)			
	Chris Chambers (CRM)			
	Kayci Owen (CRM)			
	Viviana Navarro (CRM)			
	Iveen Barrios (NAM)			
	Jake Farhar (PRM)			

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Katerina Alexis-Konstantinidis (PRM)			
17	BAAH: Nick Julier (GDB) Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Excavating trenches, drilling pylon foundation holes, grading and moving fill material, staging and moving equipment, dust control BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep, ESA T-post staking and removal, CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Adrienne Calistri-Yeh (GDB) Alicia Manzo (BM) Allie Sennett (SWHA/BUOW DB) Andrew Alba (GDB) Blake Perry (BM) Bobby Luangrath (BM) Brandon Dunnahoo (BM) Caleb Yakel (SWHA/BUOW DB) Emma Kirschten (BM) Jackie Dougherty (BM) Jorge Rodriguez (BM) Katherine Phillips (GDB) Kyle Rader (GDB) Lauren Salazar (BM) Moses Lopez (BM) Nathalie Treminio (GDB)	PVB/Gen-tie: Construction activities: Material delivery and distribution, pile driving, pipe installation for panels, MV plow, excavation, hydroseeding, scraping along road, module installation, deliveries and staging of materials, battery storage backfill trenching, pile installation, trenching, pipe installation for solar panels, placing and installing metal posts, installing cables, pouring cement, installation of MV racks, installation of homeruns, installation of wiring, backfilling trenches, installation of pile caps, vegetation trimming and mowing, drilling and placing metal cages, electrical subgrade, grading, pier and transformer preparation, dust mitigation, installation of torque tubes onto array piles (using telehandlers and manual labor) BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; ESA monitoring; assisted drone pilot; end of day clearance sweep CRM activities: monitored daily construction activities; Tachi Yokut Tribal member monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species; Swainson's hawk, ST; Northern harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Nick Fager (SWHA/BUOW DB)			
	Nick Julier (GDB)			
	Nikki Caravelli (BM)			
	Oliver Scott (BM)			
	Onkar Singh (BUOW DB)			
	Rachael Iverson (BM)			
	Reilly Miller (BM)			
	Rob Weber (BM)			
	Sam Wasserman (BM)			
	Sarah Jacobsen (GDB)			
	Sarah Vasquez (BUOW DB)			
	Sean Herman (BM)			
	Shannon Morris (BUOW, DB/GDB)			
	Summer Mersereau (BM)			
	Susie Garcia (BUOW DB)			
	Timothy Gaffney (BUOW DB)			
	Tina Tran (BM)			
	William Ryan (GDB)			
	Cristian Martinez (CRM)			
	Chris Chambers (CRM)			
	Kayci Owen (CRM)			
	Viviana Navarro (CRM)			
	Iveen Barrios (NAM)			
	Jake Farhar (PRM)			
	Katerina Alexis-Konstantinidis (PRM)			

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
18	BAAH: Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Drilling pylon foundation holes, concrete pouring, moving and staging equipment, materials delivery, form work, rip rap installation, dust suppression. BM activities: conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Gerardo Morales (BM) Madison Wallwork (BM) Camille Troncone (GDB) Daniel Hall (BUOW DB) Ruby Sainz (BM) Rainey Davis (BUOW DB) Jack Quinzon (BM) Sean Herman (BM) Jace Pearson (BM) Cameron Reid (GDB) Joshua Oyeboade (BM) Rebekah Shannon (BM) Luke Paczos (BM) Lauren Salazar (BM) Sarah Vasquez (BUOW DB) Summer Mersereau (BM) Rachael Iverson (BM) Onkar Singh (BUOW DB) Sarah Jacobsen (GDB) Andy Maldonado (BM) Alicia Manzo (BM) Brandon Dunnahoo (BM) Allie Sennett (SWHA/BUOW DB)	PVB/Gen-tie: Construction activities: Working basin and berm with skid steer, water truck and water pig, basin and perimeter berm grading and NW artery road maintenance, making transformer pads, filling holes with cement, trenching, drilling, laying down rebar, dust mitigation, pile and array install, deliveries, staging materials, scraping, bulldozing, grading with dozer, watering down soil before grading to reduce dust, installation of pile caps, pile driving, backfilling trenches, equipment deliveries, excavation of trenches, digging, laying electrical, driving posts, grading roads, metal posts, drilling pylon foundation holes, form work, rip rap installation, fill transport and stockpile management, soil compaction, electrical conduit installation, hydroseeding, removing spoil piles at Points 80, 79, 78, basin construction, digging holes, preparing molds, and laying rebar for concrete pour, ESA maintenance BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; ESA monitoring; den monitoring; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Swainson's hawk, ST; Loggerhead shrike, SSC; Northern harrier, SSC	ESA Buffer encroachment reported to CEC on 06/19/2026, see Section 4.6

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Sam Wasserman (BM) Michael Hahn (BM) Samantha Love (GDB) Tina Tran (BM) Moses Lopez (BM) Jackie Dougherty (BM) Jorge Rodriguez (BM) Emma Kirschten (BM) Oliver Scott (BM) Cristian Martinez (CRM) Chris Chambers (CRM) Kayci Owen (CRM) Viviana Navarro (CRM) Jake Farhar (PRM) Katerina Alexis-Konstantinidis (PRM)			
19	BAAH: Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	Construction activities: Cement pouring, installing circuit breakers on top of pylons, excavating trenches, backfilling trenches, staging equipment, dust suppression. BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; ESA monitoring; den monitoring; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	Alicia Manzo (BM) Allie Sennett (SWHA/BUOW DB) Andrew Alba (GDB) Andy Maldonado (BM) Blake Perry (BM) Daniel Hall (BUOW DB) Danielle Simmons (BM) Emma Kirschten (BM)	PVB/Gen-tie: Construction activities: Pile boring, subgrade excavation, MV plowing, tracker, module and array install, backfilling excavation trenches, trenching and grading, scraping, bulldozing, watering, steel piling, ingress/egress, and drone work, BESS Darden ¾ trench excavation, pile installation, pile cap installation, perimeter berm and basin grading, pole installation, drilling of gen tie structures, staging of equipment and machinery, setting of footings, dust abatement, general cleanup of area, basin construction, digging holes, preparing molds, and laying rebar for concrete pour	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern Harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Eric Cercedes (BM)	BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; ESA monitoring; den monitoring; end of day clearance sweep		
	Gerardo Morales (BM)			
	Jace Pearson (BM)			
	Jack Quinzon (BM)	CRM activities: monitored daily construction activities		
	Jackie Dougherty (BM)	PRM activities: monitored daily construction activities		
	Jessica Lotts (BM)			
	Jorge Rodriguez (BM)			
	Joshua Oyeboade (BM)			
	Lauren Salazar (BM)			
	Michael Hahn (BM)			
	Moses Lopez (BM)			
	Nicole Carpenter (BM)			
	Onkar Singh (BUOW DB)			
	Rachael Iverson (BM)			
	Rainey Davis (BUOW DB)			
	Rebekah Shannon (BM)			
	Ruby Sainz (BM)			
	Sam Wasserman (BM)			
	Sarah Vasquez (BUOW DB)			
	Tina Tran (BM)			
	William Ryan (GDB)			
	Cristian Martinez (CRM)			
	Chris Chambers (CRM)			
	Kayci Owen (CRM)			
	Viviana Navarro (CRM)			
	Jake Farhar (PRM)			
	Katerina Alexis-Konstantinidis (PRM)			

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
20	BAAH: Jessica Lotts (BM)	BAAH: Construction activities: Continued backfilling and compaction of concrete risers, continued installing panel risers, continued glass and iron work and general site clean up BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored RTHA nest ESA; end of day clearance sweep CRM activities: monitored daily construction activities	None	None to report
	Danielle Simmons (BM) Jeffery Holland (BM) Reilly Miller (BM) Oliver Scott (BM) Jackie Dougherty (BM) Kayci Owen (CRM) Jake Farhar (PRM) Katerina Alexis-Konstantinidis (PRM)	PVB/Gen-tie: Construction activities: Pouring cement, excavation, BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; ESA monitoring; assisted drone pilot; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Swainson's hawk, ST; Northern harrier, SSC	ESA Buffer encroachment reported to CEC on 06/22/2026, see Section 4.6.
22	BAAH: Whitney Vickers (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Bulldozing, moving materials, installing rip rap slope, drilling, delivering materials, installing poles, and dust control BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored RTHA nest ESA; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Jessica Lotts (BM) Kym Espinosa-Blount (BUOW DB) Sam Wasserman (BM) Blaine Grant (BUOW DB) Brandon Dunnahoo (BM) Brittany Gummo (SWHA/BUOW DB) Bryant Reynolds (BUOW DB/GDB) Cynthia Martinson (GDB) Gerardo Morales (BM) Jack Quinzon (BM) Landy Figueroa (GDB) Lauren Salazar (BM) Onkar Singh (BUOW DB) Rachael Iverson (BM) Rainey Davis (BUOW DB) Rowdy Freeland (GDB) Sarah Vasquez (BUOW DB) Tina Tran (BM) Whitney Vickers (BM) Kayci Owen (CRM) Darren Putty (CRM) Chris Chambers (CRM) Jake Farhar (PRM)	PVB/Gen-tie: Construction activities: Pile driving within Colusa ditch BUOW 1600' buffer, disking/sub grading roads 301 and 302, inverter sub grading, Hay bale installation at Burrowing Owl ESA, excavation activities, Aggregate staging by trucks, grading by blade equipment, dust control with water trucks. Roller compacting graded roadway, Backfill and pile install, pile capping, homeruns, trenching, plowing, Drilling, compaction, backfilling, rebar installation at transformer pad, breaker pads, form installation, Spreading and rolling dirt, Removing T posts from basin 2.3, installation of torque tubes onto array piles (using telehandlers and manual labor), conducted MV Plow work (including trenching, excavating, and wire placement inside trenches), conducted pile driving, received deliveries of solar equipment (i.e., wooden crates, metal beams, piles), installed solar arrays, conducted electrical work, and offloaded and staged these materials from the semi-trucks using telehandlers. Splicing cables, excavating trenches for inverters, mowing in Area 16, concrete work at structure 69, hydroseeding, inverter subgrading BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; ESA monitoring, nest monitoring; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern harrier, SSC; Loggerhead shrike, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
23	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Bulldozing, moving materials, installing rip rap slope, grading, drilling, delivering materials, installing poles, and dust control BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored RTHA nest ESA; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	N/A	None to report
	PVB/Gen-tie: Abra Schlotz (BM) Alicia Manzo (BM) Amy Plesetz (BUOW DB) Bobby Luangrath (BM) Caleb Yakel (SWHA/BUOW DB) Cameron Reid (GDB) Camille Troncone (GDB) Craig O'Neill (BUOW DB) Danielle Simmons (BM) Emma McAndrews (BM) Erwin Sandhu (BM) Gerardo Morales (BM) Jace Pearson (BM) Jack Quinzon (BM) Jeffrey Holland (BM) Joey Medina (BUOW DB) Joshua Oyeboade (BM) Katherine Phillips (GDB) Michael Hahn (BM) Moses Lopez (BM) Nathalie Tremainio (GDB) Nick Fager (SWHA/BUOW DB)	PVB/Gen-tie: Construction activities: Bridge building at Gen Tie Area 13 intersection, deliveries of soil, large area grading, water truck activity for dust abatement, new laydown yard construction in Area 5 northern section involving dump trucks, grader, roller, scrapers, and water truck, aggregate spreading, cable plowing, pile driving, trenching, grading, adding T-posts and rope around existing buffer, discing, subgrading road 302, inverter subgrading, installation of new transformer pads, hydroseeding, installation of torque tubes onto array piles (using telehandlers and manual labor), MV Plow work (including trenching, excavating, and wire placement inside trenches), pile driving, received deliveries of solar equipment (i.e., wooden crates, metal beams, piles), installation of solar modules and brackets within the solar arrays, electrical work, offloading and staging materials from trucks using telehandlers, installing hay bale barriers around Burrowing Owl burrows BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored ESAs; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern harrier, SSC; Loggerhead shrike, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Nick Fager (SWHA/BUOW DB) Nick Julier (GDB) Nikki Caravelli (BM) Oliver Scott (BM) Reggie Borntrager (BM) Reilly Miller (BM) Ruby Sainz (BM) Sarah Vasquez (BUOW DB) Shannon Morris (BUOW DB) Sierra Bennaton (BM) Stella Moore (BM) William Ryan (GDB) Kayci Owen (CRM) Darren Putty (CRM) Chris Chambers (CRM) Jake Farhar (PRM)			
24	BAAH: Nick Julier (GDB) Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Drilling, backfilling trenches, concrete pouring, pylon foundation preparations BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored RTHA nest ESA; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	N/A	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	PVB/Gen-tie: Abra Schlotz (BM) Alicia Manzo (BM) Brittany Gummo (SWHA/BUOW DB) Caleb Yakel (SWHA/BUOW DB) Cameron Reid (GDB) Camille Troncone (GDB) Danielle Simmons (BM) David Wappler (SWHA/BUOW DB) Emily Smith (BM) Emma McAndrews (BM) Eric Cerecedes (BM) Erwin Sandhu (BM) Gerardo Morales (BM) Jace Pearson (BM) Jack Quinzon (BM) Jackie Dougherty (BM) Jessica Lotts (BM) Joey Medina (BUOW DB) Katherine Phillips (GDB) Michael Hahn (BM) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Fager (SWHA/BUOW DB) Nikki Caravelli (BM) Oliver Scott (BM) Rainey Davis (BUOW DB) Reggie Borntrager (BM) Ruby Sainz (BM) Sam Wasserman (BM) Samantha Love (GDB)	PVB/Gen-tie: Construction activities: Work crews installed torque tubes onto array piles (using telehandlers and manual labor), conducted MV Plow work (including trenching, excavating, and wire placement inside trenches), conducted pile driving, received deliveries of solar equipment (i.e., wooden crates, metal beams, piles), installed solar modules and brackets within the solar arrays, conducted electrical work, and offloaded and staged these materials from the semi-trucks using telehandlers, as well as perimeter berm grading, plowing, excavating, pile installation and pile cap installation, discing/subgrading road 302 within Colusa Ditch 1600' buffer, inverter subgrading, vegetation management, hydroseeding, deliveries, staging materials, array/module installation, tracker assembly, sub grade electrical work (backfilling), solar panel installation, material delivery and distribution, compaction of EEE's, continued conduit installation and backfill, continued setting forms and piers for concrete pours, splicing cables BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored ESAs; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern harrier, SSC; Loggerhead shrike, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Sarah Jacobsen (GDB) Sarah Vasquez (BUOW DB) Sean Herman (BM) Shannon Morris (BUOW DB) Sierra Bennaton (BM) Stella Moore (BM) William Ryan (GDB) Kayci Owen (CRM) Darren Putty (CRM) Chris Chambers (CRM) Jake Farhar (PRM)			
25	BAAH: Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Drilling, backfilling trenches, installing busbars, concrete pouring, laying rip rap on downslope of switchyard, staging equipment, dust suppression. BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored RTHA nest ESA; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	PVB/Gen-tie: Alex Welch (BUOW DB) Brittany Gummo (SWHA/BUOW DB) Cameron Reid (GDB) Danielle Simmons (BM) David Wappler (SWHA/BUOW DB) Emily Smith (BM) Emma McAndrews (BM) Eric Cerecedes (BM)	PVB/Gen-tie: Construction activities: Basin and perimeter berm grading, culvert riprap installation on road 202, hydroseed spraying on berm and surrounding flat ground, installation of I-beams, conduit installation and backfill, pouring cement at pier structures, finished rebar pads, continued setting forms, continued backfill and compaction of EEE's, deliveries, staging materials, module, array and inverter installation, Excavation of trenches, installation of home runs and MV bullhorns, installation of wiring and conduit. backfilling and compacting of trenches, installation of conduit and wiring within trenches, pile cap installation, pile driving, road grading and watering, pile install and MV plow, plowing and laying electrical wire, discing of grassland by tractor, staging for cement pour, drilling, dust	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Loggerhead shrike, SSC; Northern harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Erwin Sandhu (BM)	suppression, traffic along artery road, removal of t-posts, installation of t-		
	Gerardo Morales (BM)	posts, basin construction, excavating trenches.		
	Jack Quinzon (BM)	BM activities: Conducted pre-activity sweep of project site; monitored		
	Jackie Dougherty (BM)	daily construction activities; ESA monitoring; end of day clearance sweep		
	Jessica Lotts (BM)	CRM activities: monitored daily construction activities		
	Joshua Oyeboade (BM)	PRM activities: monitored daily construction activities		
	Kyle Rader (GDB)			
	Michael Hahn (BM)			
	Michael Schwanhausser (GDB)			
	Nicole Carpenter (BM)			
	Oliver Scott (BM)			
	Rachel Clark (SWHA/BUOW DB)			
	Rainey Davis (BUOW DB)			
	Reggie Borntrager (BM)			
	Reilly Miller (BM)			
	Ruby Sainz (BM)			
	Sam Wasserman (BM)			
	Samantha Love (GDB)			
	Sarah Jacobsen (GDB)			
	Sarah Vasquez (BUOW DB)			
	Sean Herman (BM)			
	Sierra Bennaton (BM)			
	Summer Milner (BM)			
	Whitney Vickers (BM)			
	William Ryan (GDB)			
	Kayci Owen (CRM)			
	Darren Putty (CRM)			
	Chris Chambers (CRM)			
	Jake Farhar (PRM)			

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
26	BAAH: Nicole Carpenter (BM) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Drilling, cement pouring, busbar installation, preparing pylon foundations/forms, staging equipment, dust suppression BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored RTHA nest ESA; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	None	None to report
	Alex Welch (BUOW DB) Brittany Gummo (SWHA/BUOW DB) Cameron Reid (GDB) Danielle Simmons (BM) David Wappler (SWHA/BUOW DB) Bobby Luangrath (BM) Jace Pearson (BM) Emma McAndrews (BM) Eric Cerecedes (BM) Erwin Sandhu (BM) Gerardo Morales (BM) Jack Quinzon (BM) Jackie Dougherty (BM) Jessica Lotts (BM) Joshua Oyeboade (BM) Michael Schwanhausser (GDB) Nicole Carpenter (BM) Oliver Scott (BM) Rachel Clark (SWHA/BUOW DB) Rainey Davis (BUOW DB) Reggie Borntrager (BM) Reilly Miller (BM) Madison Wallwork (BM)	PVB/Gen-tie: Construction activities: Mowing transects in Area 1, discing, basin work, plowing, underground wiring, berm work with bulldozer, solar panel assembly, piledriving, electrical subgrading, transport and delivery of materials, dust abatement with water trucks, module rail install, power remediation, tracker assembly, staging materials, ESA T-Post Buffer installation/removal, FNE rack installation, backfill of trenches, installation of conduit within trenches, pile driving, installation of pile caps, movement of equipment and piles, grubbing of vegetation for new laydown yard extension east of pad, delivery of base rock and road compaction BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; monitored ESA; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Northern harrier, SSC	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Sam Wasserman (BM) Sarah Vasquez (BUOW DB) Sean Herman (BM) Sierra Bennaton (BM) Summer Milner (BM) Whitney Vickers (BM) William Ryan (GDB) Alicia Manzo (BM) Camille Troncone (GDB) Danielle Simmons (BM) Kayci Owen (CRM) Darren Putty (CRM) Chris Chambers (CRM) Jake Farhar (PRM)			
27	BAAH: Gerardo Morales (BM)	BAAH: Construction activities: Breaker installation, underground vault and conduit, cement pouring and foundation framework BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities	None	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	PVB/Gen-tie: Danielle Simmons (BM) Oliver Scott (BM) David Wappler (SWHA/BUOW DB) Erwin Sandhu (BM) Jessica Lotts (BM) Chris Chambers (CRM) Jake Farhar (PRM)	PVB/Gen-tie: Construction activities: Transformer pad replacement, drilling, excavating, and stockpiling, BESS crews installing piles, spraying for dust abatement, excavation for ground wiring installation, backfilling trenches, cement pour of rebar pad, battery pads and pier structures, continued conduit installation and backfill, continued backfill and compaction of transformer, mowing in Area 16 BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; nest buffer stake installation; nest monitoring; assisted drone pilot; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	Swainson's hawk, ST; Northern harrier, SSC, Darden-Monitoring Phase-Site 2 (CR historical refuse deposit)	None to report
29	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Bulldozing, moving materials, installing rip rap slope, grading, pouring cement, drilling, delivering materials, and dust control BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activities PRM activities: monitored daily construction activities	N/A	None to report

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Alex Aylard (GDB)	PVB/Gen-tie:	Swainson's hawk, ST; Loggerhead shrike, SSC; Northern harrier, SSC	None to report
	Amy Plesetz (BUOW DB)	Construction activities: Tilling, staging and traffic, Trenching, MV plow and big blade throughout the area, Pouring cement for transmission structure, grading and compacting, Clearing vegetation and water truck for dust abatement, Mowing in Area 16, Splicing cables, excavating trenches for inverters, grading, hydro seeding, Material Staging, Grading, Tube Installation, Pile Driving, Backfill Compaction, Excavations, installed torque tubes onto array piles (using telehandlers and manual labor), conducted MV Plow work (including trenching, excavating, and wire placement inside trenches), conducted pile driving, received deliveries of solar equipment (i.e., wooden crates, metal beams, piles), installed solar modules and brackets within the solar arrays, conducted electrical work, and offloaded and staged these materials from the semi-trucks using telehandlers, halo backfill, install and torquing pile caps, MegaPack / PMT piles, material deliveries, innerduct install, FNE trench install and backfill, conduit installation, MV Bullhorn, FNE rack, and CAT6 mockup prefab, solar homerun trenching, bedding, innerduct installation, MV wire pull, meggering, MV bullhorn trenching, NETA testing		
	Andrew Alba (GDB)			
	Bobby Luangrath (BM)			
	Caleb Yakel (SWHA/BUOW DB)			
	Cameron DeMaranville (BM)			
	Cameron Reid (GDB)			
	Camille Troncone (GDB)			
	Cody Hurt (GDB)			
	David Wappler (SWHA/BUOW DB)			
	Ellery Charelton (BM)			
	Emma McAndrews (BM)			
	Eric Cerecedes (BM)			
	Gerardo Morales (BM)			
	Jace Pearson (BM)			
	Jack Quinzon (BM)			
	Joey Medina (BUOW DB)	BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; nest checks; buffer checks; end of day clearance sweep		
	Katherine Phillips (GDB)			
	Kyle Rader (GDB)	CRM activities: monitored daily construction activities		
	Moses Lopez (BM)	PRM activities: monitored daily construction activities		
	Nathalie Treminio (GDB)			
	Nick Fager (SWHA/BUOW DB)			
	Nikki Caravelli (BM)			
	Rowdy Freeland (GDB)			
	Samantha Love (GDB)			
	Sarah Jacobsen (GDB)			
	Sean Herman (BM)			
	Shannon Morris (BUOW DB)			
	Summer Mersereau (BM)			
	Timothy Gaffney (BUOW DB)			
	Kayci Owen (CRM)			
	Darren Putty (CRM)			

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Cristian Martinez (CRM) Viviana Navarro (CRM) Jake Farhar (PRM)			
30	BAAH: Nick Julier (GDB) Breahna Fogg (CRM/PRM)	BAAH: Construction activities: Bulldozing, moving materials, installing rip rap slope, grading, pouring cement, digging, drilling, delivering materials, and dust control BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activity PRM activities: monitored daily construction activities	N/A	None to report

PVB/Gen-tie: Amy Plesetz (BUOW DB) Bobby Luangrath (BM) Caleb Yakel (SWHA/BUOW DB) Cameron Reid (GDB) David Wappler (SWHA/BUOW DB) Eduardo Corona (BM) Emily Smith (BM) Emma McAndrews (BM) Gerardo Morales (BM) Jace Pearson (BM) Jack Quinzon (BM) Jeffrey Holland (BM) Joey Medina (BUOW DB) Joshua Oyeboade (BM) Katherine Phillips (GDB) Michael Hahn (BM) Moses Lopez (BM) Nathalie Treminio (GDB) Nick Fager (SWHA/BUOW DB) Nick Julier (GDB) Nikki Caravelli (BM) Rachael Iverson (BM) Rob Weber (BM) Samantha Love (GDB) Sarah Jacobsen (GDB) Sarah Vasquez (BUOW DB) Sean Herman (BM) Shannon Morris (BUOW DB) Summer Mersereau (BM) Timothy Gaffney (BUOW DB) William Ryan (GDB) Kayci Owen (CRM) Darren Putty (CRM)	PVB/Gen-tie: Construction activities: Tilling, staging materials, compacting, tube Installation, material delivery, pile driving, soil compaction, cable plowing, cable splicing, excavations, backfilling installed MV line, solar array material placing, solar module installation, grading road, dust abatement using water, hay bale installation, grubbing, grader, water truck activity, mowing, homerun /AC trench, pile caps, FNE racks, halo, bracket installation, torque tube installation, herbicide application in Area 8, cement pour, soil deliveries, transformer walls, thumpers for compaction, conduit installations, drilling, BESS yard trenching, installing bases for solar panels, mowing in Area 16, diversion berm buildout, inverter pile driving and pile distribution BM activities: Conducted pre-activity sweep of project site; monitored daily construction activities; end of day clearance sweep CRM activities: monitored daily construction activity PRM activities: monitored daily construction activities	Burrowing owl, candidate species, SSC; Swainson's hawk, ST; Loggerhead shrike, SSC; Northern Harrier, SSC	None to report
---	---	---	----------------

Date	Monitor	Summary of Activities	Known Sensitive Resources	COC Compliance Concerns
	Cristian Martinez (CRM)			
	Viviana Navarro (CRM)			
	Jake Farhar (PRM)			

Appendix C

Harlan Switching Station Compliance Report – June 2026

HARLAN SWITCHING STATION COMPLIANCE REPORT JUNE 2026

PREPARED FOR:
CALIFORNIA ENERGY COMMISSION ON
JULY 1ST, 2026




Table of Contents

- **GEN-02 & COM-06:**

1. Project schedule
2. Project permits
3. Items added to on-site compliance file (01.2026)
4. Compliance activities outlook (.01.2026 & 02.2026)
5. Compliants, notices of violation, official warnings, and/or citations received.

- **SWITCH-AQ-01 & AQSC-04:**

1. Summary of actions taken to maintain compliance with this condition
2. Complaints filed with regional APCD received.
3. Daily air quality inspection reports

- **SWITCH-GHG-01:**

1. AQSC-05
 - Summary of actions taken to maintain compliance with this condition
 - Monthly equipment inventory & run time.
 - Monthly GHG-01 best practices inspection

- **WATER-06:**

1. Summary of monthly water use

- **WORKER-SAFETY-03:**

1. Monthly safety inspection
2. Training sign-in sheets
3. NOISE-02
 - Noise exposure log & monitoring
4. WORKER-SAFETY-11
 - Respirator training & monitoring
 - Valley fever symptoms and/or case reporting
5. SWITCH-HAZ-02
 - Monthly fire extinguisher inspection

- **TRANS-02:**

1. Haul permits log.
2. Hazardous materials delivery log

GEN-02 & COM-06

1. PROJECT SCHEDULE

Construction at the Harlan Switching Station continues to progress smoothly and remains on schedule. During the month of June, key construction activities included conduit excavation and trenching, continued drilling and pouring of foundations, and the installation and completion of structural fill and the retention basin.

The MPAC building, which arrived on site in May, is currently undergoing wiring activities. Building commissioning is scheduled to begin in July. Significant progress was also achieved by the above-grade electrical crews throughout June, including steel erection and the installation of hard bus and insulators. All structural steel is anticipated to be fully erected during the month of July.

The microwave tower foundations have been successfully poured and, pending acceptable concrete break test reports, tower installation is expected to occur in July.

Looking ahead, July will be a productive month as crews work toward completing all remaining foundations by mid-month, along with the infrastructure necessary to support distribution and station service systems. Structural steel erection is expected to be completed, allowing crews to transition into setting major electrical apparatus across the site.

Safety continues to be a top priority for the project team. Dashiell has maintained excellent safety performance to date, with zero recordable incidents on the project. The team remains committed to upholding this standard and delivering the project incident-free.

As seasonal temperatures continue to rise, additional emphasis is being placed on heat illness prevention through increased awareness, active monitoring, and enhanced mitigation measures for both crews and subcontractors. Dust control will also remain a key focus as dry summer conditions persist, with appropriate measures being implemented to minimize impacts and maintain a safe working environment.

Current progress toward major construction tasks is as follows:

<u>Task</u>	<u>Status</u>
Site preparation BMPs	100% complete
Burrow cleaning (in coordination with Rincon)	100% complete
Stripping organics across site	100% complete
Pad over-excavation	100% complete
Pad cut / fill / compaction	95% complete.
Access road installation	100% complete
Foundation Survey	100% complete
MPAC Foundation	100% complete
Cut in road/add base rock	60% complete
Installation of Rip Rap	80% complete

GEN-02 & COM-06

Foundation Installation	77% complete
MPAC Building Installation	67% complete
MPAC Internal Wiring	35% complete
Conduit Installation	45% complete
Steel Erection	76% complete
Insulator Installation	25% complete
Bus Installation	10% complete

GEN-02 & COM-06

Harlan Project

21055 South Derrick Ave, Cantua Creek, CA, 93608

WEEKLY REPORT

Job #: 604650		Week Ending: June 7, 2026																				
Site Manager: Julian Robertson		Project Manager: Trevor Young																				
Workforce	Weekly Activities	M	T	W	Th	F	S	Su														
Dacon - Civil	Fill dirt Imported	90	100	100	100	100																
	Geotech fabric																					
	Riprap																					
	SWPPP repairs																					
Dacon - Electrical	Truck Deliveries, inventory material, build glass	20	30	30	30	10																
	set bolt heights for steel set prep		10	10	10	10																
	Bring and set up steel on pad	10	20	20	20	30																
	Set steel	60	40	40	40	50																
Dacon - Foundations	Drilled foundation piers	22	12	8	10	12	20															
	Formed foundation piers/ set rebar cages/ set anchor bolts	30	40	12	38	20	14															
	Placed concrete piers			36			38															
	Placed slurry in duct banks/ backfill	26	28	24	28	26																
	Dig Trenches	32	28	38	40	30	12															
	Install underground conduit	40	42	32	34	42	44															
	Install pullboxes/ Vaults					20	22															
Trachte/Sheedy/ABB	Installing equipment and wiring inside building	40	40	40	40	40																
	Set battery buildings 49.1 and 49.2/ punch list		60	30	30	40																
Total Manhours		370	450	420	420	430	150	0														
3 WEEK LOOK AHEAD																						
Workforce	Planned Activities:	M	T	W	Th	F	S	Su	M	T	W	Th	F	S	Su	M	T	W	Th	F	S	Su
Dacon Civil	Pad Area	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28
	Import, Lift and Compaction of Quadrants 2 and 4	x	x																			
	Scrape slopes in quads 2 and 4 to final grade			x	x	x			x	x	x	x	x			x	x	x	x	x		
	Install GeoTech fabric			x	x	x			x	x	x	x	x			x	x	x	x	x		
	Install Riprap on slopes			x	x	x			x	x	x	x	x			x	x	x	x	x		
	Install road base																					
	Work on spoils	x	x	x	x	x				x							x					
Dacon Electrical	Receive/store material/build glass	x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		
	Pre work for steel installation	x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		
	Install steel	x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		
Dacon Foundation	Foundation work																					
	Breaker Panel foundations	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x	x		
	AC panels foundations																					
	Underground conduit install/pull boxes/trenching	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x	x		
	Drilling Piers, placing cages, building forms	x	x	x	x	x	x		x	x	x	x	x			x	x	x	x	x		
	Placing concrete			x		x				x		x					x		x			
Trachte/Sheedy/ABB	MPAC																					
	Installing equipment and wiring inside IMPAC	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x	x		
Total Projected Manpower																						
Project Specific Contacts																						
Contact Name & Title	Company	Phone #	Contact Name & Title	Company	Phone #																	
Trevor Young - PM	Dashiell	281-450-2971																				
Isaac Sandoval - APM	Dashiell	346-870-9501																				
Julian Robertson - CM	Dashiell	601-590-1884																				



GEN-02 & COM-06

Harlan Project

21055 South Derrick Ave, Cantua Creek, CA, 93608

WEEKLY REPORT

Job #: 604650

Week Ending:

June 14, 2026

Site Manager: Julian Robertson

Project Manager:

Trevor Young

Workforce	Weekly Activities	M	T	W	Th	F	S	Su
Dacon - Civil	Lift / level pad / build pond	85	85	15	15	15		
	Geotech fabric			40	40	40		
	Riprap			30	30	30		
	Scrape slopes	15	15	15	15	15		
Dacon - Electrical	Truck Deliveries, inventory material, build glass	20		10	15	10	20	
	set bolt heights for steel set prep	10		20	15	20	20	
	Bring and set up steel on pad	10		20	20	40	20	
	Set steel	60		40	40	20	40	
Dacon - Foundations	Drilled foundation piers	20	20	20	20	10		
	Formed foundation piers/ set rebar cages/ set anchor bolts	70	70	60	70	20		
	Placed concrete piers					60	60	
	Set imbeds	20		20	20	20	20	
	Placed slurry in duct banks/ backfill	40	40	20	10			
	Dig Trenches	30	30	30	30	30	40	
	Install underground conduit	80	80	60	60	70	70	
	Install pullboxes/ Vaults						20	
Trachte/Sheedy/ABB	Installing equipment and wiring inside building	20	40	40	40	30	15	
Total Manhours		480	380	440	440	430	325	0

3 WEEK LOOK AHEAD

Workforce	Planned Activities:	M	T	W	Th	F	S	Su	M	T	W	Th	F	S	Su	M	T	W	Th	F	S	Su
Dacon Civil	Pad Area	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5
	Import, Lift and Compaction of Quadrants 2 and 4																					
	Scrape slopes in quads 2 and 4 to final grade	x	x	x	x	x			x	x	x	x	x			x	x	x	x			
	Install GeoTech fabric	x	x	x	x	x			x	x	x	x	x			x	x	x	x			
	Install Riprap on slopes	x	x	x	x	x			x	x	x	x	x			x	x	x	x			
	Install road base																					
Dacon Electrical	Work on spoils		x		x					x		x					x		x			
	Receive/store material/build glass	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x			
	Pre work for steel installation	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x			
Dacon Foundation	Install steel	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x			
	Foundation work																					
	Breaker Panel foundations	x	x	x	x	x																
	AC panels foundations																					
	Underground conduit install/pull boxes/trenching	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x			
Trachte/Sheedy/ABB	Drilling Piers, placing cages, building forms	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x			
	Placing concrete		x		x				x		x					x		x				
MPAC	Installing equipment and wiring inside IMPAC	x	x	x	x	x	x		x	x	x	x	x	x		x	x	x	x			
Total Projected Manpower																						

Project Specific Contacts

Contact Name & Title	Company	Phone #	Contact Name & Title	Company	Phone #
Trevor Young - PM	Dashiell	281-450-2971			
Isaac Sandoval - APM	Dashiell	346-870-9501			
Julian Robertson - CM	Dashiell	601-590-1884			



GEN-02 & COM-06

Harlan Project

21055 South Derrick Ave, Cantua Creek, CA, 93608

WEEKLY REPORT

Job #: 604650

Week Ending:

June 21, 2026

Site Manager: Julian Robertson

Project Manager:

Trevor Young

Workforce	Weekly Activities	M	T	W	Th	F	S	Su
Dacon - Civil	Lift / level pad / build pond	20	20	20	20	20		
	Geotech fabric	30	30	20	20	20		
	Riprap	30	30	30	20	20		
	Bring in base rock for roads				20	20		
Dacon - Electrical	Scrape slopes	20	20	20	20	20		
	Truck Deliveries, inventory material, build glass	10	5	10	5	30	10	
	set bolt heights for steel set prep	20	35	20	20	5	20	
	Bring and set up steel on pad	20	20		5			
Dacon - Foundations	Set steel, apparatus, and insulators	50	30	60	70	65	70	
	Drilled foundation piers	20	20	20	20			
	Formed foundation piers/ set rebar cages/ set anchor bolts	60	60	60	20	60	40	
	Placed concrete				60	80	80	
Trachte/Sheedy/ABB	Set imbeds		30	15				
	Placed slurry in duct banks/ backfill	20	20	25	20	60	60	
	Dig Trenches	20	30	40	40	20	40	
	Install underground conduit	40	50	50	40		40	
Total Manhours		404	433	423	464	464	360	0

3 WEEK LOOK AHEAD		M	T	W	Th	F	S	Su	M	T	W	Th	F	S	Su	M	T	W	Th	F	S	Su
Dacon Civil	Pad Area	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6	7	8	9	10	11	12
	Import, Lift and Compaction of Quadrants 2 and 4		x		x					x	x	x					x	x	x			
	Scrape slopes in quads 2 and 4 to final grade	x	x	x	x	x				x	x	x					x	x	x	x	x	
	Install GeoTech fabric	x	x	x	x	x				x	x	x	x				x	x	x	x	x	
	Install Riprap on slopes	x	x	x	x	x				x	x	x	x				x	x	x	x	x	
	Install road base	x	x	x	x	x				x	x	x	x									
	Work on spoils		x		x					x	x						x		x			
Dacon Electrical	Receive/store material/build glass	x	x	x	x	x	x			x	x	x	x				x	x	x	x	x	
	Pre work for steel installation	x	x	x	x	x	x			x	x	x	x				x	x	x	x	x	
	Install steel, apparatus, and insulators	x	x	x	x	x	x			x	x	x	x				x	x	x	x	x	
Dacon Foundation	Foundation work	x	x	x	x	x	x															
	Breaker Panel foundations	x	x	x	x	x	x															
	AC panels foundations																					
	Underground conduit install/pull boxes/trenching	x	x	x	x	x	x			x	x	x	x				x	x	x	x	x	
	Drilling Piers, placing cages, building forms	x	x	x	x	x	x			x	x	x	x				x	x	x	x	x	
Trachte/Sheedy/ABB	Placing concrete		x				x			x	x						x		x			
	MPAC																					
	Installing equipment and wiring inside MPAC	x	x	x	x	x	x			x	x	x	x				x	x	x	x	x	
Total Projected Manpower																						

Project Specific Contacts					
Contact Name & Title	Company	Phone #	Contact Name & Title	Company	Phone #
Curtis Barth - PM	Dashiell	801-865-7314			
Isaac Sandoval - APM	Dashiell	346-870-9501			
Julian Robertson - CM	Dashiell	601-590-1884			



GEN-02 & COM-06

2. PROJECT PERMITS

Dashiell received an Encroachment Permit from the Fresno County Road Maintenance and Operations Division on November 11, 2025, authorizing construction of the switching station access road within the County Right-of-Way (ROW). The permit remains valid through December 29, 2025.

In addition, Dashiell's construction business unit, Dacon, secured water-use rights for the project from Britz Helm TIC on October 13, 2025. This agreement authorizes the use of up to seven acre-feet of water to support project activities - including, but not limited to, dust suppression for the duration of construction.

GEN-02 & COM-06

 Mohamoud Mohamed	ROAD IMPROVEMENT PERMIT COUNTY OF FRESNO ROAD MAINTENANCE AND OPERATIONS DIVISION MAILING ADDRESS: 2220 TULARE STREET, 6 TH FLOOR, FRESNO, CA 93721 OFFICE LOCATION: SOUTHWEST CORNER OF TULARE & 'M' STREETS, SUITE B In compliance with County of Fresno Ordinance Nos. 13.04040, 13.08.010 and Chapter 5.5 of Division 2 of the Streets and Highways Code, the undersigned hereby applies for permission to excavate, construct and/or otherwise encroach on the County right-of-way by performing the following work.		
	PROJECT INFORMATION		
	Permit Title: Harlan Switching Station Access Road 20' Approach Location of Proposed Work: S DERRICK AVE, APPROX. 5,000 S/O HWY I-5	Permit No: IP25-0970 Folder No.: 25 014801 For Inspection Service: Phone: (559) 600-4240 Fax: (559) 600-4203 EncroachmentPermits@fresnocountyca.gov	
	Description of Proposed Work: Authorization is granted to place and utilize traffic control devices within the County of Fresno Road right of way for constructing a 20'W gravel driveway entrance for the Harlan Switching Station as shown on the provided permit drawings.		
THIS APPLICATION IS YOUR PERMIT WHEN STAMPED AND SIGNED ABOVE	11/13/25 Estimated Starting Date	12/2/25 Estimated Completion Date	10 Traffic Control Days
consideration of the granting of this application, it is agreed that the applicant shall indemnify the County of Fresno and any of its officers, employees and agents and shall defend and hold them harmless from any and all claim or liability for personal injury or property damage due to any acts or failure to act in connection with any work permitted herein. Applicant further agrees to comply with all terms, conditions and specifications contained below and on the reverse side hereof.			
PERMIT APPROVAL			
NOTIFY THE COUNTY OF FRESNO PERMIT DESK AT (559)600-4240-4240 A MINIMUM OF 48 HOURS IN ADVANCE OF BEGINNING CONSTRUCTION ACTIVITIES. Permission is hereby granted to perform the above-described work subject to all terms, conditions and restrictions contained below and on the reverse side hereof. This permit is to be strictly construed and no work other than that specified is authorized hereby. This permit is expressly conditioned upon performance of the work. Failure to perform said work in accordance with County specifications shall be deemed an immediate revocation of this permit and without notice. WORK SHALL BE SUBJECT TO COUNTY INSPECTION. PERMITEE SHALL NOTIFY COUNTY INSPECTOR Nuvdeep Jhutti A MINIMUM OF 48 HOURS BEFORE STARTING WORK. 559-554-4101 THIS PERMIT SHALL BE VOID UNLESS THE WORK HEREIN CONTEMPLATED SHALL HAVE BEEN COMPLETED BEFORE 12/2/25 9:41AM. To commence or complete work after said date requires approved application for permit renewal or time extension. Grantor reserves the right to complete the work to restore.			
PROJECT CONDITIONS			
ATTACHED ADDENDUM IS A PART OF THIS PERMIT			
APPLICANT: Starflower Environmental ADDRESS: 801 BIG BEAVER RD W SUITE 300, TROY MS 48084- PHONE: (734) 645-4098 EMAIL:		OWNER: IP DARDEN I, LLC c/o Intersect Po ADDRESS: 9460 SW Gemini Drive PMB #68743, Beaverton, OR PHONE: (805) 644-4455 EMAIL:	
Project Manager: Myles Markey (734) 645-4096			
APPLICANT SIGNATURE: (X) _____		DATE: _____	
ACCOUNT NUMBER: _____		BOND NUMBER: _____	
PERMIT QUANTITIES & INSPECTION FEES			
2201.A.11 - Traffic Control System		426.00 10 days of TC	
2204.A.4 - Asphalt Concrete (HMA) Approach/Front		367.00 20' W Gravel A	
TOTAL PROJECT FEES: 793.00			

Permit No.: IP25-0970

MTCE Area: 03

 Steven E. White, Director
 Department of Public Works & Planning

By:

Mohamoud Mohamed

Date: 11/12/25

for

Ruben Garcia, Permit Engineer

WHITE - Office Copy

GREEN - Inspector Copy

CANARY - Permittee Copy


PINK - Accounting Copy

GOLDENROD - Area Supervisor Copy

FOR OFFICE USE ONLY




GEN-02 & COM-06

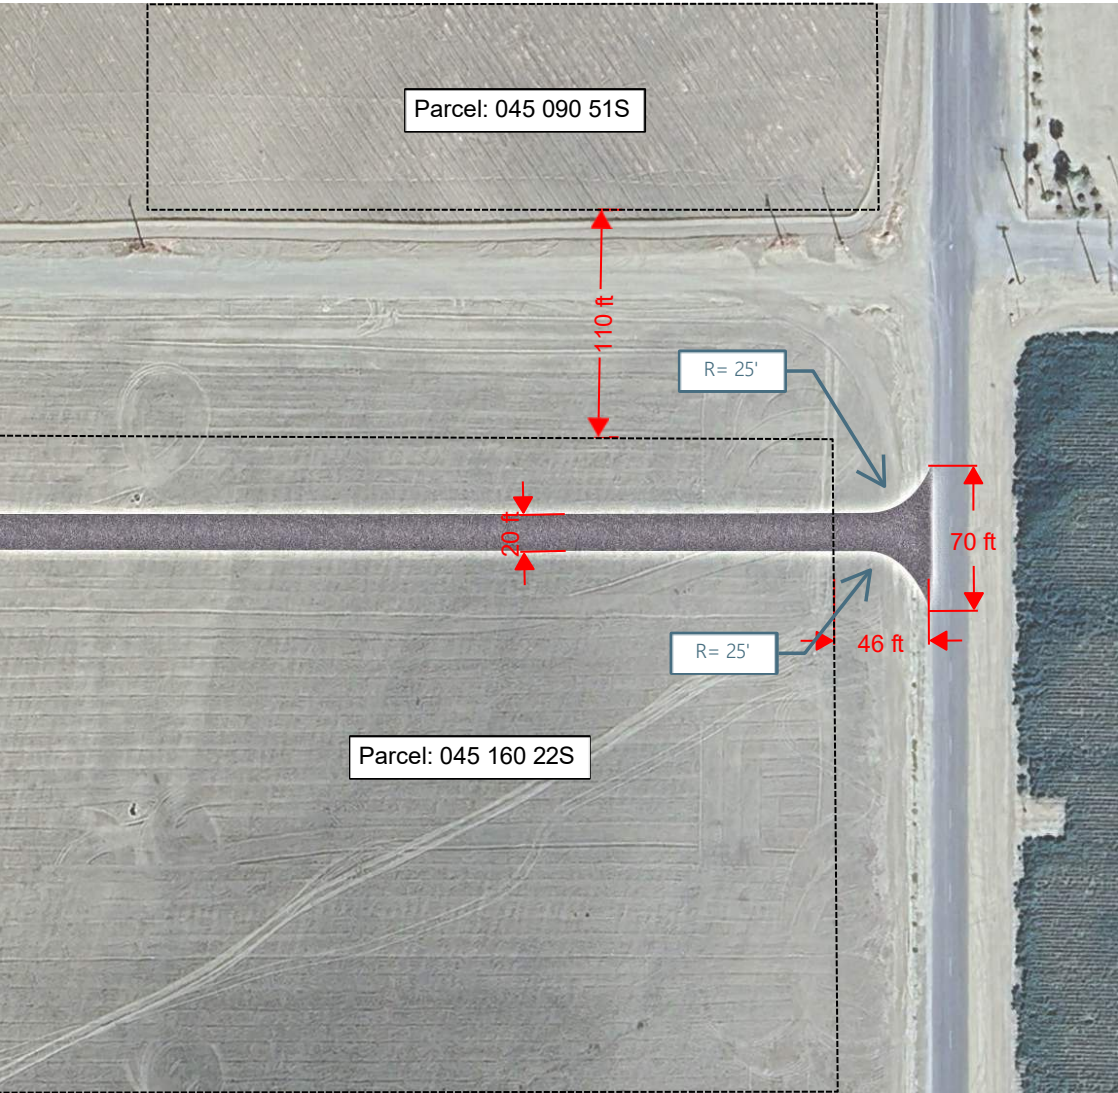

NOTES:
ROADWAY CONSTRUCTION WITHIN
FRESNO COUNTY ROW SHALL BE
CONSTRUCTED TO THE COUNTY OF
FRESNO DEPARTMENT OF PUBLIC
WORKS AND PLANNING DETAIL
ST32: RURAL RESIDENTIAL
DRIVEWAY APPROACH

SHEET TITLE:	HARLAN ACCESS ROAD JUNCTION DIMENSIONS
PROJECT:	HARLAN 500KV BAAH SWITCHYARD
ROADWAY:	S. DERRICK AVE.
DATE:	11/12/2025
REV:	02




GEN-02 & COM-06

DURATION OF ENCROACHMENT PERMIT:	12/01/2025 - 12/29/2025
TRAFFIC CONTROL TOTAL NUMBER OF DAYS:	4
WORK HOURS:	7AM-4PM
ON SITE PROJECT MANAGER:	ISAAC SANDOVAL (346)-870-9501

NOTES:
1. SEE CALIFORNIA MUTCD 2014 EDITION
DETAIL TA-6 AND FIGURE
6H-7 FOR FURTHER DETAIL.

Tracy
Barnes
2025.11.2
6 10:44:24
-08'00'

SHEET TITLE:	HARLAN EP TRAFFIC CONTROL PLAN OVERVIEW
ROADWAY:	S. DERRICK AVE.
DATE:	11/24/2025
PROJECT:	HARLAN 500KV BAAH SWITCHYARD



POLYLINE CURVE POINTS		
POINT	CURVE DATA (N/E/ELEVATION)	ELEVATION
D4	N=2041938.7003' E=6147016.7362'	572.04'
D5	N=2042003.6983' E=6147082.2477'	569.64'
D6	N=2041999.6045' E=6147602.3896'	553.03'
D7	N=2041995.3303' E=6148145.4503'	545.58'
D8	N=2041989.0340' E=6148945.4255'	530.10'
D9	N=2041991.9507' E=6149845.3976'	515.24'
D10	N=2041974.8674' E=6150745.3697'	496.25'
D11	N=2041968.4911' E=6151555.5175'	485.21'
D12	N=2041967.3953' E=6151694.7445'	484.63'
D13	N=2042021.9608' E=6151750.1756'	484.15'



GEN-02 & COM-06



DACON CORPORATION



1300 UNDERWOOD DEERPARK, TX 77536

PHONE: 713-578-6001

WATER PROCUREMENT AGREEMENT

This Water Procurement Agreement ("Agreement") is entered into as of [Effective Date] by and between ~~Britz Farming Corp.~~ ("Seller") and Dacon Corp. ("Buyer").

Britz Helm TIC

1. Purpose

Seller agrees to supply, and Buyer agrees to purchase and take delivery of, up to seven (7) acre-feet of water for Buyer's operational needs, on the terms set forth herein.

2. Quantity; Term

2.1 Contract Quantity: Total quantity available under this Agreement shall not exceed 7.0 AF during the Term.

2.2 Term: This Agreement commences on the Effective Date of 10/13/2025 and continues through 4/6/2027 unless earlier terminated.

3. Price; Billing; Payment

Price: \$3,000.00 per Acre-Foot (AF).

Billing: Seller will invoice monthly based on metered volume delivered. Each invoice will show meter readings delivered.

Payment Terms: Net 30 days from invoice date.

4. Delivery; Title; Risk of Loss

Delivery will be made at the Delivery Point(s). Title and risk of loss for water pass to Buyer at the Delivery Point.

GEN-02 & COM-06

5. Measurement; Tracking; Access

Deliveries shall be measured by calibrated meters. Seller will provide Buyer with monthly meter logs. Buyer may inspect meters with notice.

6. Shortage; Curtailment

Deliveries may be reduced or suspended due to shortages, regulatory curtailments, or force majeure. Charges apply only to volumes actually delivered.

7. Water Rights; Quality; Use

Seller represents it has the right to deliver water. Water is delivered as-is. Buyer is responsible for use and end-use permits.

8. Default; Remedies; Termination

Buyer default for nonpayment after 30 days' notice allows Seller to suspend deliveries. Seller default not cured within 15 days allows Buyer to terminate.

9. Governing Law

This Agreement is governed by the laws of the State of CA. Disputes shall be resolved in courts located in [Fresno County,CA].

SIGNATURES

SELLER: Brintz Farming Corp.

By: David Brintz

Name: David Brintz

Title: Partner

Date: 10/13/25

BUYER: Dacon Corp.

By: Richard Lee

Name: Richard Lee

Title: Purchasing

Date: 10/06/2025

GEN-02 & COM-06

3. ITEMS ADDED TO ON-SITE COMPLIANCE FILE

The following Conditions of Compliance (COC) items were added to the on-site monthly comply file for the Harlan Switching Station:

CONSTRUCTION & TRANSPORTATION

TRANS-02

Haul permits log.

Hazardous waste delivery log

TRANS-03

Roadway inspection, pre-mobilization

SWICH-WASTE-01

Waste diversion training log.

HEALTH & SAFETY

WORKER-SAFETY-11

Valley fever training log

Air quality monitoring & inspections

NOISE-02

Noise pollution training log

SWITCH-HAZ-02

Emergency & fire protection training log

Fire extinguisher inspection form

WORKER-SAFETY-03

General site safety inspection & certification

ENVIRONMENTAL

SWITCH-HAZ-01

Monthly SPCC inspection

Waste Management

SWITCH-WATER-01

Weekly & post precipitation bmp inspections

GEN-02 & COM-06

COMPLIANCE ACTIVITIES OUTLOOK – JUNE 2026 & JULY 2026

Dashiell will continue performing the following routine COC activities:

CONSTRUCTION & TRANSPORTATION

TRANS-02

Haul permits log.

Hazardous waste delivery log

SWICH-WASTE-01

Waste diversion training log

Monthly waste diversion log

Construction waste log.

HEALTH & SAFETY

WORKER-SAFETY-1 1

Valley fever training log

Air quality monitoring & inspections

SWITCH-HAZ-02

Emergency & fire protection training log

Fire extinguisher inspection form

WORKER-SAFETY-03

General site safety inspection & certification

ENVIRONMENTAL

SWITCH-HAZ-01

Monthly SPCC inspection

SWITCH-WATER-01

Weekly & post precipitation bmp inspections

SWITCH-GHG-01

Implementation of greenhouse emissions reduction

Combustion engine emissions log

GEN-02 & COM-06

Dashiell will perform the following COC activities as needed, based on corresponding conditional triggers:

CONSTRUCTION & TRANSPORTATION

VIS-02

Site lighting inspection by Compliance Project Manager (CPM)

SWITCH-AQ-01

Dust plume complaint report and corrective action plan.

HEALTH & SAFETY

WORKER-SAFETY-11

Mandatory respirator requirements, including buddy system training, implementation and fit.

checks

Suspected case report form

High risk BMP implementation and/or construction activity suspension

SWITCH-HAZ-02

Emergency & fire protection training log

Fire extinguisher inspection form

NOISE-02

High noise activity dosimeter monitoring and subsequent adjacent activity exposure logging

ENVIRONMENTAL

SWITCH-HAZ-01

Post-spill SPCC report

SWITCH-WATER-01

Post-precipitation stormwater BMP inspection and rain gauge check

SWITCH-AQ-01 & AQSC-04

1. SUMMARY OF ACTIONS TAKEN TO MAINTAIN COMPLIANCE WITH THIS CONDITION

Throughout the current phase of construction, the project team has implemented a comprehensive set of dust-control and air-quality protection measures to minimize fugitive emissions, reduce offsite particulate transport, and maintain safe working conditions. Routine watering of disturbed soil has been conducted to preserve adequate surface moisture, supplemented by the retention of vegetation and on inactive areas to reduce wind-driven erosion. Haul routes and primary traffic lanes have been actively maintained through periodic wetting and grading to ensure dust-controlled travel surfaces. Spoil piles and material stockpiles have been stabilized as needed to prevent drying and subsequent plume formation, and, where feasible, heavy equipment has been operated using enclosed, HEPA-filtered cabs to reduce operator exposure.

Operational controls have also been consistently enforced. Site-wide speed limits have been restricted to 10 miles per hour, with further reductions applied during elevated wind conditions or when visible emissions warrant additional caution. Supervisory personnel retain authority to halt dust-generating activities if plume thresholds are reached, ensuring rapid response to changing on-site conditions.

To prevent offsite tracking and transport of soil, the project has maintained rock apron and stabilization features at site exits and applied supplemental watering to minimize material carryout. Adjacent paved surfaces have been cleaned regularly to remove accumulated sediment and limit dust resuspension. Administrative measures, including routine dust-compliance spot checks, visual plume monitoring, opacity observations, and meteorologically based activity triggers, have supported continuous oversight of dust-generating operations.

In accordance with the Construction Management Plan, roadway housekeeping practices have been applied to maintain haul routes and access roads free of mud, loose soil, and track-out. Water has been applied to these surfaces during periods of heavy use to further suppress particulate generation.

Collectively, these measures demonstrate the project's proactive approach to dust mitigation and air-quality management, ensuring compliance with applicable regulatory conditions while supporting worker safety and minimizing environmental impacts.

SWITCH-AQ-01 & AQSC-04

2. COMPLAINTS FILED WITH REGIONAL APCD RECEIVED

- No complaints filed in the month of June 2026

SWITCH-AQ-01 & AQSC-04

3. DAILY AIR QUALITY INSPECTION REPORT

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/1/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/1/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/2/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/2/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/3/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/3/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/4/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/4/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/5/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/5/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/6/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/6/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/8/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/8/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/09/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/09/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/10/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/10/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/11/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/11/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/12/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/12/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/13/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/13/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/15/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/15/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/16/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/16/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/17/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/17/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/18/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/18/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/19/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/19/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/20/26

Inspector: Julian Robertson

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Julian Robertson Date: 6/20/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/22/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scrapping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/22/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/23/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/23/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/24/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/24/26

AIR QUALITY / DUST CONTROL INSPECTION FORM

Project / Site Name: Harlan Switch Station

Date: 6/25/26

Inspector: Isaac Sandoval

Time: 0900

1. Weather Conditions

Parameter	Observation
Temperature (°F)	See attached weather report
Wind Speed (mph)	See attached weather report
Wind Direction	See attached weather report
Humidity (%)	See attached weather report

Conditions: ☐ Calm ☐ Breezy ☐ Windy ☐ Gusty ☐ Other: _____

2. Dust-Producing Activities Observed

Activity	Active Today?	Notes / Area
Grading / Excavation	☒ Yes ☐ No	_____
Scraping / Stockpiling	☒ Yes ☐ No	_____
Loading / Hauling	☐ Yes ☒ No	_____
Soil Compaction / Rolling	☒ Yes ☐ No	_____
Trenching / Backfill	☒ Yes ☐ No	_____
Vehicle Travel on Unpaved Roads	☒ Yes ☐ No	_____
Material Handling / Crushing / Screening	☐ Yes ☒ No	_____
Other Dust Source(s): _____	☐ Yes ☒ No	_____

3. Best Management Practices (BMPs) Implemented

BMP / Control Measure	In Use Today	Comments / Location
Water Truck / Water Tower Application	☒ Yes ☐ No	_____
Wind Breaks / Fencing	☐ Yes ☒ No	_____
Gravel Pads / Track-Out Control	☒ Yes ☒ No	_____
Stabilized Surfaces (Soil Binder, Mulch, etc.)	☐ Yes ☒ No	_____
Reduced Vehicle Speeds (<15 mph)	☒ Yes ☐ No	_____

Ceased Work Due to High Winds	☐ Yes ☐ No	_____
Sweeping / Vacuuming Paved Areas	☐ Yes ☐ No	_____
Covering of Haul Loads	☐ Yes ☐ No	_____
Other Control(s): _____	☐ Yes ☐ No	_____

4. Observations / Corrective Actions

Description	Action Taken / Recommended	Date / Time Completed
_____	_____	_____

5. Photos

_Insert photos below (document visible dust plumes, controls in place, or any observed deficiencies.)

Inspector Signature: Isaac Sandoval Date: 6/25/26

SWITCH-GHG-01

1. AQSC-05: SUMMARY OF ACTIONS TAKEN TO MAINTAIN COMPLIANCE WITH THIS CONDITION

To reduce greenhouse gas emissions associated with construction activities, the project team has implemented a suite of operational controls and workforce practices aimed at minimizing fuel consumption and unnecessary equipment use. Workers are encouraged to carpool whenever feasible, with carpooling opportunities discussed during morning safety briefings and supported by strategically organized parking and staging areas that streamline ride-sharing logistics.

The project enforces a strict no-idling policy in accordance with California Title 13, Section 2485, which prohibits idling beyond five minutes. Crews are routinely reminded of this requirement and of the project's common-sense vehicle-use expectations, both during daily briefings and in pre-construction safety meetings. Construction equipment is staged efficiently throughout the site to reduce idle time during mobilization and sequencing of work. Additionally, all construction equipment is maintained per PG&E standards, ensuring optimal engine performance and reducing avoidable fuel burn.

As part of the project's greenhouse gas mitigation approach, a detailed equipment emissions log is being maintained. This log documents equipment make, model, usage category, and run time for each reporting period. Maintaining an accurate emissions dataset is essential for tracking fuel use, evaluating opportunities for efficiency improvements, and ensuring transparent reporting to the California Energy Commission (CEC). It also supports statewide carbon-reduction initiatives by enabling data-driven verification that construction activities remain consistent with California's greenhouse gas reduction targets under AB 32, SB 32, and CEC Conditions of Certification related to air quality and GHG performance.

Collectively, these measures reflect the project's proactive commitment to minimizing GHG emissions through responsible equipment operation, regulatory compliance, and continuous monitoring that aligns with the State of California's long-term climate and emissions-reduction goals.

SWITCH-GHG-01

2. AQSC-05: MONTHLY EQUIPMENT INVENTORY & RUN TIME

EMISSIONS & DBA LOG		
June Running Hours		
NAME OF EQUIPMENT	MAKE/MODEL	JUNE TOTAL RUN TIME
Motor grader - YA7458	CAT - 160M	171
Paddle Wheel - CK9P83	CAT - 623H	0
Water Truck - 2216	FREIGHTLINER - M2106	171
Water Truck - 2172	FREIGHTLINER - M2106	171
Water Truck - 2217	FREIGHTLINER - M2106	181
Water Truck - 10335191	FREIGHTLINER - M2106	0
Compactor - LB6X99	CAT - 815F2	0
Dozer - YP3U33	CAT - D5	171
Tractor - 11157	Jon Deere - 370 8RT	0
Loader - YM6M43	John Deere - 744	171
Skid Steer - KD8M73	JOHN DEERE - 333G	139
Skid Steer - 2222	JOHN DEERE - 325G	100
Skid Steer -	JOHN DEERE - 325G	100
Skid Steer - BW6A78	JOHN DEERE - 325G	100
UTV - 10442319	Kubota - X1140	100
UTV -	Kubota - X1140	100
UTV - 10442354	Kubota - X1140	100
UTV - 10442300	Kubota - X1140	100
Dump Truck - 10335298	Kenworth - T270	0
Dump Truck - 2225	FREIGHTLINER - M2106	0
Excavator - XJ3X96	John Deere - 210G	0
Drill Rig - 2154	CAT - 330F	121.5
Mini Ex - 2478	JOHN DEERE - 35P	
Forklift -2025	SKYTRAK - 10042	100
Forklift - RK5D38	SKYTRAK - 10042	100
Forklift - 10356562	JCB - 512	90
Light Plant - 10445828	Night Lite - LC 6kW	0
Light Plant - 10445825	Night Lite - LC 6kW	0
Generator - 11089669	Wacker Neuson - G25	480

SWITCH-GHG-01

3. AQSC-05: MONTHLY GHG-01 BEST PRACTICES REPORT

Switchyard Project – Construction Compliance Monitoring Form

Date: 06/25/26

Inspector / Supervisor: Isaac Sandoval

Project Phase: Civil Work

Weather / Conditions: Sunny

1. Carpooling & Commute Efficiency

Compliance Item	Observation / Notes	Yes	No	N/A
Workers encouraged to carpool where feasible		☒	☐	☐
Carpool opportunities discussed in morning / safety briefings		☒	☐	☐
Parking / staging areas support carpooling logistics		☒	☐	☐

2. Vehicle Idling Minimization

Compliance Item	Observation / Notes	Yes	No	N/A
No idling beyond 5 minutes (Cal. Code Regs., Title 13 §2485)		☒	☐	☐
Crews reminded of "common sense" vehicle use policy		☒	☐	☐
Idle reduction policy discussed in preconstruction / safety meetings		☒	☐	☐
Equipment staged efficiently to minimize idling		☒	☐	☐

SWITCH-GHG-01

3. Equipment Maintenance & Emissions

Compliance Item	Observation / Notes	Yes	No	N/A
Construction equipment maintained per PG&E standards		☒	☐	☐
Low-emission or electric equipment used where feasible		☐	☐	☒
Portable diesel engines ≥ 50 hp registered under CARB PERP		☐	☐	☒

4. Welding, Cutting, and Fuel Efficiency

Compliance Item	Observation / Notes	Yes	No	N/A
Mechanical/compression methods used in lieu of welding/cutting when practical		☐	☐	☒
Use of natural gas-powered vehicles encouraged / implemented		☐	☐	☒

Comments / Follow-Up:

Inspector Signature: Isaac Sandoval

Date: 06/25/26

WATER-06

1. SUMMARY OF MONTHLY WATER USE

Water Consumption					
Date	Day	Start Meter	End Meter	Total Acre Feet	Total Gallons
6/1/2026	Monday	373.789	373.944	0.155	50515
6/2/2026	Tuesday	373.944	374.098	0.154	50189
6/3/2026	Wednesday	374.098	374.253	0.155	50514
6/4/2026	Thursday	374.253	374.407	0.154	50189
6/5/2026	Friday	374.407	374.562	0.155	50515
6/6/2026	Saturday	374.562	374.716	0.154	50189
6/7/2026	Sunday				
6/8/2026	Monday	374.716	374.871	0.155	50514
6/9/2026	Tuesday	374.871	375.025	0.154	50189
6/10/2026	Wednesday	375.025	375.18	0.155	50515
6/11/2026	Thursday	375.18	375.335	0.155	50514
6/12/2026	Friday	375.335	375.489	0.154	50189
6/13/2026	Saturday	375.489	375.644	0.155	50515
6/14/2026	Sunday				
6/15/2026	Monday	375.644	375.798	0.154	50189
6/16/2026	Tuesday	375.798	375.953	0.155	50514
6/17/2026	Wednesday	375.953	376.107	0.154	50189
6/18/2026	Thursday	376.107	376.262	0.155	50514
6/19/2026	Friday	376.262	376.416	0.154	50189
6/20/2026	Saturday	376.416	376.571	0.155	50515
6/21/2026	Sunday				
6/22/2026	Monday	376.571	376.725	0.154	50189
6/23/2026	Tuesday	376.725	376.880	0.155	50514
6/24/2026	Wednesday	376.880	377.112	0.232	75609
Monthly Total				3.323	1,082,965.70

WORKER-SAFETY-03

1. MONTHLY SAFETY INSPECTION

Monthly Safety Compliance Inspection Form

Project: Harlan Switch Station Location: 21055 S. Derrick Ave, Cantua Creek, CA

Month/Year: June / 2026 Inspection Date: 6/25/26

Inspected By (Construction Safety Supervisor): Isaac Sandoval

Title: Assistant Project Manager Signature: Isaac Sandoval

1. Occupational Safety & Health Program

Criteria	Compliance (✓ / ✗ / N.A.)	Comments / Corrective Actions
Safety policies and procedures are current, posted, and communicated to all personnel		
Daily tailgate and toolbox safety meetings documented		
Job Hazard Analyses (JHAs) updated for current work activities		
Emergency contact list and response plan posted on site		
First aid kits, fire extinguishers, and eyewash stations inspected and accessible		

2. Regulatory Compliance (Cal/OSHA & Federal)

Criteria	Compliance (✓ / ✗ / N.A.)	Comments / Corrective Actions
Project safety program complies with Cal/OSHA		

2. MONTHLY SAFETY INSPECTION

Title 8, Subchapter 4 (Construction Safety Orders)		
Electrical safety protocols per 29 CFR 1926 Subpart K and NFPA 70E		
Battery Energy Storage System (BESS) measures per manufacturer and Cal/OSHA GISO §5189		
PPE issued, used, and maintained per 8 CCR §3380-§3385		
Confined space, lockout/tagout, and hot work procedures in effect		

3. Training & Worker Safety

Criteria	Compliance (✓ / ✗ / N.A.)	Comments / Corrective Actions
All workers and supervisors completed site-specific safety orientation		
Cal/OSHA required training completed (Fall Protection, Heat Illness, Valley Fever, Silica)		
Documentation of safety training maintained onsite		
New employees/subcontractors briefed on hazards before starting work		

3. MONTHLY SAFETY INSPECTION

4. Incident & Emergency Reporting

Criteria	Compliance (✓ / ✗ / N.A.)	Comments / Corrective Actions
Accident and incident investigations completed within 24 hours of event	✓	
Emergency response reports submitted to CPM as required	✓	
Near-miss events documented and reviewed for corrective measures	✓	
Emergency drills conducted and documented (fire, medical, evacuation)	✓	

5. Construction Fire Protection & Prevention Program

Criteria	Compliance (✓ / ✗ / N.A.)	Comments / Corrective Actions
Applicable standards and publications identified	✓	
Fire map includes layout, ingress/egress, drainage, grading	✓	
Fire map identifies potential ignition sources during construction phases	✓	
Fire map shows evacuation areas/muster points	✓	
Construction fire protection systems identified (water	✓	

4. MONTHLY SAFETY INSPECTION

systems, gaseous systems, extinguishers)		
Construction detection and alarm systems described		
List of all major fire hazards completed		
Procedures for controlling flammable/combustible waste accumulation implemented		
Maintenance procedures for heat-producing equipment safeguards implemented		
Project personnel responsible for fuel-source hazard control identified		

6. Summary and Corrective Actions

Overall Compliance Status (circle one):

Satisfactory

Minor Corrections Needed

Non-Compliant

Summary of Findings: Site is well kept and is following all safety regulations

Corrective Actions / Responsible Party / Completion Date: _____

Supervisor Certification

I certify that this monthly safety compliance inspection was performed in accordance with Cal/OSHA and federal safety regulations, and that all noted deficiencies will be corrected promptly.

Signature: Isaac Sandoval Date: 6/25/26

WORKER-SAFETY-03

1. TRAINING SIGN-IN SHEETS

WORKER-SAFETY-03

1. NOISE-02: NOISE EXPOSURE LOG & MONITORING

The work performed onsite thus far has not required personnel to work for extended periods of time outside of equipment cabs and/or nearby running equipment with a standing decibel average of 85 dBA or greater.

2. WORKER-SAFETY-11: RESPIRATOR TRAINING & MONITORING

Conditions onsite have yet to reach thresholds maintained in the Harlan Switching Station Valley Fever Prevention Plan which would require mandatory respirator training, monitoring, and buddy system implementation.

4. WORKER-SAFETY-11: VALLEY FEVER SYMPTOMS AND/OR CASE REPORTING

Dashiell and its subcontractors have not encountered any suspected Valley Fever or personnel exhibiting conducive symptoms.

WORKER-SAFETY-03

5. SWITCH-HAZ-02: MONTHLY FIRE EXTINGUISHER INSPECTION

Fire Extinguisher Monthly Visual Inspection Log

Regulatory References:

- OSHA 29 CFR 1910.157(e)(2): Portable fire extinguishers must be visually inspected monthly by the employer.
- California Code of Regulations, Title 8, §6151(e)(2): Mirrors federal OSHA; requires monthly visual inspections and annual maintenance by a certified technician.
- California Fire Code (CFC) §906.2: Portable extinguishers must be maintained, inspected, and tested per NFPA 10.

Project / Facility Information

Project / Facility Name	Harland Switch Station
Location / Area	Fuel Tanks
Extinguisher ID / Tag No.	9392
Type / Rating (e.g., ABC, CO ₂ , K)	ABC
Capacity (lb)	20lb
Mounting Location / Identifier	Flagged Post

Inspection Checklist (Monthly Visual Inspection)

Inspector shall initial or check "OK" or "Deficiency" for each month.

Month	Pressuree Gauge in Green	Pin & Seal Intact	No Visible Damage / Corrosion	Label Legible	Accessible & Unobstructed	Inspection Initials / Signature	Deficiency Noted (Y/N) / Comments
January	OK	OK	OK	OK	OK	OK	OK
February	OK	OK	OK	OK	OK	OK	OK
March	OK	OK	OK	OK	OK	OK	OK
April	OK	OK	OK	OK	OK	OK	OK
May	OK	OK	OK	OK	OK	OK	OK
June	OK	OK	OK	OK	OK	OK	OK
July							

WORKER-SAFETY-03

August							
September							
October							
November	OK	OK	OK	OK	OK	OK	OK
December	OK	OK	OK	OK	OK	OK	OK

Instructions

1. Inspect each extinguisher monthly for:
 - Correct pressure (needle in green zone)
 - Secure tamper seal and pin
 - No physical damage, corrosion, leakage, or clogged nozzle
 - Clear labeling and legible instructions
 - Unobstructed access and visible signage
2. Initial and date upon completion.
3. Note any deficiencies and immediately report to site safety officer or maintenance lead.
4. Maintain this log on site for at least one year per OSHA and CFC §107.6 recordkeeping requirements.

WORKER-SAFETY-03

Fire Extinguisher Monthly Visual Inspection Log

Regulatory References:

- OSHA 29 CFR 1910.157(e)(2): Portable fire extinguishers must be visually inspected monthly by the employer.
- California Code of Regulations, Title 8, §6151(e)(2): Mirrors federal OSHA; requires monthly visual inspections and annual maintenance by a certified technician.
- California Fire Code (CFC) §906.2: Portable extinguishers must be maintained, inspected, and tested per NFPA 10.

Project / Facility Information

Project / Facility Name	Harland Switch Station
Location / Area	Truck Extinguishers
Extinguisher ID / Tag No.	32180
Type / Rating (e.g., ABC, CO ₂ , K)	ABC
Capacity (lb)	2.5 lb
Mounting Location / Identifier	Inside Company Truck

Inspection Checklist (Monthly Visual Inspection)

Inspector shall initial or check "OK" or "Deficiency" for each month.

Month	Pressuree Gauge in Green	Pin & Seal Intact	No Visible Damage / Corrosion	Label Legible	Accessible & Unobstructed	Inspection Initials / Signature	Deficiency Noted (Y/N) / Comments
January	OK	OK	OK	OK	OK	OK	OK
February	OK	OK	OK	OK	OK	OK	OK
March	OK	OK	OK	OK	OK	OK	OK
April	OK	OK	OK	OK	OK	OK	OK
May	OK	OK	OK	OK	OK	OK	OK
June	OK	OK	OK	OK	OK	OK	OK
July							

WORKER-SAFETY-03

August							
September							
October							
November	OK	OK	OK	OK	OK	OK	OK
December	OK	OK	OK	OK	OK	OK	OK

Instructions

- Inspect each extinguisher monthly for:
 - Correct pressure (needle in green zone)
 - Secure tamper seal and pin
 - No physical damage, corrosion, leakage, or clogged nozzle
 - Clear labeling and legible instructions
 - Unobstructed access and visible signage
- Initial and date upon completion.
- Note any deficiencies and immediately report to site safety officer or maintenance lead.
- Maintain this log on site for at least one year per OSHA and CFC §107.6 recordkeeping requirements.

WORKER-SAFETY-03

Fire Extinguisher Monthly Visual Inspection Log

Regulatory References:

- OSHA 29 CFR 1910.157(e)(2): Portable fire extinguishers must be visually inspected monthly by the employer.
- California Code of Regulations, Title 8, §6151(e)(2): Mirrors federal OSHA; requires monthly visual inspections and annual maintenance by a certified technician.
- California Fire Code (CFC) §906.2: Portable extinguishers must be maintained, inspected, and tested per NFPA 10.

Project / Facility Information

Project / Facility Name	Harland Switch Station
Location / Area	Job site Office
Extinguisher ID / Tag No.	70740418
Type / Rating (e.g., ABC, CO ₂ , K)	ABC
Capacity (lb)	2.5 lb
Mounting Location / Identifier	Inside office on the wall

Inspection Checklist (Monthly Visual Inspection)

Inspector shall initial or check "OK" or "Deficiency" for each month.

Month	Pressure Gauge in Green	Pin & Seal Intact	No Visible Damage / Corrosion	Label Legible	Accessible & Unobstructed	Inspection Initials / Signature	Deficiency Noted (Y/N) / Comments
January							
February	OK	OK	OK	OK	OK	OK	OK
March	OK	OK	OK	OK	OK	OK	OK
April	OK	OK	OK	OK	OK	OK	OK
May	OK	OK	OK	OK	OK	OK	OK
June	OK	OK	OK	OK	OK	OK	OK
July							

Appendix D

COM-5 COC Tracking Table

COM-5 Compliance Matrix

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Air Quality	AQ-01	The project owner shall submit the emergency engine specifications to the CPM at least 30 days prior to purchasing the engine for review and approval.	at least 30 days prior to purchasing the engine for review and approval	No Action Needed	N/A	N/A				
Air Quality	AQ-02	The project owner shall submit the emergency engine specifications to the CPM at least 30 days prior to purchasing the engine for review and approval.	at least 30 days prior to purchasing the engine for review and approval	No Action Needed	N/A	N/A				
Air Quality	AQ-03	The project owner shall submit the emergency engine specifications to the CPM at least 30 days prior to purchasing the engine for review and approval.	at least 30 days prior to purchasing the engine for review and approval	No Action Needed	N/A	N/A				
Air Quality	AQ-04	The project owner shall submit the emergency engine specifications to the CPM at least 30 days prior to purchasing the engine for review and approval.	at least 30 days prior to purchasing the engine for review and approval	No Action Needed	N/A	N/A				
Air Quality	AQ-05	The right of entry described in the California Health and Safety Code (CH&SC) Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-06	The right of entry described in CH&SC Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-07	The right of entry described in CH&SC Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-08	A summary of significant operation and maintenance events and monitoring records required shall be included in the quarterly operation reports .	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-09	The right of entry described in CH&SC Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-10	The right of entry described in CH&SC Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-11	The right of entry described in CH&SC Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-12	The right of entry described in CH&SC Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-13	The project owner shall submit a quarterly compliance report to the CPM. In this report, the project owner shall indicate how this condition is being implemented. A summary of significant operation and maintenance events and monitoring records required shall be included in the quarterly operation reports.	Quarterly	No Action Needed	N/A	N/A				
Air Quality	AQ-14	A summary of significant operation and maintenance events and monitoring records required shall be included in the quarterly operation reports.	Quarterly	No Action Needed	N/A	N/A				
Air Quality	AQ-15	A summary of significant operation and maintenance events and monitoring records required shall be included in the quarterly operation reports.	Quarterly	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Air Quality	AQ-16	A negative declaration stating the engine was not used to produce power for the electrical distribution system, as part of a voluntary utility demand reduction program, or for an interruptible power contract operation shall be included in the quarterly operation reports.	Quarterly	No Action Needed	N/A	N/A				
Air Quality	AQ-17	A summary of significant operation and maintenance events and monitoring records required shall be included in the quarterly operation reports.	Quarterly	No Action Needed	N/A	N/A				
Air Quality	AQ-18	The right of entry described in CH&SC Section 41510, Division 26, shall apply at all times. The project owner shall make the site available for inspection by representatives of the District, ARB, U.S. EPA and the Energy Commission.	N/A	No Action Needed	N/A	N/A				
Air Quality	AQ-SC-01	At least 30 days prior to the start of ground disturbance, the project owner shall submit to the CPM for approval, the name, resume, qualifications, and contact information for the on-site AQCMM and all AQCMM Delegates.	At least 30 days prior to the start of ground disturbance	Submitted - CEC Review	N/A	9/24/2025 10/13/2025 2/18/2026 3/17/2026			BAAH - 10/22/2025 Darden - 11/18/2025	
Air Quality	AQ-SC-02	At least 30 days prior to the start of any ground disturbance, the project owner shall submit the AQCMP to the CPM for approval. The AQCMP shall include effectiveness and environmental data for the proposed soil stabilizer. The CPM will notify the project owner of any necessary modifications to the plan within 15 days from the date of receipt.	At least 30 days prior to the start of any ground disturbance	CEC Approved	N/A	9/26/2025			BAAH & Darden - 10/22/2025	
Air Quality	AQ-SC-03	The AQCMM shall provide the CPM a Monthly Compliance Report to include the following to demonstrate control of fugitive dust emissions: A. A summary of all actions taken to maintain compliance with this condition; B. Copies of any complaints filed with the District in relation to project construction; and C. Any other documentation deemed necessary by the CPM and AQCMM to verify compliance with this condition. Such information may be provided via electronic format or disk at the project owner’s discretion.	Monthly	Ongoing - EPC	N/A	N/A				
Air Quality	AQ-SC-04	The AQCMM shall provide the CPM a Monthly Compliance Report to include: A. A summary of all actions taken to maintain compliance with this condition; B. Copies of any complaints filed with the District in relation to project construction; and C. Any other documentation deemed necessary by the CPM and AQCMM to verify compliance with this condition. Such information may be provided via electronic format or disk at the project owner’s discretion.	Monthly	Ongoing - EPC	N/A	N/A				
Air Quality	AQ-SC-05	The AQCMM shall include in the Monthly Compliance Report the following to demonstrate control of diesel construction-related emissions: A. A summary of all actions taken to control diesel construction related emissions; B. A list of all heavy equipment used on site during that month, including the owner of that equipment and a letter from each owner indicating that equipment has been properly maintained; and C. Any other documentation deemed necessary by the CPM, and the AQCMM to verify compliance with this condition. Such information may be provided via electronic format or disk at the project owner’s discretion.	Monthly	Ongoing - EPC	N/A	11/20/2025				
Air Quality	AQ-SC-06	At least 30 days prior to ground disturbance, the project owner shall submit to the CPM for approval the VERA between the project owner and SJVAPCD.	At least 30 days prior to ground disturbance	CEC Approved	N/A	10/20/2025	SJVAPCD		BAAH & Darden - 10/22/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-01	The project owner shall submit the specified information at least 75 days prior to the start of site mobilization or construction-related ground disturbance activities. No pre-construction site mobilization or construction related activities shall commence until a Designated Biologist has been approved by the CPM. If a Designated Biologist needs to be replaced, the specified information regarding the proposed replacement must be submitted to the CPM at least ten working days prior to the termination or release of the preceding Designated Biologist. In an emergency, the project owner shall immediately notify the CPM to discuss the qualifications and approval of a short-term replacement while a permanent Designated Biologist is proposed to the CPM for consideration.	At least ten working days prior to the termination or release of the preceding Designated Biologist	No Action Needed	N/A	N/A				
Biological Resources	BIO-01	The project owner shall submit the specified information at least 75 days prior to the start of site mobilization or construction-related ground disturbance activities. No pre-construction site mobilization or construction related activities shall commence until a Designated Biologist has been approved by the CPM. If a Designated Biologist needs to be replaced, the specified information regarding the proposed replacement must be submitted to the CPM at least ten working days prior to the termination or release of the preceding Designated Biologist. In an emergency, the project owner shall immediately notify the CPM to discuss the qualifications and approval of a short-term replacement while a permanent Designated Biologist is proposed to the CPM for consideration.	at least 75 days prior to the start of site mobilization or construction-related ground disturbance activities.	CEC Approved	N/A	7/18/2025 7/25/2025 8/18/2025 9/15/2025 9/19/2025 4/17/2026 4/23/2026			9/3/2025 9/16/2025 10/22/2025 4/28/2026 - partial	
Biological Resources	BIO-02	The Designated Biologist shall submit in the MCRs to the CPM copies of all written reports and summaries that document construction activities that have the potential to affect biological resources. The Designated Biologist’s written records will be made available for the CPM’s inspection on request at any time during normal business hours. During project operation, the Designated Biologist(s) shall submit record summaries in the ACR unless their duties cease, as approved by the CPM.	Annually	Not Started - Rincon	N/A	N/A				
Biological Resources	BIO-02	The Designated Biologist shall submit in the MCRs to the CPM copies of all written reports and summaries that document construction activities that have the potential to affect biological resources. The Designated Biologist’s written records will be made available for the CPM’s inspection on request at any time during normal business hours. During project operation, the Designated Biologist(s) shall submit record summaries in the ACR unless their duties cease, as approved by the CPM.	Monthly	Ongoing - Rincon	N/A	N/A				
Biological Resources	BIO-03	The project owner shall submit the specified information to the CPM for approval for review and comment at least 45 days prior to the start of any project-related site disturbance activities. Within 10 days of completion of training, the Designated Biologist shall submit a written statement to CPM confirming that individual Biological Monitor(s) have been trained including the date when training was completed. If additional biological monitors are needed during construction or for species specific surveys, the specified information shall be submitted to the CPM for approval at least 10 days prior to their first day of monitoring activities.	For approval at least 10 days prior to their first day of monitoring activities	No Action Needed	N/A	N/A				
Biological Resources	BIO-03	The project owner shall submit the specified information to the CPM for approval for review and comment at least 45 days prior to the start of any project-related site disturbance activities. Within 10 days of completion of training, the Designated Biologist shall submit a written statement to CPM confirming that individual Biological Monitor(s) have been trained including the date when training was completed. If additional biological monitors are needed during construction or for species specific surveys, the specified information shall be submitted to the CPM for approval at least 10 days prior to their first day of monitoring activities.	at least 45 days prior to the start of any project-related site disturbance activities	CEC Approved	N/A	7/18/2025 7/25/2025 9/19/2025 4/17/2026			10/22/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-03	The project owner shall submit the specified information to the CPM for approval for review and comment at least 45 days prior to the start of any project-related site disturbance activities. Within 10 days of completion of training, the Designated Biologist shall submit a written statement to CPM confirming that individual Biological Monitor(s) have been trained including the date when training was completed. If additional biological monitors are needed during construction or for species specific surveys, the specified information shall be submitted to the CPM for approval at least 10 days prior to their first day of monitoring activities.	Within 10 days of completion of training	Completed	N/A	9/19/2025			N/A	
Biological Resources	BIO-04	The project owner shall ensure that the Designated Biologist or Biological Monitor notifies the CPM immediately (and no later than the morning following the incident, or Monday morning in the case of a weekend) of any non-compliance with biological resources conditions of certification or a halt of any site mobilization, ground disturbance, grading, construction, and operation activities with the potential to adversely impact biological resources. The project owner shall notify the CPM of the circumstances and actions being taken to resolve the problem within one (1) working day of initiating the corrective action.	Immediately (and no later than the morning following the incident, or Monday morning in the case of a weekend)	No Action Needed	N/A	N/A				
Biological Resources	BIO-04	The project owner shall ensure that the Designated Biologist or Biological Monitor notifies the CPM immediately (and no later than the morning following the incident, or Monday morning in the case of a weekend) of any non-compliance with biological resources conditions of certification or a halt of any site mobilization, ground disturbance, grading, construction, and operation activities with the potential to adversely impact biological resources. The project owner shall notify the CPM of the circumstances and actions being taken to resolve the problem within one (1) working day of initiating the corrective action.	within one (1) working day of initiating the corrective action	No Action Needed	N/A	N/A				
Biological Resources	BIO-05	At least 45 days prior to start of site mobilization the project owner shall provide to the CPM for review and approval, the draft WEAP/WEAP Light and all supporting written materials and electronic media prepared or reviewed by the Designated Biologist and a resume of the person(s) administering the program. The CPM must approve the WEAP/WEAP Light materials prior to their use. At least 10 days prior to site and related facilities mobilization, the project owner shall provide the CPM a copy of the CPM-approved final WEAP/WEAP Light. The project owner shall provide in the Monthly Compliance Report the number of persons who have completed the training in the prior month and a running total of all persons who have completed the training to date. At least 10 days prior to site mobilization the project owner shall submit the approved final WEAP/WEAP Light and implement the training for all workers. The WEAP/WEAP Light shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel working at the project site. Upon completion of the orientation, employees shall sign a form stating that they attended the program and understand all protection measures. These forms shall be maintained by the project owner and shall be made available to the CPM upon request. Workers shall receive and be required to visibly display a hardhat sticker or certificate that they have completed the training. Training acknowledgement forms signed during construction shall be kept on file by the project owner for at least 6 months after the start of commercial operation. Throughout the life of the project, the WEAP/WEAP Light shall be repeated annually for permanent employees, and shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel potentially working within the project area. During project operation, signed statements for operational personnel shall be kept on file for 6 months following the termination of an individual's employment.	At least 45 days prior to start of site mobilization	CEC Approved	N/A	8/25/2025 9/15/2025		10/22/2025		

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-05	At least 45 days prior to start of site mobilization the project owner shall provide to the CPM for review and approval, the draft WEAP/WEAP Light and all supporting written materials and electronic media prepared or reviewed by the Designated Biologist and a resume of the person(s) administering the program. The CPM must approve the WEAP/WEAP Light materials prior to their use. At least 10 days prior to site and related facilities mobilization, the project owner shall provide the CPM a copy of the CPM-approved final WEAP/WEAP Light. The project owner shall provide in the Monthly Compliance Report the number of persons who have completed the training in the prior month and a running total of all persons who have completed the training to date. At least 10 days prior to site mobilization the project owner shall submit the approved final WEAP/WEAP Light and implement the training for all workers. The WEAP/WEAP Light shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel working at the project site. Upon completion of the orientation, employees shall sign a form stating that they attended the program and understand all protection measures. These forms shall be maintained by the project owner and shall be made available to the CPM upon request. Workers shall receive and be required to visibly display a hardhat sticker or certificate that they have completed the training. Training acknowledgement forms signed during construction shall be kept on file by the project owner for at least 6 months after the start of commercial operation. Throughout the life of the project, the WEAP/WEAP Light shall be repeated annually for permanent employees, and shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel potentially working within the project area. During project operation, signed statements for operational personnel shall be kept on file for 6 months following the termination of an individual's employment.	At least 45 days prior to start of site mobilization	CEC Approved	N/A	7/18/2025 7/25/2025			10/22/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-05	At least 45 days prior to start of site mobilization the project owner shall provide to the CPM for review and approval, the draft WEAP/WEAP Light and all supporting written materials and electronic media prepared or reviewed by the Designated Biologist and a resume of the person(s) administering the program. The CPM must approve the WEAP/WEAP Light materials prior to their use. At least 10 days prior to site and related facilities mobilization, the project owner shall provide the CPM a copy of the CPM-approved final WEAP/WEAP Light. The project owner shall provide in the Monthly Compliance Report the number of persons who have completed the training in the prior month and a running total of all persons who have completed the training to date. At least 10 days prior to site mobilization the project owner shall submit the approved final WEAP/WEAP Light and implement the training for all workers. The WEAP/WEAP Light shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel working at the project site. Upon completion of the orientation, employees shall sign a form stating that they attended the program and understand all protection measures. These forms shall be maintained by the project owner and shall be made available to the CPM upon request. Workers shall receive and be required to visibly display a hardhat sticker or certificate that they have completed the training. Training acknowledgement forms signed during construction shall be kept on file by the project owner for at least 6 months after the start of commercial operation. Throughout the life of the project, the WEAP/WEAP Light shall be repeated annually for permanent employees, and shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel potentially working within the project area. During project operation, signed statements for operational personnel shall be kept on file for 6 months following the termination of an individual's employment.	At least 10 days prior to site and related facilities mobilization	CEC Approved	N/A	9/15/2025			10/22/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-05	At least 45 days prior to start of site mobilization the project owner shall provide to the CPM for review and approval, the draft WEAP/WEAP Light and all supporting written materials and electronic media prepared or reviewed by the Designated Biologist and a resume of the person(s) administering the program. The CPM must approve the WEAP/WEAP Light materials prior to their use. At least 10 days prior to site and related facilities mobilization, the project owner shall provide the CPM a copy of the CPM-approved final WEAP/WEAP Light. The project owner shall provide in the Monthly Compliance Report the number of persons who have completed the training in the prior month and a running total of all persons who have completed the training to date. At least 10 days prior to site mobilization the project owner shall submit the approved final WEAP/WEAP Light and implement the training for all workers. The WEAP/WEAP Light shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel working at the project site. Upon completion of the orientation, employees shall sign a form stating that they attended the program and understand all protection measures. These forms shall be maintained by the project owner and shall be made available to the CPM upon request. Workers shall receive and be required to visibly display a hardhat sticker or certificate that they have completed the training. Training acknowledgement forms signed during construction shall be kept on file by the project owner for at least 6 months after the start of commercial operation. Throughout the life of the project, the WEAP/Weap Light shall be repeated annually for permanent employees, and shall be routinely administered within 1 week of arrival to any new construction personnel, foremen, contractors, subcontractors, and other personnel potentially working within the project area. During project operation, signed statements for operational personnel shall be kept on file for 6 months following the termination of an individual's employment.	Monthly	Ongoing - Rincon	N/A	N/A				
Biological Resources	BIO-06	The project owner shall submit the BRMIMP to the CPM for review and approval at least 60 days prior to start of any site mobilization. The project owner shall provide final BRMIMP to the CPM at least 10 days prior to start of any site mobilization. If there are any permits that have not yet been received when the BRMIMP is first submitted, copies of these permits shall be submitted to the CPM within 5 days of their receipt, and a revised BRMIMP shall be submitted to the CPM for review within 10 days of receipt of permits by the project owner. Any changes to the approved BRMIMP shall be submitted to the CPM at least 10 days prior to implementation and must be approved by the CPM prior to implementation. Implementation of BRMIMP measures shall be reported in the MCRs (e.g., survey results, construction activities that were monitored, non-compliance incidences and resolution, species observed, etc.). Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction closure report identifying which items of the BRMIMP have been completed, a summary of all CPM-approved modifications to mitigation measures made during the project's preconstruction site mobilization and construction, and which items are still outstanding.	Within 30 days after completion of project construction	Not Started - Rincon	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-06	The project owner shall submit the BRMIMP to the CPM for review and approval at least 60 days prior to start of any site mobilization. The project owner shall provide final BRMIMP to the CPM at least 10 days prior to start of any site mobilization. If there are any permits that have not yet been received when the BRMIMP is first submitted, copies of these permits shall be submitted to the CPM within 5 days of their receipt, and a revised BRMIMP shall be submitted to the CPM for review within 10 days of receipt of permits by the project owner. Any changes to the approved BRMIMP shall be submitted to the CPM at least 10 days prior to implementation and must be approved by the CPM prior to implementation. Implementation of BRMIMP measures shall be reported in the MCRs (e.g., survey results, construction activities that were monitored, non-compliance incidences and resolution, species observed, etc.). Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction closure report identifying which items of the BRMIMP have been completed, a summary of all CPM-approved modifications to mitigation measures made during the project's preconstruction site mobilization and construction, and which items are still outstanding.	At least 10 days prior to implementation and must be approved by the CPM prior to implementation.	No Action Needed	N/A	N/A				
Biological Resources	BIO-06	The project owner shall submit the BRMIMP to the CPM for review and approval at least 60 days prior to start of any site mobilization. The project owner shall provide final BRMIMP to the CPM at least 10 days prior to start of any site mobilization. If there are any permits that have not yet been received when the BRMIMP is first submitted, copies of these permits shall be submitted to the CPM within 5 days of their receipt, and a revised BRMIMP shall be submitted to the CPM for review within 10 days of receipt of permits by the project owner. Any changes to the approved BRMIMP shall be submitted to the CPM at least 10 days prior to implementation and must be approved by the CPM prior to implementation. Implementation of BRMIMP measures shall be reported in the MCRs (e.g., survey results, construction activities that were monitored, non-compliance incidences and resolution, species observed, etc.). Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction closure report identifying which items of the BRMIMP have been completed, a summary of all CPM-approved modifications to mitigation measures made during the project's preconstruction site mobilization and construction, and which items are still outstanding.	submitted to the CPM within 5 days of receipt	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-06	The project owner shall submit the BRMIMP to the CPM for review and approval at least 60 days prior to start of any site mobilization. The project owner shall provide final BRMIMP to the CPM at least 10 days prior to start of any site mobilization. If there are any permits that have not yet been received when the BRMIMP is first submitted, copies of these permits shall be submitted to the CPM within 5 days of their receipt, and a revised BRMIMP shall be submitted to the CPM for review within 10 days of receipt of permits by the project owner. Any changes to the approved BRMIMP shall be submitted to the CPM at least 10 days prior to implementation and must be approved by the CPM prior to implementation. Implementation of BRMIMP measures shall be reported in the MCRs (e.g., survey results, construction activities that were monitored, non-compliance incidences and resolution, species observed, etc.). Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction closure report identifying which items of the BRMIMP have been completed, a summary of all CPM-approved modifications to mitigation measures made during the project's preconstruction site mobilization and construction, and which items are still outstanding.	within 10 days of receipt of permits by the project owner	No Action Needed	N/A	N/A				
Biological Resources	BIO-06	The project owner shall submit the BRMIMP to the CPM for review and approval at least 60 days prior to start of any site mobilization. The project owner shall provide final BRMIMP to the CPM at least 10 days prior to start of any site mobilization. If there are any permits that have not yet been received when the BRMIMP is first submitted, copies of these permits shall be submitted to the CPM within 5 days of their receipt, and a revised BRMIMP shall be submitted to the CPM for review within 10 days of receipt of permits by the project owner. Any changes to the approved BRMIMP shall be submitted to the CPM at least 10 days prior to implementation and must be approved by the CPM prior to implementation. Implementation of BRMIMP measures shall be reported in the MCRs (e.g., survey results, construction activities that were monitored, non-compliance incidences and resolution, species observed, etc.). Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction closure report identifying which items of the BRMIMP have been completed, a summary of all CPM-approved modifications to mitigation measures made during the project's preconstruction site mobilization and construction, and which items are still outstanding.	at least 60 days prior to start of any site mobilization	CEC Approved	N/A	8/25/2025 10/14/2025 10/22/2025			10/24/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-06	The project owner shall submit the BRMIMP to the CPM for review and approval at least 60 days prior to start of any site mobilization. The project owner shall provide final BRMIMP to the CPM at least 10 days prior to start of any site mobilization. If there are any permits that have not yet been received when the BRMIMP is first submitted, copies of these permits shall be submitted to the CPM within 5 days of their receipt, and a revised BRMIMP shall be submitted to the CPM for review within 10 days of receipt of permits by the project owner. Any changes to the approved BRMIMP shall be submitted to the CPM at least 10 days prior to implementation and must be approved by the CPM prior to implementation. Implementation of BRMIMP measures shall be reported in the MCRs (e.g., survey results, construction activities that were monitored, non-compliance incidences and resolution, species observed, etc.). Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction closure report identifying which items of the BRMIMP have been completed, a summary of all CPM-approved modifications to mitigation measures made during the project's preconstruction site mobilization and construction, and which items are still outstanding.	at least 10 days prior to start of any site mobilization	CEC Approved	N/A	10/22/2025			10/24/2025	
Biological Resources	BIO-06	The project owner shall submit the BRMIMP to the CPM for review and approval at least 60 days prior to start of any site mobilization. The project owner shall provide final BRMIMP to the CPM at least 10 days prior to start of any site mobilization. If there are any permits that have not yet been received when the BRMIMP is first submitted, copies of these permits shall be submitted to the CPM within 5 days of their receipt, and a revised BRMIMP shall be submitted to the CPM for review within 10 days of receipt of permits by the project owner. Any changes to the approved BRMIMP shall be submitted to the CPM at least 10 days prior to implementation and must be approved by the CPM prior to implementation. Implementation of BRMIMP measures shall be reported in the MCRs (e.g., survey results, construction activities that were monitored, non-compliance incidences and resolution, species observed, etc.). Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction closure report identifying which items of the BRMIMP have been completed, a summary of all CPM-approved modifications to mitigation measures made during the project's preconstruction site mobilization and construction, and which items are still outstanding.	monthly	Ongoing - Rincon	N/A	N/A				
Biological Resources	BIO-07	All general impact avoidance and minimization measures shall be included in the BRMIMP and implemented. Implementation of the measures shall be reported by the Designated Biologist in the MCRs. Within 60 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Within 60 days after completion of project construction, the project owner shall provide to the CPM	Not Started - Rincon	N/A	N/A				
Biological Resources	BIO-07	All general impact avoidance and minimization measures shall be included in the BRMIMP and implemented. Implementation of the measures shall be reported by the Designated Biologist in the MCRs. Within 60 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly	Ongoing - Rincon	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-08	The project owner shall submit the NBMP to the CPM at least 30 days prior to start of site mobilization activities. The project owner shall submit preconstruction survey reports to the CPM no more than 30 days after each survey effort has been completed. The project owner shall submit reports in the MCR during nesting season, and an annual NBMP report to the CPM within 60 days of the end of nesting season. The project owner shall provide a letter report detailing the outcome of the care of any special-status injured birds or nest failures to the CPM within 14 days of the incident. If nesting tricolored blackbird are detected, the project owner shall submit the Nesting Tricolored Blackbird Monitoring Report bi-monthly to the CPM.	N/A	No Action Needed	N/A	N/A				
Biological Resources	BIO-08	The project owner shall submit the NBMP to the CPM at least 30 days prior to start of site mobilization activities. The project owner shall submit preconstruction survey reports to the CPM no more than 30 days after each survey effort has been completed. The project owner shall submit reports in the MCR during nesting season, and an annual NBMP report to the CPM within 60 days of the end of nesting season. The project owner shall provide a letter report detailing the outcome of the care of any special-status injured birds or nest failures to the CPM within 14 days of the incident. If nesting tricolored blackbird are detected, the project owner shall submit the Nesting Tricolored Blackbird Monitoring Report bi-monthly to the CPM.	Bi-monthly if nesting tricolored blackbirds are observed	No Action Needed	N/A	N/A				
Biological Resources	BIO-08	The project owner shall submit the NBMP to the CPM at least 30 days prior to start of site mobilization activities. The project owner shall submit preconstruction survey reports to the CPM no more than 30 days after each survey effort has been completed. The project owner shall submit reports in the MCR during nesting season, and an annual NBMP report to the CPM within 60 days of the end of nesting season. The project owner shall provide a letter report detailing the outcome of the care of any special-status injured birds or nest failures to the CPM within 14 days of the incident. If nesting tricolored blackbird are detected, the project owner shall submit the Nesting Tricolored Blackbird Monitoring Report bi-monthly to the CPM.	Within 30 days after each survey effort has been completed	No Action Needed	N/A	N/A				
Biological Resources	BIO-08	The project owner shall submit the NBMP to the CPM at least 30 days prior to start of site mobilization activities. The project owner shall submit preconstruction survey reports to the CPM no more than 30 days after each survey effort has been completed. The project owner shall submit reports in the MCR during nesting season, and an annual NBMP report to the CPM within 60 days of the end of nesting season. The project owner shall provide a letter report detailing the outcome of the care of any special-status injured birds or nest failures to the CPM within 14 days of the incident. If nesting tricolored blackbird are detected, the project owner shall submit the Nesting Tricolored Blackbird Monitoring Report bi-monthly to the CPM.	at least 30 days prior to start of site mobilization activities.	CEC Approved	N/A	12/15/2025 1/22/2026			1/23/2026	
Biological Resources	BIO-08	The project owner shall submit the NBMP to the CPM at least 30 days prior to start of site mobilization activities. The project owner shall submit preconstruction survey reports to the CPM no more than 30 days after each survey effort has been completed. The project owner shall submit reports in the MCR during nesting season, and an annual NBMP report to the CPM within 60 days of the end of nesting season. The project owner shall provide a letter report detailing the outcome of the care of any special-status injured birds or nest failures to the CPM within 14 days of the incident. If nesting tricolored blackbird are detected, the project owner shall submit the Nesting Tricolored Blackbird Monitoring Report bi-monthly to the CPM.	Within 60 days of the end of nesting season	Ongoing - Rincon	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-09	No fewer than 60 days prior to the start of pre-construction site mobilization the project owner shall submit to the CPM, for review and approval, a draft Swainson’s Hawk Conservation Strategy and a draft Foraging Habitat Revegetation and Management Plan to be included the Swainson’s Hawk Conservation Strategy and Foraging Habitat Revegetation and Management Plan (Plan). The Plan shall be finalized prior to the start of ground disturbance. The project owner shall submit the annual monitoring reports to the CPM for review within 30 days after the end of each reporting period.	N/A	Ongoing - Rincon	N/A	N/A				
Biological Resources	BIO-09	No fewer than 60 days prior to the start of pre-construction site mobilization the project owner shall submit to the CPM, for review and approval, a draft Swainson’s Hawk Conservation Strategy and a draft Foraging Habitat Revegetation and Management Plan to be included the Swainson’s Hawk Conservation Strategy and Foraging Habitat Revegetation and Management Plan (Plan). The Plan shall be finalized prior to the start of ground disturbance. The project owner shall submit the annual monitoring reports to the CPM for review within 30 days after the end of each reporting period.	At least 60 days prior to the start of pre-construction site mobilization the project	CEC Approved	N/A	10/23/2025 11/25/2025 1/6/2026 1/20/2026 1/21/2026 1/29/2026 2/17/2026	WWD	3/23/2027	3/16/2026	
Biological Resources	BIO-10	The project owner shall provide the preconstruction survey results to the CPM in a written report at least five (5) days prior to beginning preconstruction site mobilization. A Swainson’s Hawk Nest Survey Report shall be submitted to the CPM on an annual basis. The Designated Biologist shall prepare a Swainson’s hawk Nest Abandonment Contingency Plan and submit it to the CPM for written approval at least 45 days prior to the start of preconstruction site mobilization.	5 days prior to preconstruction mobilization	Not Started - Rincon	N/A	N/A				
Biological Resources	BIO-10	The project owner shall provide the preconstruction survey results to the CPM in a written report at least five (5) days prior to beginning preconstruction site mobilization. A Swainson’s Hawk Nest Survey Report shall be submitted to the CPM on an annual basis. The Designated Biologist shall prepare a Swainson’s hawk Nest Abandonment Contingency Plan and submit it to the CPM for written approval at least 45 days prior to the start of preconstruction site mobilization.	At least 5 days prior to the start of preconstruction site mobilization.	No Action Needed	N/A	N/A				
Biological Resources	BIO-10	The project owner shall provide the preconstruction survey results to the CPM in a written report at least five (5) days prior to beginning preconstruction site mobilization. A Swainson’s Hawk Nest Survey Report shall be submitted to the CPM on an annual basis. The Designated Biologist shall prepare a Swainson’s hawk Nest Abandonment Contingency Plan and submit it to the CPM for written approval at least 45 days prior to the start of preconstruction site mobilization.	45 days prior to mobilization	CEC Approved	N/A	10/22/2025 1/7/2026			1/15/2026	
Biological Resources	BIO-11	The project owner shall provide the CPM with approved Security at least 30 days prior to the start of pre-construction site mobilization activities. The project owner shall provide the recorded conservation easement within 24 months from the start of pre-construction site mobilization.	Within 24 months from the start of pre-construction site mobilization.	Not Started - IP	N/A	N/A				
Biological Resources	BIO-11	The project owner shall provide the CPM with approved Security at least 30 days prior to the start of pre-construction site mobilization activities. The project owner shall provide the recorded conservation easement within 24 months from the start of pre-construction site mobilization.	30 days prior to the start of pre-construction site mobilization activities.	Completed	N/A	10/17/2025 - BAAH 11/25/2025 - Darden			BAAH - 10/22/2025 Darden - N/A	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-12	The Designated Biologist shall provide to the CPM preconstruction survey results to the CPM within 10 days of the completion of the survey. If surveys detect burrowing owls within 500 feet of proposed construction activities, the Designated Biologist shall provide to the CPM documentation indicating that non-disturbance buffer fencing has been installed no less than 10 days prior to the start of any project-related site disturbance activities. The documentation shall include information as specified in Items 4 and 5, or as otherwise requested by the CPM. If pre-construction surveys detect burrowing owls or active burrowing owl burrows within the project disturbance area, the project owner shall provide to the CPM a Burrowing Owl Mortality Reduction Plan prior to the start of activities (the measures described in the plan shall be incorporated into the BRMIMP and implemented.) The plan shall be for review and comment by the CPM and shall be finalized no less than 30 days prior to commencing activities which may disturb or take burrowing owls. During operations, the project owner shall provide a written report with Burrow Map (Item 5) to the CPM 10 days prior to starting Burrowing Owl Exclusion Activities on the site or in each distinct work areas(s). The project owner shall submit a Burrowing Owl Artificial Burrow Replacement Plan to the CPM for review and comment at least 30 days prior to initiation of pre-construction site mobilization. The final approved Burrowing Owl Artificial Burrow Replacement Plan shall be submitted prior to activities which may disturb or take burrowing owls. At the conclusion of the construction period, the Project Owner shall submit a final Burrowing Owl Mitigation Implementation Report detailing location of all burrowing owl observed, take measures implemented, and their effectiveness. During operations, the project owner shall include in the Annual Compliance Report an accounting of all burrowing owl documented on site, including copies of the Designated Biologist or Biological Monitor’s field notes, any buffers zones erected, maps, additional avoidance and minimization measures implemented, and their perceived effectiveness.	At conclusion of construction	Not Started - Rincon	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-12	The Designated Biologist shall provide to the CPM preconstruction survey results to the CPM within 10 days of the completion of the survey. If surveys detect burrowing owls within 500 feet of proposed construction activities, the Designated Biologist shall provide to the CPM documentation indicating that non-disturbance buffer fencing has been installed no less than 10 days prior to the start of any project-related site disturbance activities. The documentation shall include information as specified in Items 4 and 5, or as otherwise requested by the CPM. If pre-construction surveys detect burrowing owls or active burrowing owl burrows within the project disturbance area, the project owner shall provide to the CPM a Burrowing Owl Mortality Reduction Plan prior to the start of activities (the measures described in the plan shall be incorporated into the BRMIMP and implemented.) The plan shall be for review and comment by the CPM and shall be finalized no less than 30 days prior to commencing activities which may disturb or take burrowing owls. During operations, the project owner shall provide a written report with Burrow Map (Item 5) to the CPM 10 days prior to starting Burrowing Owl Exclusion Activities on the site or in each distinct work areas(s). The project owner shall submit a Burrowing Owl Artificial Burrow Replacement Plan to the CPM for review and comment at least 30 days prior to initiation of pre-construction site mobilization. The final approved Burrowing Owl Artificial Burrow Replacement Plan shall be submitted prior to activities which may disturb or take burrowing owls. At the conclusion of the construction period, the Project Owner shall submit a final Burrowing Owl Mitigation Implementation Report detailing location of all burrowing owl observed, take measures implemented, and their effectiveness. During operations, the project owner shall include in the Annual Compliance Report an accounting of all burrowing owl documented on site, including copies of the Designated Biologist or Biological Monitor’s field notes, any buffers zones erected, maps, additional avoidance and minimization measures implemented, and their perceived effectiveness.	Annually with ACR	Not Started - Rincon	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-12	The Designated Biologist shall provide to the CPM preconstruction survey results to the CPM within 10 days of the completion of the survey. If surveys detect burrowing owls within 500 feet of proposed construction activities, the Designated Biologist shall provide to the CPM documentation indicating that non-disturbance buffer fencing has been installed no less than 10 days prior to the start of any project-related site disturbance activities. The documentation shall include information as specified in Items 4 and 5, or as otherwise requested by the CPM. If pre-construction surveys detect burrowing owls or active burrowing owl burrows within the project disturbance area, the project owner shall provide to the CPM a Burrowing Owl Mortality Reduction Plan prior to the start of activities (the measures described in the plan shall be incorporated into the BRMIMP and implemented.) The plan shall be for review and comment by the CPM and shall be finalized no less than 30 days prior to commencing activities which may disturb or take burrowing owls. During operations, the project owner shall provide a written report with Burrow Map (Item 5) to the CPM 10 days prior to starting Burrowing Owl Exclusion Activities on the site or in each distinct work areas(s). The project owner shall submit a Burrowing Owl Artificial Burrow Replacement Plan to the CPM for review and comment at least 30 days prior to initiation of pre-construction site mobilization. The final approved Burrowing Owl Artificial Burrow Replacement Plan shall be submitted prior to activities which may disturb or take burrowing owls. At the conclusion of the construction period, the Project Owner shall submit a final Burrowing Owl Mitigation Implementation Report detailing location of all burrowing owl observed, take measures implemented, and their effectiveness. During operations, the project owner shall include in the Annual Compliance Report an accounting of all burrowing owl documented on site, including copies of the Designated Biologist or Biological Monitor’s field notes, any buffers zones erected, maps, additional avoidance and minimization measures implemented, and their perceived effectiveness.	Submitted before project activities; finalized no less than 30 days prior to commencing pre-construction site mobilization.	CEC Approved	N/A	10/21/2025 11/20/2025 11/24/2025			11/24/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-12	The Designated Biologist shall provide to the CPM preconstruction survey results to the CPM within 10 days of the completion of the survey. If surveys detect burrowing owls within 500 feet of proposed construction activities, the Designated Biologist shall provide to the CPM documentation indicating that non-disturbance buffer fencing has been installed no less than 10 days prior to the start of any project-related site disturbance activities. The documentation shall include information as specified in Items 4 and 5, or as otherwise requested by the CPM. If pre-construction surveys detect burrowing owls or active burrowing owl burrows within the project disturbance area, the project owner shall provide to the CPM a Burrowing Owl Mortality Reduction Plan prior to the start of activities (the measures described in the plan shall be incorporated into the BRMIMP and implemented.) The plan shall be for review and comment by the CPM and shall be finalized no less than 30 days prior to commencing activities which may disturb or take burrowing owls. During operations, the project owner shall provide a written report with Burrow Map (Item 5) to the CPM 10 days prior to starting Burrowing Owl Exclusion Activities on the site or in each distinct work areas(s). The project owner shall submit a Burrowing Owl Artificial Burrow Replacement Plan to the CPM for review and comment at least 30 days prior to initiation of pre-construction site mobilization. The final approved Burrowing Owl Artificial Burrow Replacement Plan shall be submitted prior to activities which may disturb or take burrowing owls At the conclusion of the construction period, the Project Owner shall submit a final Burrowing Owl Mitigation Implementation Report detailing location of all burrowing owl observed, take measures implemented, and their effectiveness. During operations, the project owner shall include in the Annual Compliance Report an accounting of all burrowing owl documented on site, including copies of the Designated Biologist or Biological Monitor’s field notes, any buffers zones erected, maps, additional avoidance and minimization measures implemented, and their perceived effectiveness.	at least 30 days prior to initiation of pre-construction site mobilization.	CEC Approved	N/A	10/21/2025 11/24/2025			11/24/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-12	The Designated Biologist shall provide to the CPM preconstruction survey results to the CPM within 10 days of the completion of the survey. If surveys detect burrowing owls within 500 feet of proposed construction activities, the Designated Biologist shall provide to the CPM documentation indicating that non-disturbance buffer fencing has been installed no less than 10 days prior to the start of any project-related site disturbance activities. The documentation shall include information as specified in Items 4 and 5, or as otherwise requested by the CPM. If pre-construction surveys detect burrowing owls or active burrowing owl burrows within the project disturbance area, the project owner shall provide to the CPM a Burrowing Owl Mortality Reduction Plan prior to the start of activities (the measures described in the plan shall be incorporated into the BRMIMP and implemented.) The plan shall be for review and comment by the CPM and shall be finalized no less than 30 days prior to commencing activities which may disturb or take burrowing owls. During operations, the project owner shall provide a written report with Burrow Map (Item 5) to the CPM 10 days prior to starting Burrowing Owl Exclusion Activities on the site or in each distinct work area(s). The project owner shall submit a Burrowing Owl Artificial Burrow Replacement Plan to the CPM for review and comment at least 30 days prior to initiation of pre-construction site mobilization. The final approved Burrowing Owl Artificial Burrow Replacement Plan shall be submitted prior to activities which may disturb or take burrowing owls. At the conclusion of the construction period, the Project Owner shall submit a final Burrowing Owl Mitigation Implementation Report detailing location of all burrowing owl observed, take measures implemented, and their effectiveness. During operations, the project owner shall include in the Annual Compliance Report an accounting of all burrowing owl documented on site, including copies of the Designated Biologist or Biological Monitor’s field notes, any buffers zones erected, maps, additional avoidance and minimization measures implemented, and their perceived effectiveness.	within 10 days of the completion of the survey.	Completed	N/A	10/21/2025 - BAAH 12/23/2025 - Darden			BAAH - 11/10/2025 Darden - N/A	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-12	The Designated Biologist shall provide to the CPM preconstruction survey results to the CPM within 10 days of the completion of the survey. If surveys detect burrowing owls within 500 feet of proposed construction activities, the Designated Biologist shall provide to the CPM documentation indicating that non-disturbance buffer fencing has been installed no less than 10 days prior to the start of any project-related site disturbance activities. The documentation shall include information as specified in Items 4 and 5, or as otherwise requested by the CPM. If pre-construction surveys detect burrowing owls or active burrowing owl burrows within the project disturbance area, the project owner shall provide to the CPM a Burrowing Owl Mortality Reduction Plan prior to the start of activities (the measures described in the plan shall be incorporated into the BRMIMP and implemented.) The plan shall be for review and comment by the CPM and shall be finalized no less than 30 days prior to commencing activities which may disturb or take burrowing owls. During operations, the project owner shall provide a written report with Burrow Map (Item 5) to the CPM 10 days prior to starting Burrowing Owl Exclusion Activities on the site or in each distinct work areas(s). The project owner shall submit a Burrowing Owl Artificial Burrow Replacement Plan to the CPM for review and comment at least 30 days prior to initiation of pre-construction site mobilization. The final approved Burrowing Owl Artificial Burrow Replacement Plan shall be submitted prior to activities which may disturb or take burrowing owls. At the conclusion of the construction period, the Project Owner shall submit a final Burrowing Owl Mitigation Implementation Report detailing location of all burrowing owl observed, take measures implemented, and their effectiveness. During operations, the project owner shall include in the Annual Compliance Report an accounting of all burrowing owl documented on site, including copies of the Designated Biologist or Biological Monitor’s field notes, any buffers zones erected, maps, additional avoidance and minimization measures implemented, and their perceived effectiveness.	no less than 10 days prior to the start of any project-related site disturbance activities	No Action Needed	N/A	N/A				
Biological Resources	BIO-13	The project owner shall provide Security in the amount of in the form of an irrevocable letter of credit or another form of Security approved to the CPM prior to the start of pre-construction site mobilization, or the project owner may alternatively submit to the CPM a copy of the Bill of Sale(s) and Payment Receipt prior to initiating pre-construction site mobilization or within 24 months from issuance of the pre-construction site mobilization if Security is provided.	prior to the start of pre-construction site mobilization	Completed	N/A	10/17/2025 - BAAH 11/25/2025 - Darden			BAAH - 10/22/2025 Darden - N/A	
Biological Resources	BIO-13	The project owner shall provide Security in the amount of in the form of an irrevocable letter of credit or another form of Security approved to the CPM prior to the start of pre-construction site mobilization, or the project owner may alternatively submit to the CPM a copy of the Bill of Sale(s) and Payment Receipt prior to initiating pre-construction site mobilization or within 24 months from issuance of the pre-construction site mobilization if Security is provided.	prior to initiating pre-construction site mobilization or within 24 months from issuance of the pre-construction site mobilization if Security is provided.	No Action Needed	N/A	N/A				
Biological Resources	BIO-14	The project owner shall submit a report to the CPM within 30 days of completion of American badger surveys. The report shall describe survey methods, results, impact avoidance and minimization measures implemented, and the results of those measures. Ongoing (operation) sightings and avoidance measures as implemented by the Designated Biologist(s) or Biological Monitor(s) shall be noted in the MCR/ACRs.	within 30 days of completion of American badger surveys	Completed	N/A	10/21/2025 - BAAH 12/23/2025 - Darden			BAAH - 11/10/2025 Darden - N/A	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-14	The project owner shall submit a report to the CPM within 30 days of completion of American badger surveys. The report shall describe survey methods, results, impact avoidance and minimization measures implemented, and the results of those measures. Ongoing (operation) sightings and avoidance measures as implemented by the Designated Biologist(s) or Biological Monitor(s) shall be noted in the MCR/ACRs.	Monthly	In Progress - Rincon	N/A	N/A				
Biological Resources	BIO-15	The project owner shall submit a report to the CPM within 30 days of completion of San Joaquin kit fox surveys. The report shall include the names of the surveyors and qualifications as well as describe survey methods, results, impact avoidance and minimization measures to be implemented. The project owner shall submit information describing the findings of any additional San Joaquin kit fox surveys and implementation of any avoidance measures in the Monthly Compliance Report (MCR) (per BIO-6) to the CPM.	within 30 days of completion of San Joaquin kit fox surveys.	No Action Needed	N/A	10/21/2025 - BAAH			11/10/2025	
Biological Resources	BIO-15	The project owner shall submit a report to the CPM within 30 days of completion of San Joaquin kit fox surveys. The report shall include the names of the surveyors and qualifications as well as describe survey methods, results, impact avoidance and minimization measures to be implemented. The project owner shall submit information describing the findings of any additional San Joaquin kit fox surveys and implementation of any avoidance measures in the Monthly Compliance Report (MCR) (per BIO-6) to the CPM.	Monthly	No Action Needed	N/A	N/A				
Biological Resources	BIO-16	The project owner shall submit the results of the habitat assessment to the CPM for review and approval within 30 days of completion, and prior to start of both construction and subsequent surveys (if necessary). If surveys are performed, the Designated Biologist shall report monthly in the MCR. The report shall describe survey methods, results, impact avoidance and minimization measures implemented, and the results of those measures. The Designated Biologist or Biological Monitor shall ensure that appropriate CNDDDB records are filed. The Designated Biologist shall report all sightings of this species on the project site to the CPM within 24 hours.	Report survey results in MCR	In Progress - Rincon	N/A	N/A	CNDDDB (CDFW)			
Biological Resources	BIO-16	The project owner shall submit the results of the habitat assessment to the CPM for review and approval within 30 days of completion, and prior to start of both construction and subsequent surveys (if necessary). If surveys are performed, the Designated Biologist shall report monthly in the MCR. The report shall describe survey methods, results, impact avoidance and minimization measures implemented, and the results of those measures. The Designated Biologist or Biological Monitor shall ensure that appropriate CNDDDB records are filed. The Designated Biologist shall report all sightings of this species on the project site to the CPM within 24 hours.	within 30 days of completion, and prior to start of both construction and subsequent surveys (if necessary)	Submitted - CEC Review	N/A	10/17/2025 - BAAH 11/21/2025 - Darden III (pre-seeding) 12/17/2025 - Darden Gen-tie 12/19/2025 - Darden IV 12/22/2025 - Darden II	CNDDDB (CDFW)		BAAH - 10/24/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	at least 45 days prior to start of operation	Not Started - Rincon	N/A	N/A				
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	at least 7 days prior to start of operation.	Not Started - Rincon	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	at least 90 days prior to implementation	No Action Needed	N/A	N/A				
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	at least 30 days prior to implementation	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	30 days from receiving written comments from CPM	No Action Needed	N/A	N/A				
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	within 30 days of receipt	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	With quarterly reports	No Action Needed	N/A	N/A				
Biological Resources	BIO-17	The project owner shall submit the draft Informal Monitoring Study (IMP) to the CPM for review and approval and to the USFWS for review and comment at least 45 days prior to start of operation. The project owner shall provide the final IMP to the CPM, and USFWS at least 7 days prior to start of operation. The results of the IMP shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. If, at the direction of the CPM, a formal 2-year monitory study is determined necessary (in consultation with USFWS), the project owner shall submit the draft Avian and Bat Monitoring Study to the CPM for review and approval, and to USFWS for review and comment, at least 90 days prior to implementation. The project owner shall provide the final B Avian and Bat Monitoring Study to the CPM and USFWS at least 30 days prior to implementation. The results of the formal monitoring study shall be submitted to the CPM in quarterly reports. The Annual Report shall be subject to review and approval by the CPM in consultation with USFWS. The project owner shall submit revisions within 30 days of receiving written comments from the CPM. The project owner shall submit copies of all written or electronic communications from USFWS regarding the status of the SPUT or any related requirements to the CPM within 30 days of receipt. This includes any follow-up actions required by the project owner as specified by USFWS.	With quarterly reports	Not Started - Rincon	N/A	N/A				
Community Benefits Agreement	CBA-01	In the Annual Compliance Report, the project owner shall provide documentation evidencing compliance with the terms of the eight community benefits agreements listed above.	Annual	In Progress - IP	N/A	N/A				
Community Benefits Agreement	CBA-02	On or before January 1 and July 1 of each of the first 3 years after certification, the project owner shall file a progress report to the docket as outlined above. After the first 3 years, the project owner shall include this progress report in the Annual Compliance Report. The progress report shall also include an update on the status of the community benefits agreement with Comunidades de Westside.	On or before January 1 and July 1	Ongoing	N/A	12/30/2025			N/A	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	CIVIL-01	At least 15 days (or project owner- and DCBO-approved alternative time frame) prior to the start of site grading the project owner shall submit the documents described above to the DCBO for design review and approval. In the next MCR following the DCBO's approval, the project owner shall submit a written statement certifying that the documents have been approved by the DCBO.	At least 15 days (or project owner- and DCBO-approved alternative time frame) prior to the start of site grading.	DCBO Approved	8/12/2025 9/23/2025 12/31/2025	N/A			N/A - DCBO Approved 11/19/2025 - Initial Infrastructure Work Plan only N/A - DCBO Approved 1/14/2026	
Facility Design	CIVIL-01	At least 15 days (or project owner- and DCBO-approved alternative time frame) prior to the start of site grading the project owner shall submit the documents described above to the DCBO for design review and approval. In the next MCR following the DCBO's approval, the project owner shall submit a written statement certifying that the documents have been approved by the DCBO.	In the next MCR following the DCBO's approval	In Progress - EPC	N/A	N/A				
Facility Design	CIVIL-02	The project owner shall notify the CPM within 24 hours when earthwork and construction is stopped as a result of unforeseen adverse geologic/soil conditions. Within 24 hours of the DCBO's approval to resume earthwork and construction in the affected areas, the project owner shall provide to the CPM a copy of the DCBO's approval.	Within 24 hours when earthwork and construction is stopped as a result of unforeseen adverse geologic/soil conditions; Within 24 hours of the DCBO's approval to resume earthwork and construction in the affected areas.	No Action Needed	N/A	N/A				
Facility Design	CIVIL-02	The project owner shall notify the CPM within 24 hours when earthwork and construction is stopped as a result of unforeseen adverse geologic/soil conditions. Within 24 hours of the DCBO's approval to resume earthwork and construction in the affected areas, the project owner shall provide to the CPM a copy of the DCBO's approval.	Within 24 hours of the DCBO's approval to resume earthwork and construction in the affected areas	No Action Needed	N/A	N/A				
Facility Design	CIVIL-03	Within five days of the discovery of any discrepancies, the resident engineer shall transmit to the DCBO and the CPM a non-conformance report (NCR), and the proposed corrective action for review and approval. Within five days of resolution of the NCR, the project owner shall submit the details of the corrective action to the DCBO and the CPM. A list of NCRs for the reporting month shall also be included in the following MCR.	Within five days of the discovery of any discrepancies; within five days of resolution.	No Action Needed	N/A	N/A				
Facility Design	CIVIL-03	Within five days of the discovery of any discrepancies, the resident engineer shall transmit to the DCBO and the CPM a non-conformance report (NCR), and the proposed corrective action for review and approval. Within five days of resolution of the NCR, the project owner shall submit the details of the corrective action to the DCBO and the CPM. A list of NCRs for the reporting month shall also be included in the following MCR.	Within five days of the resolution	No Action Needed	N/A	N/A				
Facility Design	CIVIL-03	Within five days of the discovery of any discrepancies, the resident engineer shall transmit to the DCBO and the CPM a non-conformance report (NCR), and the proposed corrective action for review and approval. Within five days of resolution of the NCR, the project owner shall submit the details of the corrective action to the DCBO and the CPM. A list of NCRs for the reporting month shall also be included in the following MCR.	In the following MCR	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	CIVIL-04	Within 30 days (or project owner- and DCBO-approved alternative time frame) of the completion of the erosion and sediment control mitigation and drainage work, the project owner shall submit to the DCBO, for review and approval, the final grading plans (including final changes) and the responsible civil engineer's signed statement that the installation of the facilities and all erosion control measures were completed in accordance with the final approved combined grading plans, and that the facilities are adequate for their intended purposes. The project owner shall submit a copy of the DCBO's approval to the CPM in the next MCR.	Within 30 days (or project owner- and DCBO-approved alternative time frame) of the completion of the erosion and sediment control mitigation and drainage work.	In Progress - EPC	N/A	N/A				
Facility Design	CIVIL-04	Within 30 days (or project owner- and DCBO-approved alternative time frame) of the completion of the erosion and sediment control mitigation and drainage work, the project owner shall submit to the DCBO, for review and approval, the final grading plans (including final changes) and the responsible civil engineer's signed statement that the installation of the facilities and all erosion control measures were completed in accordance with the final approved combined grading plans, and that the facilities are adequate for their intended purposes. The project owner shall submit a copy of the DCBO's approval to the CPM in the next MCR.	Within 30 days (or project owner- and DCBO-approved alternative time frame) of the completion of the erosion and sediment control mitigation and drainage work.	Not Started - EPC	N/A	N/A				
Facility Design	CIVIL-04	Within 30 days (or project owner- and DCBO-approved alternative time frame) of the completion of the erosion and sediment control mitigation and drainage work, the project owner shall submit to the DCBO, for review and approval, the final grading plans (including final changes) and the responsible civil engineer's signed statement that the installation of the facilities and all erosion control measures were completed in accordance with the final approved combined grading plans, and that the facilities are adequate for their intended purposes. The project owner shall submit a copy of the DCBO's approval to the CPM in the next MCR.	Within 30 days (or project owner- and DCBO-approved alternative time frame) of the completion of the erosion and sediment control mitigation and drainage work.	Not Started - IP	N/A	N/A				
Compliance Conditions and Compliance Monitoring Plan	COM-01	Unrestricted Access. The project owner shall take all steps necessary to ensure that the CPM, responsible CEC staff, and delegate agencies or consultants, have unrestricted access to the facility site, related facilities, project-related staff, and the records maintained on site for the purpose of conducting audits, surveys, inspections, or general or closure-related site visits. Although the CPM will normally schedule site visits on dates and times agreeable to the project owner, the CPM reserves the right to make unannounced visits at any time, whether such visits are by the CPM in person or through representatives from CEC staff, delegated agencies, or consultants.	N/A	Completed	N/A	11/18/2025			N/A	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-02	The project owner shall maintain electronic copies of all project files and submittals accessible on site, or at an alternative site approved by the CPM, for the operational life and closure of the project. The files shall also contain at least one hard copy of: - the facility’s Opt-In Application; - all amendment petitions and CEC orders; - all site-related environmental impact and survey documentation; - all appraisals, assessments, and studies for the project; - all finalized original and amended structural plans and “as-built” drawings for the entire project; - all citations, warnings, violations, or corrective actions applicable to the project, and - the most current versions of any plans, manuals, and training documentation required by the COCs or applicable LORS. The CEC staff and delegate agencies shall, upon request to the project owner, be given unrestricted access to the files maintained pursuant to this condition which includes electronic submission of records to the CEC.	N/A	Completed	N/A	11/18/2025			N/A	
Compliance Conditions and Compliance Monitoring Plan	COM-03	Verification lead times associated with the start of construction may require the project owner to file submittals during application or amendment processing, particularly if construction is planned to commence shortly after certification. The verification procedures may be modified as necessary by the CPM after notice to the project owner. A cover letter from the project owner or an authorized agent is required for all compliance submittals and correspondence pertaining to compliance matters. The cover letter subject line shall identify the project by docket number, cite the appropriate condition of certification number(s), and give a brief description of the subject of the submittal. When submitting supplementary or corrected information, the project owner shall reference the date of the submittal and the condition(s) of certification applicable. All reports and plans required by the project’s COCs shall be submitted in a searchable electronic format (.pdf, MS Word or Excel, etc.) and include standard formatting elements such as a table of contents identifying by title and page number each section, table, graphic, exhibit, or addendum. All report and/or plan graphics and maps shall be adequately scaled and shall include a key with descriptive labels, directional headings, a bar scale, and the most recent revision date. The project owner is responsible for the content and delivery of all verification submittals to the CPM showing that the actions required by the verification were satisfied by the project owner or an agent of the project owner. All submittals shall be submitted electronically by email.	N/A	Ongoing	N/A	N/A			N/A	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-04	Prior to construction, the project owner shall submit to the CPM a compliance matrix including only those conditions that must be fulfilled before the start of construction. The matrix shall be included with the project owner’s first compliance submittal or prior to the first pre-construction meeting, whichever comes first, and shall be submitted in a format similar to the description below. Site mobilization and construction activities shall not start until the following have occurred: - the project owner has submitted the pre-construction matrix and all compliance verifications pertaining to pre-construction COCs; and - the CPM has issued an authorization-to-construct letter to the project owner. The deadlines for submitting various compliance verifications to the CPM allow staff sufficient time to review and comment on, and, if necessary, also allow the project owner to revise the submittal in a timely manner. These procedures help ensure that project construction proceeds according to schedule. Failure to submit required compliance documents by the specified deadlines may result in delayed authorizations to commence various stages of the project. If the project owner anticipates site mobilization immediately following project certification, it may be necessary for the project owner to file compliance submittals prior to project certification. In these instances, compliance verifications can be submitted in advance of the required deadlines and the anticipated authorizations to start construction. The project owner must understand that submitting items required in compliance verifications prior to these authorizations is at the owner’s own risk. Any approval by CEC staff prior to project certification is subject to change based upon the Commission Decision, or amendment thereto, and early staff compliance approvals do not imply that the CEC will certify the project for actual construction and operation.	Prior to construction	Completed	N/A	7/11/2025			N/A	
Compliance Conditions and Compliance Monitoring Plan	COM-05	The project owner shall submit a compliance matrix to the CPM with each MCR and ACR. The compliance matrix shall identify: - the technical area (e.g., biological resources, facility design, etc.); - the condition number; - a brief description of the verification action or submittal required by the condition; - the date the submittal is required (e.g., 60 days prior to construction, after final inspection, etc.); - the expected or actual submittal date; - the date a submittal or action was approved by the Delegate Chief Building Official (DCBO), CPM, or delegate agency, if applicable; - the compliance status of each condition (e.g., “not started,” “in progress” or “completed” (include the date)); and - if the condition was amended, the updated language and the date the amendment was proposed or approved. The CPM can provide a template for the compliance matrix upon request.	monthly and annually	Ongoing	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-05	The project owner shall submit a compliance matrix to the CPM with each MCR and ACR. The compliance matrix shall identify: - the technical area (e.g., biological resources, facility design, etc.); - the condition number; - a brief description of the verification action or submittal required by the condition; - the date the submittal is required (e.g., 60 days prior to construction, after final inspection, etc.); - the expected or actual submittal date; - the date a submittal or action was approved by the Delegate Chief Building Official (DCBO), CPM, or delegate agency, if applicable; - the compliance status of each condition (e.g., “not started,” “in progress” or “completed” (include the date)); and - if the condition was amended, the updated language and the date the amendment was proposed or approved. The CPM can provide a template for the compliance matrix upon request.	monthly and annually	Ongoing	N/A	7/11/2025 8/14/2025				
Compliance Conditions and Compliance Monitoring Plan	COM-06	The first MCR is due one month following the docketing of the project’s Decision unless otherwise agreed to by the CPM. The first MCR shall include the docket number and an initial list of dates for each of the events identified on the Key Events List. (The Key Events List form is found at the end of this Compliance Conditions and Compliance Monitoring Plan section.) During preconstruction, construction, or closure, the project owner or authorized agent shall submit an electronic searchable version of the MCR to the CPM within 10 business days after the end of each reporting month. MCRs shall be submitted each month until construction is complete and the final certificate of occupancy is issued by the DCBO. MCRs shall be clearly identified for the month being reported. The MCR shall contain, at a minimum: - a summary of the current project construction status, a revised/updated schedule if there are significant delays, and an explanation of any significant changes to the schedule; - documents required by specific conditions to be submitted along with the MCR. Each of these items shall be identified in the transmittal letter, as well as the conditions they satisfy, and submitted as attachments to the MCR; - an initial, and thereafter updated, compliance matrix showing the status of all COCs; - a list of conditions that have been satisfied during the reporting period, and a description or reference to the actions that satisfied the condition; - a list of any submittal deadlines that were missed, accompanied by an explanation and an estimate of when the information will be provided; - a cumulative listing of any approved changes to COCs; - a listing of any filings submitted to, and permits issued by, other governmental agencies during the month; - a projection of project compliance activities scheduled during the next two months; the project owner shall notify the CPM as soon as any changes are made to the project construction schedule that would affect compliance with COCs; - a listing of the month’s additions to the on-site compliance file; and - a listing of incidents, complaints, notices of violation, official warnings, and citations received during the month; a list of any incidents that occurred during the month, a description of the actions taken to date to resolve the issues; and the status of any unresolved actions noted in the previous MCRs.	one month following the docketing of the project’s Decision unless otherwise agreed to by the CPM	Completed	N/A	7/11/2025		N/A - Docketed 7/11/2025		

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-06	The first MCR is due one month following the docketing of the project’s Decision unless otherwise agreed to by the CPM. The first MCR shall include the docket number and an initial list of dates for each of the events identified on the Key Events List. (The Key Events List form is found at the end of this Compliance Conditions and Compliance Monitoring Plan section.) During preconstruction, construction, or closure, the project owner or authorized agent shall submit an electronic searchable version of the MCR to the CPM within 10 business days after the end of each reporting month. MCRs shall be submitted each month until construction is complete and the final certificate of occupancy is issued by the DCBO. MCRs shall be clearly identified for the month being reported. The MCR shall contain, at a minimum: a summary of the current project construction status, a revised/updated schedule if there are significant delays, and an explanation of any significant changes to the schedule; documents required by specific conditions to be submitted along with the MCR. Each of these items shall be identified in the transmittal letter, as well as the conditions they satisfy, and submitted as attachments to the MCR; an initial, and thereafter updated, compliance matrix showing the status of all COCs; a list of conditions that have been satisfied during the reporting period, and a description or reference to the actions that satisfied the condition; a list of any submittal deadlines that were missed, accompanied by an explanation and an estimate of when the information will be provided; a cumulative listing of any approved changes to COCs; a listing of any filings submitted to, and permits issued by, other governmental agencies during the month; a projection of project compliance activities scheduled during the next two months; the project owner shall notify the CPM as soon as any changes are made to the project construction schedule that would affect compliance with COCs; a listing of the month’s additions to the on-site compliance file; and a listing of incidents, complaints, notices of violation, official warnings, and citations received during the month; a list of any incidents that occurred during the month, a description of the actions taken to date to resolve the issues; and the status of any unresolved actions noted in the previous MCRs.	within 10 days after end of each reporting month	Ongoing	N/A	7/11/2025		N/A		
						8/14/2025				
						9/15/2025				
						10/15/2025				
						11/17/2025				
						12/12/2025				
						1/14/2026				
						2/13/2026				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-07	After construction is complete, the project must submit searchable electronic ACRs to the CPM, as well as other periodic compliance reports (PCRs) required by the various technical disciplines. ACRs shall be completed for each year of commercial operation and are due each year on a date agreed to by the CPM. Other PCRs (e.g. quarterly reports or decommissioning reports to monitor closure compliance), may be specified by the CPM. The searchable electronic copies may be filed on an electronic storage medium or by e-mail, subject to CPM approval. Each ACR must include the docket number, identify the reporting period, and contain the following: - an updated compliance matrix which shows the status of all COCs (fully satisfied conditions do not need to be included in the matrix after they have been reported as completed); - a summary of the current project operating status and an explanation of any significant changes to facility operations during the year; - documents required by specific conditions to be submitted along with the ACR; each of these items shall be identified in the transmittal letter with the condition(s) it satisfies, and submitted as an attachment to the ACR; - a cumulative list of all post-certification changes approved by the Energy Commission or the CPM; - an explanation for any submittal deadlines that were missed, accompanied by an estimate of when the information will be provided; - a listing of filings submitted to, or permits issued by, other governmental agencies during the year; - a projection of project compliance activities scheduled during the next year; - a listing of the year’s additions to the on-site compliance file; - an evaluation of the Site Contingency Plan, including amendments and plan updates; and - a listing of complaints, incidents, notices of violation, official warnings, and citations received during the year, a description of how the issues were resolved, and the status of any unresolved complaints.	Post construction	Not Started - Rincon	N/A	N/A				
Compliance Conditions and Compliance Monitoring Plan	COM-08	Any information that the project owner designates as confidential shall be submitted to the Energy Commission’s Executive Director with an application for confidentiality, pursuant to Title 20, California Code of Regulations, section 2505(a). Any information deemed confidential pursuant to the regulations will remain undisclosed, as provided in Title 20, California Code of Regulations, section 2501 et seq.	N/A	Ongoing	N/A	N/A			N/A	
Compliance Conditions and Compliance Monitoring Plan	COM-09	Pursuant to the provisions of section 25806(b) of the Public Resources Code, the project owner is required to pay an annually adjusted compliance fee. Current compliance fee information is available on the CEC’s website at http://www.energy.ca.gov/siting/filing_fees.html . The project owner may also contact the CPM for the current fee information. The initial payment is due on the date the CEC docket its final Decision. All subsequent payments are due by July 1 of each year in which the facility retains its certification.	The initial payment is due on the date the CEC docket its final Decision.	Ongoing	N/A	N/A			N/A	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-10	The project owner shall petition the CEC, pursuant to Title 20, California Code of Regulations, section 1882, to modify the design, operation, or performance requirements of the project or linear facilities. The CPM will determine whether staff approval will be sufficient, or whether CEC approval will be necessary. It is the project owner’s responsibility to contact the CPM to determine if a proposed project change triggers the requirements of section 1882. Section 1882 details the required contents for a petition to amend a CEC Decision. For changes in ownership or operational control the existing owner/operator and incoming owner/operator shall jointly in writing notify the CPM, 30 days in advance of the pending change in ownership or operational control, the fact of the change and all relevant contact information. Upon the transition, the new owner/operator will be obligated to comply with all requirements of the certification and will be subject to enforcement actions. A project owner is required to submit a \$5,000 fee for every petition to amend a previously certified facility, pursuant to Public Resources Code section 25806 (e). If the actual amendment processing costs exceed \$5,000.00, the total PTA reimbursement fees owed by a project owner will not exceed the OPT cap of \$1,050,850, adjusted annually. Current amendment fee information is available on the CEC’s website at http://www.energy.ca.gov/siting/filing_fees.html.	N/A	No Action Needed	N/A	N/A				
Compliance Conditions and Compliance Monitoring Plan	COM-10	The project owner shall petition the CEC, pursuant to Title 20, California Code of Regulations, section 1882, to modify the design, operation, or performance requirements of the project or linear facilities. The CPM will determine whether staff approval will be sufficient, or whether CEC approval will be necessary. It is the project owner’s responsibility to contact the CPM to determine if a proposed project change triggers the requirements of section 1882. Section 1882 details the required contents for a petition to amend a CEC Decision. For changes in ownership or operational control the existing owner/operator and incoming owner/operator shall jointly in writing notify the CPM, 30 days in advance of the pending change in ownership or operational control, the fact of the change and all relevant contact information. Upon the transition, the new owner/operator will be obligated to comply with all requirements of the certification and will be subject to enforcement actions. A project owner is required to submit a \$5,000 fee for every petition to amend a previously certified facility, pursuant to Public Resources Code section 25806 (e). If the actual amendment processing costs exceed \$5,000.00, the total PTA reimbursement fees owed by a project owner will not exceed the OPT cap of \$1,050,850, adjusted annually. Current amendment fee information is available on the CEC’s website at http://www.energy.ca.gov/siting/filing_fees.html.	30 days prior in advance of the pending change in ownership or operational control	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-10	The project owner shall petition the CEC, pursuant to Title 20, California Code of Regulations, section 1882, to modify the design, operation, or performance requirements of the project or linear facilities. The CPM will determine whether staff approval will be sufficient, or whether CEC approval will be necessary. It is the project owner’s responsibility to contact the CPM to determine if a proposed project change triggers the requirements of section 1882. Section 1882 details the required contents for a petition to amend a CEC Decision. For changes in ownership or operational control the existing owner/operator and incoming owner/operator shall jointly in writing notify the CPM, 30 days in advance of the pending change in ownership or operational control, the fact of the change and all relevant contact information. Upon the transition, the new owner/operator will be obligated to comply with all requirements of the certification and will be subject to enforcement actions. A project owner is required to submit a \$5,000 fee for every petition to amend a previously certified facility, pursuant to Public Resources Code section 25806 (e). If the actual amendment processing costs exceed \$5,000.00, the total PTA reimbursement fees owed by a project owner will not exceed the OPT cap of \$1,050,850, adjusted annually. Current amendment fee information is available on the CEC’s website at http://www.energy.ca.gov/siting/filing_fees.html.	Upon every petition to amend certified facility	No Action Needed	N/A	N/A				
Compliance Conditions and Compliance Monitoring Plan	COM-11	Prior to the start of construction or closure, the project owner shall send a letter to property owners and residences within one mile of the project boundaries, notifying them of a telephone number to contact project representatives with questions, complaints or concerns. All notifications and complaint forms shall be provided in both English and Spanish to ensure effective communication with Spanish-speaking residents. If the telephone is not staffed 24 hours per day, it must include automatic answering with date and time stamp recording. The project owner shall respond to all recorded complaints within 24 hours or the next business day. The project owner shall post the telephone number onsite and make it easily visible to passersby during construction, the first year of project operation, and closure. The project owner shall provide the contact information to the CPM and promptly report any disruption to the contact system or telephone number change to the CPM, who will provide it to any persons contacting him or her with a complaint. Within five business days of receipt, the project owner shall report, and provide copies to the CPM, all complaints, including, but not limited to, noise and lighting complaints, notices of violation, notices of fines, official warnings, and citations. Complaints shall be logged and numbered. Noise complaints shall be recorded on the form provided in the Noise and Vibration conditions of certification. All other complaints shall be recorded on the complaint form at the end of this compliance plan. Additionally, the project owner must include in the next MCR, ACR or PCR, copies of all complaints, notices, warnings, citations and fines, a description of how the issues were resolved, and the status of any unresolved or ongoing matters.	within five business days of receipt of a complaint	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-11	Prior to the start of construction or closure, the project owner shall send a letter to property owners within one mile of the project, notifying them of a telephone number to contact project representatives with questions, complaints or concerns. If the telephone is not staffed 24 hours per day, it must include automatic answering with date and time stamp recording. The project owner shall respond to all recorded complaints within 24 hours or the next business day. The project owner shall post the telephone number onsite and make it easily visible to passersby during construction, operation, and closure. The project owner shall provide the contact information to the CPM and promptly report any disruption to the contact system or telephone number change to the CPM, who will provide it to any persons contacting him or her with a complaint. Within five business days of receipt, the project owner shall report, and provide copies to the CPM, all complaints, including, but not limited to, noise and lighting complaints, notices of violation, notices of fines, official warnings, and citations. Complaints shall be logged and numbered. Noise complaints shall be recorded on the form provided in the Noise and Vibration conditions of certification. All other complaints shall be recorded on the complaint form at the end of this compliance plan. Additionally, the project owner must include in the next MCR, ACR or PCR, copies of all complaints, notices, warnings, citations and fines, a description of how the issues were resolved, and the status of any unresolved or ongoing matters.	next MCR prior to the start of construction or closure	CEC Approved	N/A	10/23/2025 11/14/2025			11/18/2025	
Compliance Conditions and Compliance Monitoring Plan	COM-11	Prior to the start of construction or closure, the project owner shall send a letter to property owners and residences within one mile of the project, notifying them of a telephone number to contact project representatives with questions, complaints or concerns. All notifications and complaint forms shall be provided in both English and Spanish to ensure effective communication with Spanish-speaking residents. If the telephone is not staffed 24 hours per day, it must include automatic answering with date and time stamp recording. The project owner shall respond to all recorded complaints within 24 hours or the next business day. The project owner shall post the telephone number onsite and make it easily visible to passersby during construction, and first year of project operation, and closure. The project owner shall provide the contact information to the CPM and promptly report any disruption to the contact system or telephone number change to the CPM, who will provide it to any persons contacting him or her with a complaint. Within five business days of receipt, the project owner shall report, and provide copies to the CPM, all complaints, including, but not limited to, noise and lighting complaints, notices of violation, notices of fines, official warnings, and citations. Complaints shall be logged and numbered. Noise complaints shall be recorded on the form provided in the Noise and Vibration conditions of certification. All other complaints shall be recorded on the complaint form at the end of this compliance plan. Additionally, the project owner must include in the next MCR, ACR or PCR, copies of all complaints, notices, warnings, citations and fines, a description of how the issues were resolved, and the status of any unresolved or ongoing matters.	within 5 business days; next MCR, ACR, PCR	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-12	No less than 60 days prior to the start of construction (or other CPM-approved) date, the project owner shall submit, for CPM review and approval, an Emergency Response Site Contingency Plan (Contingency Plan). Subsequently, no less than 60 days prior to the start of commercial operation, the project owner shall update (as necessary) and resubmit the Contingency Plan for CPM review and approval. The Contingency Plan shall evidence a facility’s coordinated emergency response and recovery preparedness for a series of reasonably foreseeable emergency events. The CPM may require Contingency Plan updating over the life of the facility. Contingency Plan elements include, but are not limited to: 1. a site-specific list and direct contact information for persons, agencies, and responders to be notified for an unanticipated event; 2. a detailed and labeled facility map, including all fences and gates, the windsock location (if applicable), the on and off-site assembly areas, and the main roads and highways near the site; 3. a detailed and labeled map of population centers, sensitive receptors, and the nearest emergency response facilities; 4. a description of the on-site, first response and backup emergency alert and communication systems, site-specific emergency response protocols, and procedures for maintaining the facility’s contingency response capabilities, including a detailed map of interior and exterior evacuation routes, and the planned location(s) of all permanent safety equipment; 5. an organizational chart including the name, contact information, and first aid/emergency response certification(s) and renewal date(s) for all personnel regularly on-site; 6. a brief description of reasonably foreseeable, site-specific incidents and accident sequences (on- and off-site), including response procedures and protocols and site security measures to maintain twenty-four-hour site security; 7. procedures for maintaining contingency response capabilities; and 8. the procedures and implementation sequence for the safe and secure shutdown of all non-critical equipment and removal of hazardous materials and waste (see also specific conditions of certification for the technical areas of Public Health, Solid Waste Management, Hazards, Hazardous Materials, and Wildfire, and Worker Safety and Fire Protection).	60 days prior to start of commercial operation	Not Started - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-12	No less than 60 days prior to the start of construction (or other CPM-approved) date, the project owner shall submit, for CPM review and approval, an Emergency Response Site Contingency Plan (Contingency Plan). Subsequently, no less than 60 days prior to the start of commercial operation, the project owner shall update (as necessary) and resubmit the Contingency Plan for CPM review and approval. The Contingency Plan shall evidence a facility’s coordinated emergency response and recovery preparedness for a series of reasonably foreseeable emergency events. The CPM may require Contingency Plan updating over the life of the facility. Contingency Plan elements include, but are not limited to: - a site-specific list and direct contact information for persons, agencies, and responders to be notified for an unanticipated event; - a detailed and labeled facility map, including all fences and gates, the windsock location (if applicable), the on and off-site assembly areas, and the main roads and highways near the site; - a detailed and labeled map of population centers, sensitive receptors, and the nearest emergency response facilities; - a description of the on-site, first response and backup emergency alert and communication systems, site-specific emergency response protocols, and procedures for maintaining the facility’s contingency response capabilities, including a detailed map of interior and exterior evacuation routes, and the E283planned location(s) of all permanent safety equipment; - an organizational chart including the name, contact information, and first aid/emergency response certification(s) and renewal date(s) for all personnel regularly on-site; - a brief description of reasonably foreseeable, site-specific incidents and accident sequences (on- and off-site), including response procedures and protocols and site security measures to maintain twenty-four-hour site security; - procedures for maintaining contingency response capabilities; and - the procedures and implementation sequence for the safe and secure shutdown of all non-critical equipment and removal of hazardous materials and waste (see also specific conditions of certification for the technical areas of Public Health, Solid Waste Management, Hazards, Hazardous Materials, and Wildfire, and Worker Safety and Fire Protection).	No less than 60 days prior to the start of construction (or other CPM-approved) date; no less than 60 days prior to the start of commercial operation	CEC Approved	N/A	9/9/2025 10/21/2025 - BAAH 11/4/2025 - Darden 11/21/2025-Darden			BAAH - 10/24/2025 Darden - 04/21/2026	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-13	The project owner shall notify the CPM within one hour after it is safe and feasible, of any incident at the facility that results in any of the following: 1. An event of any kind that causes a “Forced Outage” as defined in the CAISO tariff; 2. The activation of onsite emergency fire suppression equipment to combat a fire; 3. Any chemical, gas or hazardous materials release that could result in potential health impacts to the surrounding population; or create an offsite odor issue; and 4. Notification to, or response by, any off-site emergency response federal, state or local agency regarding a fire, hazardous materials release, onsite injury, or any physical or cyber security incident. Notification shall describe the circumstances, status, and expected duration of the incident. If warranted, as soon as it is safe and feasible, the project owner shall implement the safe shutdown of any non-critical equipment and removal of any hazardous materials and waste that pose a threat to public health and safety and to environmental quality (also, see specific conditions of certification for the technical areas of Hazards, Hazardous Materials and Wildfire, and Solid Waste Management). Within six business days of the incident, the project owner shall submit to the CPM a detailed incident report that includes, as applicable, the following information: 1. A brief description of the incident, including its date, time, and location; 2. A description of the cause of the incident, or likely causes if it is still under investigation; 3. The location of any off-site impacts; 4. Description of any resultant impacts; 5. A description of emergency response actions associated with the incident; 6. Identification of responding agencies; 7. Identification of emergency notifications made to federal, state, and local agencies; 8. Identification of any hazardous materials released and an estimate of the quantity released; 9. A description of any injuries, fatalities, or property damage that occurred as a result of the incident; 10. Fines or violations assessed or being processed by other agencies; 11. Name, phone number, and e-mail address of the appropriate facility contact person having knowledge of the event; and 12. Corrective actions to prevent a recurrence of the incident. The project owner shall maintain all incident report records for the life of the project, including closure. After the submittal of the initial report for any incident, the project owner shall submit to the CPM copies of incident reports within 48 hours of a request. If the project owner requests that an incident notification or report be designated as a confidential record and not publicly disclosed, the project owner shall submit copies of notices or reports with an application for confidential designation in accordance with CEC regulations.	Within one hour of the incident after it is safe and feasible	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-13	The project owner shall notify the CPM within one hour after it is safe and feasible, of any incident at the facility that results in any of the following: 1. An event of any kind that causes a “Forced Outage” as defined in the CAISO tariff; 2. The activation of onsite emergency fire suppression equipment to combat a fire; 3. Any chemical, gas or hazardous materials release that could result in potential health impacts to the surrounding population; or create an offsite odor issue; and 4. Notification to, or response by, any off-site emergency response federal, state or local agency regarding a fire, hazardous materials release, onsite injury, or any physical or cyber security incident. Notification shall describe the circumstances, status, and expected duration of the incident. If warranted, as soon as it is safe and feasible, the project owner shall implement the safe shutdown of any non-critical equipment and removal of any hazardous materials and waste that pose a threat to public health and safety and to environmental quality (also, see specific conditions of certification for the technical areas of Hazards, Hazardous Materials and Wildfire, and Solid Waste Management). Within six business days of the incident, the project owner shall submit to the CPM a detailed incident report that includes, as applicable, the following information: 1. A brief description of the incident, including its date, time, and location; 2. A description of the cause of the incident, or likely causes if it is still under investigation; 3. The location of any off-site impacts; 4. Description of any resultant impacts; 5. A description of emergency response actions associated with the incident; 6. Identification of responding agencies; 7. Identification of emergency notifications made to federal, state, and local agencies; 8. Identification of any hazardous materials released and an estimate of the quantity released; 9. A description of any injuries, fatalities, or property damage that occurred as a result of the incident; 10. Fines or violations assessed or being processed by other agencies; 11. Name, phone number, and e-mail address of the appropriate facility contact person having knowledge of the event; and 12. Corrective actions to prevent a recurrence of the incident. The project owner shall maintain all incident report records for the life of the project, including closure. After the submittal of the initial report for any incident, the project owner shall submit to the CPM copies of incident reports within 48 hours of a request. If the project owner requests that an incident notification or report be designated as a confidential record and not publicly disclosed, the project owner shall submit copies of notices or reports with an application for confidential designation in accordance with CEC regulations.	Within six business days of the incident, depending on specific criteria met.	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-14	If the facility ceases operation temporarily (excluding planned and unplanned maintenance) for longer than one week (or other CPM approved date), but less than three months (or other CPM-approved date), the project owner shall notify the CPM. Notice of planned non-operation shall be given at least two weeks prior to the scheduled date. Notice of unplanned non-operation shall be provided no later than one week after non-operation begins. a. For any non-operation, a Repair/Restoration Plan for conducting the activities necessary to restore the facility to availability and reliable and/or improved performance shall be submitted to the CPM within one week after notice of nonoperation is given. If non-operation is due to an unplanned incident, temporary repairs and/or corrective actions may be undertaken before the Repair/Restoration Plan is submitted. The Repair/Restoration Plan shall include: 1. Identification of operational and non-operational components of the plant; 2. A detailed description of the repair and inspection or restoration activities; 3. A proposed schedule for completing the repair and inspection or restoration activities; 4. An assessment of whether or not the proposed activities would require changing, adding, and/or deleting any COCs, and/or would cause noncompliance with any applicable LORS; and 5. Planned activities during non-operation, including any measures to ensure continued compliance with all COCs and LORS. b. Written monthly updates (or other CPM-approved intervals) to the CPM for nonoperational periods, until operation resumes, shall include: 1. Progress relative to the schedule; 2. Developments that delayed or advanced progress or that may delay or advance future progress; 3. Any public, agency, or media comments or complaints; and 4. Projected date for the resumption of operation c. During non-operation, all applicable COCs and reporting requirements remain in effect. If, after one year from the date of the project owner’s last report of productive repair/restoration plan work, the facility does not resume operation or does not provide a plan to resume operation, the Executive Director may assign suspended status to the facility and recommend commencement of permanent closure activities. Within 90 days of the Executive Director’s determination, the project owner shall do one of the following: 1. If the facility has a closure plan, the project owner shall update it and submit it for CEC review and approval; or 2. If the facility does not have a closure plan, the project owner shall develop one consistent with the requirements in this Compliance Plan and submit it for CEC review and approval.	2 weeks prior to date of non operation	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-14	If the facility ceases operation temporarily (excluding planned and unplanned maintenance for longer than one week (or other CPM approved date), but less than three months (or other CPM-approved date), the project owner shall notify the CPM. Notice of planned non-operation shall be given at least two weeks prior to the scheduled date. Notice of unplanned non-operation shall be provided no later than one week after non-operation begins. a. For any non-operation, a Repair/Restoration Plan for conducting the activities necessary to restore the facility to availability and reliable and/or improved performance shall be submitted to the CPM within one week after notice of nonoperation is given. If non-operation is due to an unplanned incident, temporary repairs and/or corrective actions may be undertaken before the Repair/Restoration Plan is submitted. The Repair/Restoration Plan shall include: 1. Identification of operational and non-operational components of the plant; 2. A detailed description of the repair and inspection or restoration activities; 3. A proposed schedule for completing the repair and inspection or restoration activities; 4. An assessment of whether or not the proposed activities would require changing, adding, and/or deleting any COCs, and/or would cause noncompliance with any applicable LORS; and 5. Planned activities during non-operation, including any measures to ensure continued compliance with all COCs and LORS. b. Written monthly updates (or other CPM-approved intervals) to the CPM for nonoperational periods, until operation resumes, shall include: 1. Progress relative to the schedule; 2. Developments that delayed or advanced progress or that may delay or advance future progress; 3. Any public, agency, or media comments or complaints; and 4. Projected date for the resumption of operation c. During non-operation, all applicable COCs and reporting requirements remain in effect. If, after one year from the date of the project owner’s last report of productive repair/restoration plan work, the facility does not resume operation or does not provide a plan to resume operation, the Executive Director may assign suspended status to the facility and recommend commencement of permanent closure activities. Within 90 days of the Executive Director’s determination, the project owner shall do one of the following: 1. If the facility has a closure plan, the project owner shall update it and submit it for CEC review and approval; or 2. If the facility does not have a closure plan, the project owner shall develop one consistent with the requirements in this Compliance Plan and submit it for CEC review and approval.	One week after non-operation begins	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-14	If the facility ceases operation temporarily (excluding planned and unplanned maintenance for longer than one week (or other CPM approved date), but less than three months (or other CPM-approved date), the project owner shall notify the CPM. Notice of planned non-operation shall be given at least two weeks prior to the scheduled date. Notice of unplanned non-operation shall be provided no later than one week after non-operation begins. a. For any non-operation, a Repair/Restoration Plan for conducting the activities necessary to restore the facility to availability and reliable and/or improved performance shall be submitted to the CPM within one week after notice of nonoperation is given. If non-operation is due to an unplanned incident, temporary repairs and/or corrective actions may be undertaken before the Repair/Restoration Plan is submitted. The Repair/Restoration Plan shall include: 1. Identification of operational and non-operational components of the plant; 2. A detailed description of the repair and inspection or restoration activities; 3. A proposed schedule for completing the repair and inspection or restoration activities; 4. An assessment of whether or not the proposed activities would require changing, adding, and/or deleting any COCs, and/or would cause noncompliance with any applicable LORS; and 5. Planned activities during non-operation, including any measures to ensure continued compliance with all COCs and LORS. b. Written monthly updates (or other CPM-approved intervals) to the CPM for nonoperational periods, until operation resumes, shall include: 1. Progress relative to the schedule; 2. Developments that delayed or advanced progress or that may delay or advance future progress; 3. Any public, agency, or media comments or complaints; and 4. Projected date for the resumption of operation c. During non-operation, all applicable COCs and reporting requirements remain in effect. If, after one year from the date of the project owner’s last report of productive repair/restoration plan work, the facility does not resume operation or does not provide a plan to resume operation, the Executive Director may assign suspended status to the facility and recommend commencement of permanent closure activities. Within 90 days of the Executive Director’s determination, the project owner shall do one of the following: 1. If the facility has a closure plan, the project owner shall update it and submit it for CEC review and approval; or 2. If the facility does not have a closure plan, the project owner shall develop one consistent with the requirements in this Compliance Plan and submit it for CEC review and approval.	within one week after non-operation notice given	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Compliance Conditions and Compliance Monitoring Plan	COM-14	If the facility ceases operation temporarily (excluding planned and unplanned maintenance for longer than one week (or other CPM approved date), but less than three months (or other CPM-approved date), the project owner shall notify the CPM. Notice of planned non-operation shall be given at least two weeks prior to the scheduled date. Notice of unplanned non-operation shall be provided no later than one week after non-operation begins. a. For any non-operation, a Repair/Restoration Plan for conducting the activities necessary to restore the facility to availability and reliable and/or improved performance shall be submitted to the CPM within one week after notice of nonoperation is given. If non-operation is due to an unplanned incident, temporary repairs and/or corrective actions may be undertaken before the Repair/Restoration Plan is submitted. The Repair/Restoration Plan shall include: 1. Identification of operational and non-operational components of the plant; 2. A detailed description of the repair and inspection or restoration activities; 3. A proposed schedule for completing the repair and inspection or restoration activities; 4. An assessment of whether or not the proposed activities would require changing, adding, and/or deleting any COCs, and/or would cause noncompliance with any applicable LORS; and 5. Planned activities during non-operation, including any measures to ensure continued compliance with all COCs and LORS. b. Written monthly updates (or other CPM-approved intervals) to the CPM for nonoperational periods, until operation resumes, shall include: 1. Progress relative to the schedule; 2. Developments that delayed or advanced progress or that may delay or advance future progress; 3. Any public, agency, or media comments or complaints; and 4. Projected date for the resumption of operation c. During non-operation, all applicable COCs and reporting requirements remain in effect. If, after one year from the date of the project owner’s last report of productive repair/restoration plan work, the facility does not resume operation or does not provide a plan to resume operation, the Executive Director may assign suspended status to the facility and recommend commencement of permanent closure activities. Within 90 days of the Executive Director’s determination, the project owner shall do one of the following: 1. If the facility has a closure plan, the project owner shall update it and submit it for CEC review and approval; or 2. If the facility does not have a closure plan, the project owner shall develop one consistent with the requirements in this Compliance Plan and submit it for CEC review and approval.	90 days from Executive Director's determination	No Action Needed	N/A	N/A				
Compliance Conditions and Compliance Monitoring Plan	COM-15	To ensure that a facility’s eventual permanent closure and maintenance do not pose a threat to public health and safety and/or to environmental quality, the project owner shall coordinate with the CEC to plan and prepare for eventual permanent closure.	Prior to permanent closure	No Action Needed	N/A	N/A				
Cultural and Tribal Cultural Resources	CUL-01	Within 30 days of selection of a CRS, the project owner shall provide a copy of any resume(s) to CEC for review and approval that the CRS meets the Standards.	within 30 days of selection of CRS	CEC Approved	N/A	7/25/2025			8/1/2025	
Cultural and Tribal Cultural Resources	CUL-02	At least 90 days prior to the start of construction, the project owner shall provide a draft CTCRMMP to CEC for review and approval.	90 days prior to construction	CEC Approved	N/A	8/14/2025 9/26/2025			10/15/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Cultural and Tribal Cultural Resources	CUL-03	At least 20 days prior to the start of construction, the project owner shall notify CEC that the WEAP has been scheduled and allow for participation of any tribal participants should they have requested so during CEC’s ongoing tribal consultation for the undertaking.	20 days prior to construction	Completed	N/A	N/A			N/A	
Cultural and Tribal Cultural Resources	CUL-04	Within 60 days of completion of ground disturbing activities requiring monitoring, the CRS shall provide a monitoring report to the CEC for review and approval, consistent with the CTCRMMP prepared under COC CUL-2.	Submit within 60 days after construction monitoring is completed	Not Started - Rincon	N/A	N/A				
Cultural and Tribal Cultural Resources	CUL-05	Should there be an unanticipated discovery of cultural or tribal cultural resources, the CRS shall comply with state law and any provisions described in the CTCRMMP. The CRS shall notify CEC within 24 hours of the discovery and invite CEC’s participation in the resolution of the find.	within 24 hours of unanticipated discovery	No Action Needed	N/A	N/A				
Cultural and Tribal Cultural Resources	CUL-06	Should human remains be discovered, the CRS shall comply with state law and any provisions described in the AMDP. The CRS shall notify CEC within 24 hours of the discovery and invite CEC’s participation in the resolution of the find.	within 24 hours of HR discovery	No Action Needed	N/A	N/A				
Facility Design	ELEC-01	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of each increment of electrical construction, the project owner shall submit to the DCBO for design review and approval the above listed documents. The project owner shall include in this submittal a copy of the signed and stamped statement from the responsible electrical engineer attesting compliance with the applicable LORS and shall send the CPM a copy of the transmittal letter in the next MCR.	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of each increment of electrical construction	In Progress - EPC	8/13/2025 9/23/2025 10/2/2025 10/17/2025 10/31/2025 1/12/2026	N/A			N/A - DCBO Approved 2/13/2026 - PV only N/A - DCBO Approved 4/7/2026 - BESS	
Facility Design	ELEC-01	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of each increment of electrical construction, the project owner shall submit to the DCBO for design review and approval the above listed documents. The project owner shall include in this submittal a copy of the signed and stamped statement from the responsible electrical engineer attesting compliance with the applicable LORS and shall send the CPM a copy of the transmittal letter in the next MCR.	Next MCR	In Progress- EPC	N/A	N/A				
Facility Design	GEN-01	Within 30 days following receipt of the certificate of occupancy (CofO), the project owner shall submit to the Compliance project Manager (CPM) a statement of verification, signed by the responsible design engineer, attesting that all designs, construction, installation, and inspection requirements of the applicable LORS and the CEC's decision have been met in the area of Facility Design. The project owner shall provide the CPM a copy of the CofO within 30 days of receipt from the DCBO. Once the CofO has been issued, the project owner shall inform the CPM at least 30 days prior to any construction, addition, alteration, moving, demolition, repair, or maintenance to be performed on any portion(s) of the completed facility that requires DCBO approval for compliance with the above codes. The CPM will then determine if the DCBO needs to approve the work. A statement of verification, signed by the responsible design engineer, attesting that all designs, construction, installation, and inspection requirements of the applicable LORS and the CEC's decision have been met in the area of Facility Design, shall be submitted to the Compliance Project Manager (CPM).	30 days following the receipt of CofO	Not Started - IP	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	GEN-01	Within 30 days following receipt of the certificate of occupancy (CofO), the project owner shall submit to the Compliance project Manager (CPM) a statement of verification, signed by the responsible design engineer, attesting that all designs, construction, installation, and inspection requirements of the applicable LORS and the CEC's decision have been met in the area of Facility Design. The project owner shall provide the CPM a copy of the CofO within 30 days of receipt from the DCBO. Once the CofO has been issued, the project owner shall inform the CPM at least 30 days prior to any construction, addition, alteration, moving, demolition, repair, or maintenance to be performed on any portion(s) of the completed facility that requires DCBO approval for compliance with the above codes. The CPM will then determine if the DCBO needs to approve the work. A statement of verification, signed by the responsible design engineer, attesting that all designs, construction, installation, and inspection requirements of the applicable LORS and the CEC's decision have been met in the area of Facility Design, shall be submitted to the Compliance Project Manager (CPM).	The project owner shall provide the CPM a copy of the certificate of occupancy (CofO) within 30 days of receipt from the DCBO.	Not Started - IP	N/A	N/A				
Facility Design	GEN-01	Within 30 days following receipt of the certificate of occupancy (CofO), the project owner shall submit to the Compliance project Manager (CPM) a statement of verification, signed by the responsible design engineer, attesting that all designs, construction, installation, and inspection requirements of the applicable LORS and the CEC's decision have been met in the area of Facility Design. The project owner shall provide the CPM a copy of the CofO within 30 days of receipt from the DCBO. Once the CofO has been issued, the project owner shall inform the CPM at least 30 days prior to any construction, addition, alteration, moving, demolition, repair, or maintenance to be performed on any portion(s) of the completed facility that requires DCBO approval for compliance with the above codes. The CPM will then determine if the DCBO needs to approve the work. A statement of verification, signed by the responsible design engineer, attesting that all designs, construction, installation, and inspection requirements of the applicable LORS and the CEC's decision have been met in the area of Facility Design, shall be submitted to the Compliance Project Manager (CPM).	The project owner shall inform the CPM at least 30 days prior to any scheduled activity.	No Action Needed	N/A	N/A				
Facility Design	GEN-02	At least 60 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of rough grading, the project owner shall submit to the DCBO and to the CPM the schedule, and the master drawings and master specifications list of documents to be submitted to the DCBO, for review and approval. These documents shall be the pertinent design documents for the major structures, systems, and equipment. Major structures, systems, and equipment shall be added to or deleted from the list only with CPM approval. The project owner shall provide schedule updates in the monthly compliance report (MCR).	At least 60 days prior to the start of rough grading (or a project owner and DCBO mutually agreed upon alternative time frame)	DCBO Approved	8/8/2025 10/23/2025	8/15/2025 10/29/2025			N/A - DCBO Approved 10/29/2025	
Facility Design	GEN-03	The project owner shall make the required payments to the DCBO in accordance with the agreement between the project owner and the DCBO. If the CEC delegates the DCBO function to a third party or local agency, the project owner, at the CEC's direction, shall make payments directly to the DCBO based upon a fee schedule negotiated between the CEC and the DCBO. The project owner shall send a copy of the DCBO's receipt of payment to the CPM in the next MCR indicating that applicable fees have been paid.	In accordance with the agreement between the project owner and the DCBO or based upon a fee schedule negotiated between the CEC and the DCBO.	In Progress - IP	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	GEN-04	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of rough grading, the project owner shall submit to the DCBO for review and approval, the resume and qualifications registration number of the RE and any other delegated engineers or construction project manager assigned to the project. The project owner shall notify the CPM of the DCBO's approvals of the RE and other delegated engineer(s) within five days of the approval. If the RE or the delegated engineer(s) is subsequently reassigned or replaced, the project owner has five days to submit the name, qualifications, and registration number of the newly assigned engineer or construction project manager to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO's approval of the new engineer within five days of the approval.	At least 30 days prior to the start of rough grading (or a project owner and DCBO mutually agreed upon alternative time frame). The project owner shall notify the CPM of the DCBO's approvals of the RE and other delegated engineer(s) within five days of the approval.	DCBO Approved	9/3/2025	9/26/2025			N/A - DCBO Approved 9/26/2025	
Facility Design	GEN-05	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of rough grading, the project owner shall submit to the DCBO for review and approval, resumes and registration numbers of the responsible civil engineer, soils (geotechnical) engineer, and engineering geologist assigned to the project. At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of construction, the project owner shall submit to the DCBO for review and approval, resumes and registration numbers of the responsible design engineer, mechanical engineer, and electrical engineer assigned to the project. The project owner shall notify the CPM of the DCBO's approvals of the responsible engineers within five days of the approval. If any one of the designated responsible engineers is subsequently reassigned or replaced, the project owner has five days in which to submit the name, qualifications, and registration number of the newly assigned engineer to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO's approval of the new engineer within five days of the approval.	At least 30 days prior to the start of rough grading (or a project owner and DCBO mutually agreed upon alternative time frame)	DCBO Approved	9/10/2025 9/30/2025	10/6/2025			N/A - DCBO Approved 10/6/2025	
Facility Design	GEN-06	At least 15 days (or project owner- and DCBO-approved alternative time frame) prior to the start of an activity requiring special inspection, the project owner shall submit to the DCBO for review and approval, with a copy to the CPM, the name(s) and qualifications of the certified weld inspector(s), or other certified special inspector(s) assigned to the project to perform one or more of the duties set forth above. The project owner shall also submit to the CPM a copy of the DCBO's approval of the qualifications of all special inspectors in the next MCR. If the special inspector is subsequently reassigned or replaced, the project owner has five days in which to submit the name and qualifications of the newly assigned special inspector to the DCBO for approval. The project owner shall notify the CPM of the DCBO's approval of the newly assigned inspector within five days of the approval.	15 days (or project owner- and DCBO-approved alternative time frame) prior to the start of an activity requiring special inspection	DCBO Approved	N/A	12/30/2025			N/A - DCBO Approved 1/5/2026	
Facility Design	GEN-07	The project owner shall transmit a copy of the DCBO's approval of any corrective action taken to resolve a discrepancy to the CPM in the next MCR. If any corrective action is disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval and the revised corrective action to obtain DCBO's approval.	Discrepancy documentation submitted to the DCBO.	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	GEN-08	Within 15 days of the completion of any work, the project owner shall submit to the DCBO, with a copy to the CPM in the next MCR, (a) a written notice that the completed work is ready for final inspection, and (b) a signed statement that the work conforms to the final approved plans. After storing the final approved engineering plans, specifications, and calculations described above, the project owner shall submit to the CPM a letter stating both that the above documents have been stored and the storage location of those documents. Within 90 days of the completion of construction, the project owner shall provide to the DCBO three sets of electronic copies of the above documents at the project owner's expense. These are to be provided in the form of "read only" files (the latest version of Adobe .pdf available), with restricted (passwordprotected) printing privileges.	After storing the final approved engineering plans, specifications, and calculations	Not Started - EPC	N/A	N/A				
Facility Design	GEN-08	Within 15 days of the completion of any work, the project owner shall submit to the DCBO, with a copy to the CPM in the next MCR, (a) a written notice that the completed work is ready for final inspection, and (b) a signed statement that the work conforms to the final approved plans. After storing the final approved engineering plans, specifications, and calculations described above, the project owner shall submit to the CPM a letter stating both that the above documents have been stored and the storage location of those documents. Within 90 days of the completion of construction, the project owner shall provide to the DCBO three sets of electronic copies of the above documents at the project owner's expense. These are to be provided in the form of "read only" files (the latest version of Adobe .pdf available), with restricted (passwordprotected) printing privileges.	Within 90 days of the completion of construction	Not Started - EPC/IP	N/A	N/A				
Facility Design	GEN-08	Within 15 days of the completion of any work, the project owner shall submit to the DCBO, with a copy to the CPM in the next MCR, (a) a written notice that the completed work is ready for final inspection, and (b) a signed statement that the work conforms to the final approved plans. After storing the final approved engineering plans, specifications, and calculations described above, the project owner shall submit to the CPM a letter stating both that the above documents have been stored and the storage location of those documents. Within 90 days of the completion of construction, the project owner shall provide to the DCBO three sets of electronic copies of the above documents at the project owner's expense. These are to be provided in the form of "read only" files (the latest version of Adobe .pdf available), with restricted (passwordprotected) printing privileges.	Within 15 days of the completion of any work, the project owner shall submit to the DCBO	Not Started - EPC	N/A	N/A				
Geology, Paleontology, and Minerals	GEO-01	As described in the CBC (2022) Section 1803.6, the project owner shall submit a written geotechnical report to the DCBO. The project owner shall provide to the CPM copies of the geotechnical investigations and geohazards report, building permit, and any comments by the DCBO at least 60 days prior to grading.	60 days prior to grading	DCBO Approved	11/10/2025				N/A - DCBO Approved 11/19/2025	
Geology, Paleontology, and Minerals	GEO-01	As described in the CBC (2022) Section 1803.6, the project owner shall submit a written geotechnical report to the DCBO. The project owner shall provide to the CPM copies of the geotechnical investigations and geohazards report, building permit, and any comments by the DCBO at least 60 days prior to grading.	Prior to submittal to CPM, which must occur at least 60 days prior to grading	Completed	8/12/2025	N/A			N/A	
Climate Change and Greenhouse Gas Emissions	GHG-01	To ensure compliance with this condition the project owner must identify and confirm the compliant refrigerant cooling fluid installation, along with an estimated annual greenhouse gas emissions in metric tons of CO2-equivalent (MTCO2e) to be submitted to the CEC CPM for verification, within 30 days prior to installation of HVAC. Once confirmed and approved by the CEC CPM, this verification is considered complete.	30 days prior to installation of HVAC unit.	Submitted - CEC Review	N/A	1/13/2026 1/22/2026 2/3/2026 3/4/2026				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-01	At least 60 days prior to the start of operation the project owner shall prepare and submit the HMBP and SPCC Plan to the Fresno County HazMat Compliance Program for review and comment and to the CPM for review and approval. The project owner shall also provide the CPM with a copy of the transmittal letter to the Fresno County HazMat Compliance Program requesting review and comment. At least 30 days prior to the start of operation, the project owner shall provide copies of any comment letters received from the Fresno County HazMat Compliance Program along with any changes to the HMBP and SPCC plans for CPM review and approval. After CPM review and approval, the project owner shall provide complete copies of the final HMBP and SPCC to the Fresno County HazMat Compliance Program, sending copies of the correspondence to the CPM.	60 days prior to the start of operation	Not Started - EPC	N/A	N/A	Fresno County HazMat Compliance Program	HMBP: 9/15/2025		
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-01	At least 60 days prior to the start of operation the project owner shall prepare and submit the HMBP and SPCC Plan to the Fresno County HazMat Compliance Program for review and comment and to the CPM for review and approval. The project owner shall also provide the CPM with a copy of the transmittal letter to the Fresno County HazMat Compliance Program requesting review and comment. At least 30 days prior to the start of operation, the project owner shall provide copies of any comment letters received from the Fresno County HazMat Compliance Program along with any changes to the HMBP and SPCC plans for CPM review and approval. After CPM review and approval, the project owner shall provide complete copies of the final HMBP and SPCC to the Fresno County HazMat Compliance Program, sending copies of the correspondence to the CPM.	30 days prior to the start of operation	Not Started - EPC	N/A	N/A	Fresno County HazMat Compliance Program	HMBP: 9/15/2025		
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-02	At least 30 days prior to changing the quantity of or using a new hazardous material onsite, the project owner shall notify and seek approval from the CPM. The project owner shall provide to the CPM, in the Annual Compliance Report, the HMBP's list of hazardous materials and quantities contained at the facility.	30 days prior to changing the quantity or using a new hazmat onsite	Not Started - EPC/IP	N/A	N/A				
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-02	At least 30 days prior to changing the quantity of or using a new hazardous material onsite, the project owner shall notify and seek approval from the CPM. The project owner shall provide to the CPM, in the Annual Compliance Report, the HMBP's list of hazardous materials and quantities contained at the facility.	30 days prior to changing the quantity or using a new hazmat onsite	No Action Needed	N/A	N/A				
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-03	The project owner shall keep a copy of the identification number(s) on file at the project site and provide documentation of the hazardous waste generation and notification and receipt of the number to the CPM in the next scheduled Monthly Compliance Report after receipt of the number. Submittal of the notification and issued number documentation to the CPM is only needed once, unless there is a change in ownership, operation, waste generation, or waste characteristics that requires a new notification to EPA. Documentation of any new or revised hazardous waste generation notifications or changes in identification number shall be provided to the CPM 30 days before the change occurs.	As needed when new identification numbers are required	Not Started - EPC/IP	N/A	N/A				
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-04	At least 30 days prior to commencing construction, the project owner shall notify the CPM that a site-specific Construction Security Plan is available for review and approval.	30 days prior to the start of construction	CEC Approved	N/A	10/20/2025			11/18/2025	
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-05	At least 30 days prior to the initial receipt of hazardous materials onsite, the project owner shall notify the CPM that a site-specific operations site security plan is available for review and approval. In the annual compliance report, the project owner shall include signed statements similar to Attachments A and B that all current project employees and appropriate contractor background investigations have been performed, and that updated certification statements have been appended to the operations security plan. In the annual compliance report, the project owner shall include a signed statement similar to Attachment C that the operations security plan includes all current hazardous materials transport vendor certifications for security plans and employee background investigations.	30 days prior to receipt of hazardous materials on-site	Not Started - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-06	At least 45 days prior to any ground disturbance, the project owner shall submit the SMP to the Fresno County CUPA for review and comment and to the CPM for review and approval. An SMP summary shall be submitted to the CPM within 30 days of completion of any ground disturbance.	45 days prior to ground disturbance	CEC Approved	N/A	9/9/2025 10/21/2025	Fresno County CUPA	9/25/2025	10/23/2025	
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-06	At least 45 days prior to any ground disturbance, the project owner shall submit the SMP to the Fresno County CUPA for review and comment and to the CPM for review and approval. An SMP summary shall be submitted to the CPM within 30 days of completion of any ground disturbance.	Within 30 days of completion of ground disturbance	Not Started - EPC	N/A	N/A				
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-07	At least 30 days prior to the start of site mobilization, the project owner shall submit the resume of an experienced and qualified professional engineer or professional geologist to the CPM for review and approval.	30 days prior to site mobilization	CEC Approved	N/A	10/20/2025			11/18/2025	
Hazards, Hazardous Materials/Waste, and Wildfire	HAZ-08	The project owner shall submit the proposed sampling plan to the CPM 45 days prior to proposed BESS operations for review, revisions, and approval prior to BESS operations.	45 days prior to BESS operations	Not Started - EPC	N/A	N/A				
Mandatory Opt In Regulations	LABOR-01	Upon request by the Compliance Project Manager (CPM), the project owner shall provide documentation evidencing compliance with the requirements of Public Resources Code section 25545.3.3.	Upon request	No Action Needed	N/A	N/A				
Facility Design	MECH-01	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of any increment of major mechanical related components' construction listed in the DCBO-approved master drawing and master specifications list, the project owner shall submit to the DCBO for design review and approval the final plans, specifications, and calculations, including a copy of the signed and stamped statement from the responsible mechanical engineer certifying compliance with applicable LORS, and shall send the CPM a copy of the transmittal letter in the next MCR. The project owner shall transmit to the CPM, in the MCR following completion of any inspection, a copy of the transmittal letter conveying the DCBO's inspection approvals.	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of any increment of major mechanical related components' construction listed in the DCBO-approved master drawing and master specifications list	DCBO Approved	9/17/2025 10/28/2025	N/A			N/A - DCBO Approved 11/4/2025	
Facility Design	MECH-01	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of any increment of major mechanical related components' construction listed in the DCBO-approved master drawing and master specifications list, the project owner shall submit to the DCBO for design review and approval the final plans, specifications, and calculations, including a copy of the signed and stamped statement from the responsible mechanical engineer certifying compliance with applicable LORS, and shall send the CPM a copy of the transmittal letter in the next MCR. The project owner shall transmit to the CPM, in the MCR following completion of any inspection, a copy of the transmittal letter conveying the DCBO's inspection approvals.	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of any increment of major mechanical related components' construction listed in the DCBO-approved master drawing and master specifications list	In Progress - EPC	N/A	N/A				
Facility Design	MECH-02	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of construction of any permanent HVAC or refrigeration system, the project owner shall submit to the DCBO the required HVAC and refrigeration calculations, plans, and specifications, including a copy of the signed and stamped statement from the responsible mechanical engineer certifying compliance with the CBC and other applicable codes, with a copy of the transmittal letter to the CPM.	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of construction of any HVAC or refrigeration system,	DCBO Approved	10/6/2025	N/A			N/A - DCBO Approved 10/27/25	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Noise and Vibration	NOISE-01	Within five days of receiving a noise complaint, the project owner shall file with the CPM the Noise Complaint Resolution Form, that documents the resolution of the complaint. If mitigation is required to resolve the complaint, and the complaint is not resolved within three business days, the project owner shall submit an updated Noise Complaint Resolution Form when the mitigation is implemented.	Within five days of receiving a noise complaint	No Action Needed	N/A	N/A				
Noise and Vibration	NOISE-02	At least 30 days prior to the start of ground disturbance, the project owner shall submit the noise control program to the CPM. The project owner shall make the program available to Cal-OSHA upon request.	At least 30 days prior to the start of ground disturbance	CEC Approved	N/A	9/24/2025 - BAAH 9/9/2025 - MAM	Cal-OSHA		BAAH - 10/22/2025 Darden - 11/18/2025	
Noise and Vibration	NOISE-03	The survey shall take place within 45 days of the project first achieving a sustained output that produces the highest noise level. Within 30 days after completing the survey, the project owner shall submit a summary report of the survey to the CPM. Included in the survey report will be a description of any additional mitigation measures necessary to achieve compliance with the above listed noise limits, and a schedule, subject to CPM approval, for implementing these measures. When these measures are in place, the project owner shall repeat the noise survey. Within 15 days of completion of the new survey, the project owner shall submit to the CPM a summary report of the new noise survey, performed as described above and showing compliance with this condition.	Survey shall take place within 45 days of project achieving a sustained output that produces the highest noise level; summary report shall be submitted within 30 days of completing the survey	Not Started - Rincon	N/A	N/A				
Noise and Vibration	NOISE-03	The survey shall take place within 45 days of the project first achieving a sustained output that produces the highest noise level. Within 30 days after completing the survey, the project owner shall submit a summary report of the survey to the CPM. Included in the survey report will be a description of any additional mitigation measures necessary to achieve compliance with the above listed noise limits, and a schedule, subject to CPM approval, for implementing these measures. When these measures are in place, the project owner shall repeat the noise survey. Within 15 days of completion of the new survey, the project owner shall submit to the CPM a summary report of the new noise survey, performed as described above and showing compliance with this condition.	Survey shall take place within 45 days of project achieving a sustained output that produces the highest noise level; summary report shall be submitted within 30 days of completing the survey	Not Started - Rincon	N/A	N/A				
Noise and Vibration	NOISE-04	Within 30 days after completing each survey, the project owner shall submit the noise survey report to the CPM. The project owner shall make the report available to Cal-OSHA upon request from Cal-OSHA.	Survey shall take place within 45 days of project achieving a sustained output that produces the highest noise level; summary report shall be submitted within 30 days of completing the survey	Not Started - EPC	N/A	N/A				
Noise and Vibration	NOISE-05	Prior to ground disturbance, the project owner shall transmit to the CPM a statement acknowledging that the above restrictions will be observed throughout the construction of the project.	Prior to ground disturbance	CEC Approved	N/A	9/19/2025 - BAAH 10/29/2025 - Darden			BAAH - 10/22/2025 Darden - 11/18/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Noise and Vibration	NOISE-06	At least 15 days prior to first pile driving, the project owner shall submit to the CPM a description of the pile driving technique to be employed, including calculations showing its projected noise impacts and peak particle velocity at monitoring locations R-5, R-8, and R-13. Examples of noise-reducing techniques include: (1) the use of pads or impact cushions of plywood; (2) dampened driving, which involves some form of blanket or enclosure around the hammer; (3) the use of vibratory drivers or hydraulic pile pushers instead of impact; or (4) installation of a temporary barriers such as a mobile sound screen near the pile driver or other effective mitigation measures that reduce the noise and vibration impacts of pile driving. At least 10 days prior to first production pile driving, the project owner shall notify residences in the vicinity of the project. The notification may be in the form of letters, or other effective means, as approved by the CPM. In this notification, the project owner shall state that it will perform this activity in a manner to reduce the potential for any project-related noise and vibration complaints.	10 days prior to first pile driving to notify residences	Submitted - CEC Review	N/A	1/13/2026 3/17/2026				
Noise and Vibration	NOISE-06	At least 15 days prior to first pile driving, the project owner shall submit to the CPM a description of the pile driving technique to be employed, including calculations showing its projected noise impacts and peak particle velocity at monitoring locations R-5, R-8, and R-13. Examples of noise-reducing techniques include: (1) the use of pads or impact cushions of plywood; (2) dampened driving, which involves some form of blanket or enclosure around the hammer; (3) the use of vibratory drivers or hydraulic pile pushers instead of impact; or (4) installation of a temporary barriers such as a mobile sound screen near the pile driver or other effective mitigation measures that reduce the noise and vibration impacts of pile driving. At least 10 days prior to first production pile driving, the project owner shall notify residences in the vicinity of the project. The notification may be in the form of letters, or other effective means, as approved by the CPM. In this notification, the project owner shall state that it will perform this activity in a manner to reduce the potential for any project-related noise and vibration complaints.	15 days prior to first pile driving for statement of techniques to be employed and calculations; 10 days prior to first pile driving to notify residences	Submitted - CEC Review	N/A	1/2/2026				
Geology, Paleontology, and Minerals	PAL-01	At least 60 days prior to the start of ground disturbance, the project owner shall submit a resume and statement of availability of its designated PRS for on-site work to the CPM, whose approval must be obtained prior to initiation of ground disturbing activities. At least 30 days prior to ground disturbance, the PRS or project owner shall provide a letter with resumes naming anticipated PRMs for the project. The letter shall state that the identified PRMs meet the minimum qualifications for paleontological resource monitoring as required by this condition of certification. If additional PRMs are needed during the project, the PRS shall provide additional letters and resumes to the CPM. The letter shall be provided to the CPM for approval no later than one week prior to the monitor’s beginning on-site duties. Prior to any change of the PRS, the project owner shall submit the resume of the proposed new PRS to the CPM for review and approval.	60 days prior to the start of construction for PRS	CEC Approved	N/A	7/25/2025 3/17/2026			10/22/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Geology, Paleontology, and Minerals	PAL-01	At least 60 days prior to the start of ground disturbance, the project owner shall submit a resume and statement of availability of its designated PRS for on-site work to the CPM, whose approval must be obtained prior to initiation of ground disturbing activities. At least 30 days prior to ground disturbance, the PRS or project owner shall provide a letter with resumes naming anticipated PRMs for the project. The letter shall state that the identified PRMs meet the minimum qualifications for paleontological resource monitoring as required by this condition of certification. If additional PRMs are needed during the project, the PRS shall provide additional letters and resumes to the CPM. The letter shall be provided to the CPM for approval no later than one week prior to the monitor’s beginning on-site duties. Prior to any change of the PRS, the project owner shall submit the resume of the proposed new PRS to the CPM for review and approval.	30 days prior to the start of construction	CEC Approved	N/A	9/19/2025 12/4/2025 3/17/2026			10/22/2025 1/28/2026	
Geology, Paleontology, and Minerals	PAL-02	At least 30 days prior to the start of ground disturbance, the project owner shall provide the maps and drawings to the PRS and CPM. If there are planned changes to the footprint of the project, revised maps and drawings shall be provided to the PRS and CPM at least 15 days prior to the start of ground disturbance. If there are changes to the scheduling of the construction phases, the Project owner shall submit a letter to the CPM within five days of identifying the changes.	15 days prior to the start of previously unplanned activities or beginning of new construction phases	No Action Needed	N/A	N/A				
Geology, Paleontology, and Minerals	PAL-02	At least 30 days prior to the start of ground disturbance, the project owner shall provide the maps and drawings to the PRS and CPM. If there are planned changes to the footprint of the project, revised maps and drawings shall be provided to the PRS and CPM at least 15 days prior to the start of ground disturbance. If there are changes to the scheduling of the construction phases, the Project owner shall submit a letter to the CPM within five days of identifying the changes.	30 days prior to the start of construction	CEC Approved	N/A	9/24/2025 10/27/2025			BAAH - 10/22/2025 Darden - 11/18/2025	
Geology, Paleontology, and Minerals	PAL-03	At least 30 days prior to ground disturbance, the project owner shall provide a copy of the PRMMP to the CPM. Approval of the PRMMP by the CPM shall occur prior to any ground disturbance. The PRMMP shall include an affidavit of authorship by the PRS and acceptance of the PRMMP by the project owner evidenced by a signature.	30 days prior to the start of construction	CEC Approved	N/A	9/19/2025			10/22/2025	
Geology, Paleontology, and Minerals	PAL-04	At least 30 days prior to ground disturbance, the project owner shall submit to the CPM for review and comment the draft WEAP, including the brochure and sticker. The submittal shall also include a draft training script and the set of reporting procedures for workers to follow. At least 15 days prior to ground disturbance, the project owner shall submit to the CPM for approval the final WEAP and training script. If the project owner is planning to use a video for training, a copy of the training video shall be submitted following final approval of the WEAP and training script.	15 days prior to construction (final slides; final brochure; final script; video)	CEC Approved	N/A	9/19/2025			10/22/2025	
Geology, Paleontology, and Minerals	PAL-04	At least 30 days prior to ground disturbance, the project owner shall submit to the CPM for review and comment the draft WEAP, including the brochure and sticker. The submittal shall also include a draft training script and the set of reporting procedures for workers to follow. At least 15 days prior to ground disturbance, the project owner shall submit to the CPM for approval the final WEAP and training script. If the project owner is planning to use a video for training, a copy of the training video shall be submitted following final approval of the WEAP and training script.	30 days prior to construction (draft slides, draft brochure, sticker, draft script)	CEC Approved	N/A	9/19/2025			10/22/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Geology, Paleontology, and Minerals	PAL-05	In the Monthly Compliance Report (MCR), the project owner shall provide copies of the WEAP certification of completion forms with the names of those trained, trainer identification, and type of training (in-person and/or video) offered that month. The MCR shall also include a running total of all persons who have completed the training to date. The resume and qualifications of the trainer shall be submitted to the CPM for review and approval prior to providing WEAP training. If the project owner requests an alternate paleontological WEAP trainer, the resume and qualifications of the trainer shall be submitted to the CPM for review and approval prior to installation of an alternate trainer. Alternate trainers shall not conduct WEAP training prior to CPM authorization.	Prior to delivery of WEAP by someone other than PRS	CEC Approved	N/A	9/19/2025			10/22/2025	
Geology, Paleontology, and Minerals	PAL-05	In the Monthly Compliance Report (MCR), the project owner shall provide copies of the WEAP certification of completion forms with the names of those trained, trainer identification, and type of training (in-person and/or video) offered that month. The MCR shall also include a running total of all persons who have completed the training to date. The resume and qualifications of the trainer shall be submitted to the CPM for review and approval prior to providing WEAP training. If the project owner requests an alternate paleontological WEAP trainer, the resume and qualifications of the trainer shall be submitted to the CPM for review and approval prior to installation of an alternate trainer. Alternate trainers shall not conduct WEAP training prior to CPM authorization.	Monthly	Ongoing - Rincon	N/A	N/A				
Geology, Paleontology, and Minerals	PAL-06	A copy of the daily monitoring log of paleontological resource activities shall be included in the MCR. The project owner shall ensure that the PRS submits the summary of monitoring and paleontological activities in the MCR. When feasible, the CPM shall be notified 15 days in advance of any proposed changes in monitoring different from that identified in the PRMMP, which require concurrence between the PRS and CPM. If there is any unforeseen change in monitoring, the notice shall be given as soon as possible prior to implementation of the change.	As-needed; 15 days prior to the enactment of monitoring protocol changes	No Action Needed	N/A	N/A				
Geology, Paleontology, and Minerals	PAL-06	For any significant paleontological resources encountered, either the project owner or the PRS shall notify the CPM within 24 hours. If the resources are encountered on a weekend or holiday, notification shall occur on the morning of the next business day. In the event construction has been stopped because of a paleontological find, such notification shall be provided as soon as practical, but not later than 24 hours after a stop work order has been issued.	As-needed within 24 hours of incident of non-compliance (or next business day)	No Action Needed	N/A	N/A				
Geology, Paleontology, and Minerals	PAL-06	A copy of the daily monitoring log of paleontological resource activities shall be included in the MCR. The project owner shall ensure that the PRS submits the summary of monitoring and paleontological activities in the MCR. When feasible, the CPM shall be notified 15 days in advance of any proposed changes in monitoring different from that identified in the PRMMP, which require concurrence between the PRS and CPM. If there is any unforeseen change in monitoring, the notice shall be given as soon as possible prior to implementation of the change.	As-needed within 24 hours of fossil discovery (or next business day)	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Geology, Paleontology, and Minerals	PAL-06	A copy of the daily monitoring log of paleontological resource activities shall be included in the MCR. The project owner shall ensure that the PRS submits the summary of monitoring and paleontological activities in the MCR. When feasible, the CPM shall be notified 15 days in advance of any proposed changes in monitoring different from that identified in the PRMMP, which require concurrence between the PRS and CPM. If there is any unforeseen change in monitoring, the notice shall be given as soon as possible prior to implementation of the change.	Logs to be recorded daily; submitted monthly	Ongoing - Rincon	N/A	N/A				
Geology, Paleontology, and Minerals	PAL-06	A copy of the daily monitoring log of paleontological resource activities shall be included in the MCR. The project owner shall ensure that the PRS submits the summary of monitoring and paleontological activities in the MCR. When feasible, the CPM shall be notified 15 days in advance of any proposed changes in monitoring different from that identified in the PRMMP, which require concurrence between the PRS and CPM. If there is any unforeseen change in monitoring, the notice shall be given as soon as possible prior to implementation of the change.	Monthly	Ongoing - Rincon	N/A	N/A				
Geology, Paleontology, and Minerals	PAL-07	Within 90 days after completion of ground-disturbing activities, including landscaping, the project owner shall submit the PRR under confidential cover to the CPM.	90 days after completion of ground-disturbing activities	Not Started - Rincon	N/A	N/A				
Geology, Paleontology, and Minerals	PAL-08	Within 60 days after the submittal of the PRR, the project owner shall submit documentation to the CPM identifying the entity that would be responsible for curating collected specimens. This documentation shall also show that fees have been paid for curation and the owner relinquishes control and ownership of all fossil material.	60 days after submittal of Paleontological Resources Report (if necessary)	No Action Needed	N/A	N/A				
Socioeconomics	SOCIO-01	At least 30 days prior to the start of project construction, the project owner shall provide to the CPM proof of payment to the Office of Education of the statutory development fee.	At least 30 days prior to the start of project construction	Completed	N/A	11/24/2025			N/A	
Facility Design	STRUC-01	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of any increment of construction of any structure or component listed in the DCBO-approved master drawing and master specifications list, the project owner shall submit to the DCBO the above final design plans, specifications and calculations, with a copy of the transmittal letter to the CPM. The project owner shall submit to the CPM, in the next MCR, a copy of a statement from the DCBO that the proposed structural plans, specifications, and calculations have been approved and comply with the requirements set forth in applicable engineering LORS.	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of any increment of construction of any structure or component listed in the DCBO-approved master drawing and master specifications list	In Progress - EPC	8/13/2025 9/23/2025 10/17/2025 3/19/2026	N/A			N/A - DCBO Approved 12/19/2025 - BESS and PV only	
Facility Design	STRUC-01	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of any increment of construction of any structure or component listed in the DCBO-approved master drawing and master specifications list, the project owner shall submit to the DCBO the above final design plans, specifications and calculations, with a copy of the transmittal letter to the CPM. The project owner shall submit to the CPM, in the next MCR, a copy of a statement from the DCBO that the proposed structural plans, specifications, and calculations have been approved and comply with the requirements set forth in applicable engineering LORS.	Next MCR	In Progress - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Within 5 days of discrepancy discovery	No Action Needed	N/A	N/A				
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Within 5 days of discrepancy resolution	No Action Needed	N/A	N/A				
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Within 15 days of DCBO approval	No Action Needed	N/A	N/A				
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Within 5 days of the reason for disapproval.	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Completion of Work	Not Started - EPC	N/A	N/A				
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Completion of Work	Not Started - EPC	N/A	N/A				
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Completion of Work	Not Started - EPC	N/A	N/A				
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Completion of Work	Not Started - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Facility Design	STRUC-02	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the DCBO, with a copy of the transmittal letter to the CPM. The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the DCBO and the CPM. The project owner shall transmit a copy of the DCBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, of the reason for disapproval, and the revised corrective action to obtain DCBO's approval.	Completion of Work	Not Started - EPC	N/A	N/A				
Facility Design	STRUC-03	On a schedule suitable to the DCBO, the project owner shall notify the DCBO of the intended filing of design changes, and shall submit the required number of sets of revised drawings and the required number of copies of the other above-mentioned documents to the DCBO, with a copy of the transmittal letter to the CPM. The project owner shall notify the CPM, via the MCR, when the DCBO has approved the revised plans.	Schedule suitable to DCBO	No Action Needed	N/A	N/A				
Facility Design	STRUC-03	On a schedule suitable to the DCBO, the project owner shall notify the DCBO of the intended filing of design changes, and shall submit the required number of sets of revised drawings and the required number of copies of the other above-mentioned documents to the DCBO, with a copy of the transmittal letter to the CPM. The project owner shall notify the CPM, via the MCR, when the DCBO has approved the revised plans.	when DCBO has approved the plans	No Action Needed	N/A	N/A				
Facility Design	STRUC-04	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of installation of the tanks or vessels containing the above specified quantities of toxic or hazardous materials, the project owner shall submit to the DCBO for design review and approval final design plans, specifications, and calculations, including a copy of the signed and stamped engineer's certification. The project owner shall send copies of the DCBO approvals of plan checks to the CPM in the MCR following receipt of such approvals. The project owner shall also transmit a copy of the DCBO's inspection approvals to the CPM in the MCR following completion of any inspection.	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of installation of the tanks or vessels containing the above specified quantities of toxic or hazardous materials	DCBO Approved	1/12/2026	N/A			N/A - DCBO Approved 03/09/2026	
Facility Design	STRUC-04	At least 30 days (or a project owner and DCBO mutually agreed upon alternative time frame) prior to the start of installation of the tanks or vessels containing the above specified quantities of toxic or hazardous materials, the project owner shall submit to the DCBO for design review and approval final design plans, specifications, and calculations, including a copy of the signed and stamped engineer's certification. The project owner shall send copies of the DCBO approvals of plan checks to the CPM in the MCR following receipt of such approvals. The project owner shall also transmit a copy of the DCBO's inspection approvals to the CPM in the MCR following completion of any inspection.	when DCBO has approved the plan checks.	In Progress - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Air Quality	SWITCH AQ-01	The AQCMM shall provide the CPM a Monthly Compliance Report to include the following to demonstrate control of fugitive dust emissions: A. A summary of all actions taken to maintain compliance with this condition; B. Copies of any complaints filed with the District in relation to project construction; and C. Any other documentation deemed necessary by the CPM and AQCMM to verify compliance with this condition. Such information may be provided via electronic format or disk at the project owner’s discretion.	Monthly	Ongoing - EPC	N/A	N/A				
Biological Resources	SWITCH BIO-01	The project owner shall submit a report to the CPM, CDFW and USFWS within 30 days of completion of surveys performed within work areas identified as suitable BNLL habitat. The report shall include the names of the surveyors and qualifications as well as describe survey methods, results, impact avoidance and minimization measures to be implemented. The project owner shall summarize the survey findings and describe any implemented avoidance or minimization measures in the Monthly Compliance Report (MCR), pursuant to Condition of Certification BIO-6.	30 days from completion of surveys	N/A	N/A	10/17/2025 - BAAH	CDFW, USFWS		10/24/2025	
Biological Resources	SWITCH BIO-01	The project owner shall submit a report to the CPM, CDFW and USFWS within 30 days of completion of surveys performed within work areas identified as suitable BNLL habitat. The report shall include the names of the surveyors and qualifications as well as describe survey methods, results, impact avoidance and minimization measures to be implemented. The project owner shall summarize the survey findings and describe any implemented avoidance or minimization measures in the Monthly Compliance Report (MCR), pursuant to Condition of Certification BIO-6.	Monthly	Ongoing - Rincon	N/A	N/A				
Biological Resources	SWITCH BIO-02	The project owner shall submit the resume of the qualified bat biologist at least 15 days prior to initiating bat surveys. The project owner and/or DB shall submit an email to the CPM prior to tree removal notify the CPM if bats are present. The project owner shall submit a final survey report to the CPM within 30 days after tree removal. The project owner shall summarize the survey findings and describe any implemented avoidance or minimization measures in the Monthly Compliance Report (MCR), pursuant to Condition of Certification BIO-6.	Within 30 days after tree removal	N/A	N/A				N/A	
Biological Resources	SWITCH BIO-02	The project owner shall submit the resume of the qualified bat biologist at least 15 days prior to initiating bat surveys. The project owner and/or DB shall submit an email to the CPM prior to tree removal notify the CPM if bats are present. The project owner shall submit a final survey report to the CPM within 30 days after tree removal. The project owner shall summarize the survey findings and describe any implemented avoidance or minimization measures in the Monthly Compliance Report (MCR), pursuant to Condition of Certification BIO-6.	Monthly	N/A	N/A	7/25/2025 9/19/2025			N/A	
Biological Resources	SWITCH BIO-02	The project owner shall submit the resume of the qualified bat biologist at least 15 days prior to initiating bat surveys. The project owner and/or DB shall submit an email to the CPM prior to tree removal notify the CPM if bats are present. The project owner shall submit a final survey report to the CPM within 30 days after tree removal. The project owner shall summarize the survey findings and describe any implemented avoidance or minimization measures in the Monthly Compliance Report (MCR), pursuant to Condition of Certification BIO-6.	15 days prior to starting bat survey	N/A	N/A	9/19/2025			10/22/2025	
Cultural and Tribal Cultural Resources	SWITCH CUL-01	Within 30 days of selection of a CRS, the project owner shall provide a copy of any resume(s) to CEC for review and approval that the CRS meets the Standards.	30 days from selection of a CRS	N/A	N/A	7/25/2025			8/1/2025	
Cultural and Tribal Cultural Resources	SWITCH CUL-02	At least 90 days prior to the start of construction, the project owner shall provide a draft CTCRMMP to CEC for review and approval.	90 days prior to start of construction	N/A	N/A	8/14/2025 9/26/2025			10/15/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Cultural and Tribal Cultural Resources	SWITCH CUL-03	At least 20 days prior to the start of construction, the project owner shall notify CEC that the WEAP has been scheduled and allow for participation of any tribal participants should they have requested so during CEC’s ongoing tribal consultation for the undertaking.	20 days prior to construction	N/A	N/A	10/28/2025			N/A	
Cultural and Tribal Cultural Resources	SWITCH CUL-04	Within 60 days of completion of ground disturbing activities requiring monitoring, the CRS shall provide a monitoring report to the CEC for review and approval, consistent with the CTCRMMP prepared under COC SWITCH CUL-2.	60 days of completion of ground activities	Not Started - Rincon	N/A	N/A				
Cultural and Tribal Cultural Resources	SWITCH CUL-05	Should there be an unanticipated discovery of cultural or tribal cultural resources, the CRS shall comply with state law and any provisions described in the CTCRMMP. The CRS shall notify CEC within 24 hours of the discovery and invite CEC’s participation in the resolution of the find.	within 24 hours of discovery	No Action Needed	N/A	N/A				
Cultural and Tribal Cultural Resources	SWITCH CUL-06	Should human remains be discovered, the CRS shall comply with state law and any provisions described in the AMDP. The CRS shall notify CEC within 24 hours of the discovery and invite CEC’s participation in the resolution of the find.	within 24 hours of discovery	No Action Needed	N/A	N/A				
Geology, Paleontology, and Minerals	SWITCH GEO-01	As described in the CBC (2022) Section 1803.6, the project owner shall submit a written geotechnical report to the DCBO. The project owner shall provide to the CPM copies of the geotechnical investigations and geohazards report, building permit, and any comments by the DCBO at least 60 days prior to grading.	60 days prior to grading	N/A	7/31/2025	8/18/2025			10/6/2025	
Geology, Paleontology, and Minerals	SWITCH GEO-01	As described in the CBC (2022) Section 1803.6, the project owner shall submit a written geotechnical report to the DCBO. The project owner shall provide to the CPM copies of the geotechnical investigations and geohazards report, building permit, and any comments by the DCBO at least 60 days prior to grading.	60 days prior to grading	N/A	N/A	8/18/2025			9/4/2025	
Climate Change and Greenhouse Gas Emissions	SWITCH GHG-01	The Air Quality Construction Mitigation Manager (AQCMM) in Condition of Certification AQ-SC1 shall provide the CPM a Monthly Compliance Report to demonstrate compliance with this condition.	Monthly	Ongoing - EPC	N/A	N/A				
Hazards, Hazardous Materials/Waste, and Wildfire	SWITCH HAZ-01	Prior to construction, a Hazardous Materials Management Plan shall be prepared	Prior to construction	N/A	N/A	9/19/2025			10/22/2025	
Hazards, Hazardous Materials/Waste, and Wildfire	SWITCH HAZ-02	At least 90 days prior to the start of construction, the project owner shall provide to the CPM a copy of letters from the FCFPD detailing resolved comments on the Construction Fire Prevention Plan, the Emergency Action Plan, and Emergency Response Plan. At least 30 days prior to the start of commissioning, the project Operations and Maintenance Safety and Health Program. The project owner shall provide a copy to the CPM of letters from the FCFPD detailing the resolved comments on the Operations Fire Prevention Plan, Fire Protection System Impairment Program, and Emergency Action Plan.	90 days prior to the start of construction	N/A	N/A	9/19/2025 10/20/2025	FCFPD Comments provided on 8/25/2025		10/22/2025	
Transmission Line Safety and Nuisance	SWITCH TLSN-01	At least 30 days before the construction of structures above 200 feet tall, the project owner shall transmit to the CPM a letter confirming compliance with this condition.	30 days before the construction of structures above 200 feet tall	N/A	N/A	9/9/2025	N/A	N/A	9/23/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Visual Resources	SWITCH VIS-01	a. The project owner shall submit an exterior surface coating, color, finish and materials plan to the CPM for approval and simultaneously to the Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase coating, color, finish and materials with a vendor. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. b. If the CPM determines that the exterior surface coating, color, finish, and materials plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. c. The project owner shall notify the CPM that exterior surface coatings, colors, and finishes of all listed buildings, equipment, and structures that has been completed are ready for inspection. With this notification, the applicant shall supply to the CPM one set of color photographs showing the project from the Key Views evaluated for the project certification, and individual color photographs showing the completed exterior surface coatings, colors, finishes, and materials for the following: the clarifiers, control room, cooling tower, maintenance building, thickener, and any other building, equipment, and structure as requested by the CPM. Color photographs may be electronically filed or manually filed on electronic media. d. Exterior surface coatings, colors, finishes, and materials shall be installed/applied (completed) on the exterior surfaces of the large/major buildings, equipment, and structures prior to the start of commercial operation. e. The project owner shall supply a description of the condition (status) of the exterior surface coatings, colors, finishes, and materials for the large/major buildings, equipment, structures, and others as needed for the reporting year in the Annual Compliance Report. The report shall include: 1. The condition of the exterior surfaces of buildings, equipment, and structures at the end of the reporting year. 2. A listing of maintenance activities performed during the reporting year. 3. A tentative time schedule for maintenance activities for the upcoming year.	60 days prior to executing a contract	N/A	N/A	N/A	Director of Planning and Development Services for the County of Fresno			
Solid Waste Management	SWITCH WASTE-01	No less than 30 days prior to the start of site mobilization, the project owner shall submit the Construction Waste Management Plan to the CPM for approval. The Operation Waste Management Plan shall be submitted to the CPM no less than 30 days prior to the start of project operation for approval. The project owner shall submit any required revisions within 20 days of notification by the CPM. In the Annual Compliance Reports, the project owner shall document the actual waste management methods used during the year compared to the planned management methods.	30 days prior to operations	Not Started - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Solid Waste Management	SWITCH WASTE-01	No less than 30 days prior to the start of site mobilization, the project owner shall submit the Construction Waste Management Plan to the CPM for approval. The Operation Waste Management Plan shall be submitted to the CPM no less than 30 days prior to the start of project operation for approval. The project owner shall submit any required revisions within 20 days of notification by the CPM. In the Annual Compliance Reports, the project owner shall document the actual waste management methods used during the year compared to the planned management methods.	Annual	Not Started - EPC	N/A	N/A				
Solid Waste Management	SWITCH WASTE-01	No less than 30 days prior to the start of site mobilization, the project owner shall submit the Construction Waste Management Plan to the CPM for approval. The Operation Waste Management Plan shall be submitted to the CPM no less than 30 days prior to the start of project operation for approval. The project owner shall submit any required revisions within 20 days of notification by the CPM. In the Annual Compliance Reports, the project owner shall document the actual waste management methods used during the year compared to the planned management methods.	30 days prior to the start of site mobilization	N/A	N/A	9/9/2025			10/3/2025	
Solid Waste Management	SWITCH WASTE-01	No less than 30 days prior to the start of site mobilization, the project owner shall submit the Construction Waste Management Plan to the CPM for approval. The Operation Waste Management Plan shall be submitted to the CPM no less than 30 days prior to the start of project operation for approval. The project owner shall submit any required revisions within 20 days of notification by the CPM. In the Annual Compliance Reports, the project owner shall document the actual waste management methods used during the year compared to the planned management methods. The CEC requests that the owner provide copies of all hazardous waste manifests in the Monthly Compliance Reports to document the disposal of hazardous wastes generated during construction (<i>not a component of the original COC requirement</i>)	Monthly	Ongoing - EPC						
Water Resources	SWITCH WATER-01	At least thirty (30) days prior to site mobilization, the project owner shall submit to the Compliance Project Manager (CPM) proof that the construction permit was granted and that a waste discharge identification number (WDID) was issued by the SWRCB. Within ten (10) days of its mailing or receipt, the project owner shall submit to the CPM any correspondence between the project owner and the SWRCB or the Central Valley Regional Water Quality Control Board (CVRWQCB) concerning the CGP. This information shall include the NOI, any updates to the construction SWPPP, and the notice of termination. The project owner shall notify the CPM in writing of any reported non-compliance and include these in the annual compliance report. Any monitoring documentation associated with the SWPPP shall be included in the annual compliance report.	At least thirty (30) days prior to site mobilization	N/A	N/A	10/15/2025	State Water Resources Control Board’s SMARTS		10/22/2025	
Water Resources	SWITCH WATER-02	At least thirty (30) days prior to commencement of project operation, the project owner shall submit a copy of the Operation DESCP to the CPM for review and approval. The project owner shall notify the CPM in writing of any reported non-compliance instances and include these in the annual compliance report. Any monitoring documentation associated with the DESCP shall be included in the annual compliance report.	At least 30 days prior to commencement of project operation	Not Started - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Transmission Line Safety and Nuisance	TLSN-01	At least 30 days before starting construction of the transmission lines or related structures and facilities, the project owner shall submit to the compliance project manager (CPM) a letter signed by a California-registered electrical engineer affirming that the lines will be constructed according to the requirements stated in the condition.	30 days prior to construction of the transmission lines or related structures/facilities	Completed	N/A	1/15/2026			N/A	
Transmission Line Safety and Nuisance	TLSN-02	During the first five years of plant operation, the project owner shall provide a summary of inspection results, and any fire prevention activities carried out along the proposed route and provide such summaries in the Annual Compliance Report on transmission line safety and nuisance-related requirements.	During first five years of operation	Not Started - Intersect	N/A	N/A				
Transmission Line Safety and Nuisance	TLSN-03	At least 30 days before the lines are energized, the project owner shall transmit to the CPM a letter confirming compliance with this condition.	30 days before the lines are energized	Not Started - EPC	N/A	N/A				
Transmission Line Safety and Nuisance	TLSN-04	The project owner shall file copies of the pre- and post-energizing measurements with the CPM within 60 days after the measurements are completed.	Within 60 days of completing measurements	Not Started - EPC	N/A	N/A				
Transmission Line Safety and Nuisance	TLSN-05	At least 30 days before the construction of structures above 200 feet tall, the project owner shall transmit to the CPM a letter confirming compliance with this condition.	30 days before construction of structures above 200 feet tall	Completed	N/A	12/15/2025			N/A	
Transportation	TRANS-01	The project owner shall retain copies of permits and supporting documents on-site for CPM inspection if requested.	Prior to construction	Ongoing	N/A	10/3/2025			N/A	
Transportation	TRANS-02	The project owner shall include in its Monthly Compliance Reports (MCR's) copies of all permits/licenses acquired by the project owner and/or subcontractors concerning the transport of hazardous substances.	Monthly	Ongoing	N/A	10/3/2025	CHP, Caltrans		N/A	
Transportation	TRANS-03	At least 60 calendar days prior to the start of construction, the project owner shall submit the CMP to Caltrans and Fresno County for review and comment and to the compliance project manager (CPM) for review and approval. The project owner shall also provide the CPM with a copy of the transmittal letter to Caltrans and Fresno County requesting review and comment. At least 30 calendar days prior to the start of construction, the project owner shall provide copies of any comment letters received from Caltrans or Fresno County, or any other interested agencies, along with any changes to the CMP, for CPM review and approval. After CPM review and approval, the project owner shall provide completed copies of the final CMP to Caltrans and Fresno County and any other interested agencies, sending copies of the correspondence to the CPM.	30 days prior to the start of construction	CEC Approved	N/A	10/23/2025 - BAAH 11/11/2025 - Darden 11/18/2025 - PV/BESS 12/10/2025	Fresno County and Caltrans		BAAH - 10/24/2025 Darden - 04/21/2026	10/20/2025 - Caltrans 10/22/2025 - County 11/7/2025 - Caltrans
Transportation	TRANS-03	At least 60 calendar days prior to the start of construction, the project owner shall submit the CMP to Caltrans and Fresno County for review and comment and to the compliance project manager (CPM) for review and approval. The project owner shall also provide the CPM with a copy of the transmittal letter to Caltrans and Fresno County requesting review and comment. At least 30 calendar days prior to the start of construction, the project owner shall provide copies of any comment letters received from Caltrans or Fresno County, or any other interested agencies, along with any changes to the CMP, for CPM review and approval. After CPM review and approval, the project owner shall provide completed copies of the final CMP to Caltrans and Fresno County and any other interested agencies, sending copies of the correspondence to the CPM.	60 days prior to the start of construction	Submitted - CEC Review	N/A	9/25/2025 10/8/2025	Caltrans and Fresno County	10/9/2025	BAAH - 10/24/2025 Darden - 04/21/2026	10/20/2025 - Caltrans 10/22/2025 - County

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Transmission System Engineering	TSE-01	Before the start of construction, the project owner shall submit the schedule, a Master Drawing List, and a Master Specifications List to the DCBO and to the CPM. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment (see a list of major equipment in Table 1: Major Equipment List below). Additions and deletions shall be made to the table only with CPM and DCBO approval. The project owner shall provide schedule updates in the Monthly Compliance Report.	Before the start of construction	DCBO Approved	8/8/2025 10/23/2025	8/15/2025 10/29/2025			N/A - DCBO Approved 10/29/2025	
Transmission System Engineering	TSE-01	Before the start of construction, the project owner shall submit the schedule, a Master Drawing List, and a Master Specifications List to the DCBO and to the CPM. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment (see a list of major equipment in Table 1: Major Equipment List below). Additions and deletions shall be made to the table only with CPM and DCBO approval. The project owner shall provide schedule updates in the Monthly Compliance Report.	in the MCR	In Progress - EPC	N/A	N/A			Ongoing MCR	
Transmission System Engineering	TSE-02	Before the start of rough grading, the project owner shall submit the names, qualifications, and registration numbers of all the responsible engineers assigned to the project to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO’s approvals of the engineers within five days of the approval. Suppose the designated responsible engineer is subsequently reassigned or replaced. In that case, the project owner has five days to submit the newly assigned engineer's name, qualifications, and registration number to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO’s approval of the new engineer within five days of the approval.	5 days from reassigning or replacing	No Action Needed	N/A	N/A				
Transmission System Engineering	TSE-02	Before the start of rough grading, the project owner shall submit the names, qualifications, and registration numbers of all the responsible engineers assigned to the project to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO’s approvals of the engineers within five days of the approval. Suppose the designated responsible engineer is subsequently reassigned or replaced. In that case, the project owner has five days to submit the newly assigned engineer's name, qualifications, and registration number to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO’s approval of the new engineer within five days of the approval.	Before the start of rough grading	DCBO Approved	9/10/2025 9/30/2025	10/6/2025			N/A - DCBO Approved 10/6/2025	
Transmission System Engineering	TSE-02	Before the start of rough grading, the project owner shall submit the names, qualifications, and registration numbers of all the responsible engineers assigned to the project to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO’s approvals of the engineers within five days of the approval. Suppose the designated responsible engineer is subsequently reassigned or replaced. In that case, the project owner has five days to submit the newly assigned engineer's name, qualifications, and registration number to the DCBO for review and approval. The project owner shall notify the CPM of the DCBO’s approval of the new engineer within five days of the approval.	5 days from the approval	Completed	N/A	10/6/2025			N/A - DCBO Approved 10/6/2025	
Transmission System Engineering	TSE-03	Before the start of each increment of construction, the project owner shall submit to the DCBO for review and approval the final design plans, specifications, and calculations for equipment and systems of the power plant switchyard, outlet line, and termination, including a copy of the signed and stamped statement from the responsible electrical engineer verifying compliance with all applicable LORS, and send the CPM a copy of the transmittal letter in the next monthly compliance report.	Before the start of each increment of construction	In Progress - Addressing DCBO Comments	10/1/2025	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Transmission System Engineering	TSE-03	Before the start of each increment of construction, the project owner shall submit to the DCBO for review and approval the final design plans, specifications, and calculations for equipment and systems of the power plant switchyard, outlet line, and termination, including a copy of the signed and stamped statement from the responsible electrical engineer verifying compliance with all applicable LORS, and send the CPM a copy of the transmittal letter in the next monthly compliance report.	Before the start of each increment of construction	In Progress - EPC	N/A	N/A				
Transmission System Engineering	TSE-04	Before the start of construction or start of modification of transmission facilities, the project owner shall submit to the DCBO for approval: a. Design drawings, specifications, and calculations conforming with CPUC General Order 95 or National Electric Safety Code (NESC); Title 8 of the California Code and Regulations (Title 8); Articles 35, 36, and 37 of the High Voltage Electric Safety Orders, National Electric Code (NEC) and related industry standards, for the poles/towers, foundations, anchor bolts, conductors, grounding systems, and major switchyard equipment. b. For each element of the transmission facilities identified above, the submittal package to the DCBO shall contain the design criteria, a discussion of the calculation method(s), a sample calculation based on “worst case conditions” ¹ and a statement signed and sealed by the registered engineer in responsible charge, or other acceptable alternative verification, that the transmission element(s) will conform with CPUC General Order 95 or National Electric Safety Code (NESC); Title 8 of the California Code and Regulations (Title 8); Articles 35, 36 and 37 of the High Voltage Electric Safety Orders, PG&E standards, National Electric Code (NEC), and related industry standards. c. Electrical one-line diagrams signed and sealed by the registered professional electrical engineer in charge, a route map, and an engineering description of the equipment and configurations covered by requirements TSE-5 a through f. d. The Generator Special Facilities Agreement shall be provided concurrently to the CPM and DCBO. The project owner shall identify and justify the substitution of equipment and substation configurations for DCBO and CPM approval. e. Any changes or updates to the executed LGIA signed by the PG&E and the project owner. f. Before the construction of any project modification requiring approval of the PG&E, provide the interconnection approval to the CPM. Interconnectional approval for modification of existing facilities can be in the form of an approved Material Modification or approval of the proposed changes to the project and the existing interconnection facilities. Within 15 days after the cessation of construction, the project owner shall provide a statement to the CPM from the registered engineer in responsible charge (signed and sealed) that the switchyard and transmission facilities conform to the abovelisted requirements.	Before the start of construction or start of modification of transmission facilities	Submitted - DCBO Review	8/13/2025 (60% design) 3/17/2026	4/7/2026		4/7/2026		
Transmission System Engineering	TSE-05	The project owner shall provide copies of the California ISO letter to the CPM when it is sent to the California ISO one week prior to initial synchronization with the grid. The project owner shall contact the California ISO Outage Coordination Department, Monday through Friday, between the hours of 0700 and 1530 at (916) 351-2300 at least one business day prior to synchronizing the facility with the grid for testing. A report of conversation with the California ISO shall be provided electronically to the CPM one day before synchronizing the facility with the California transmission system for the first time.	one week prior to initial synchronization with the grid	Not Started - EPC/IP	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Transmission System Engineering	TSE-05	The project owner shall provide copies of the California ISO letter to the CPM when it is sent to the California ISO one week prior to initial synchronization with the grid. The project owner shall contact the California ISO Outage Coordination Department, Monday through Friday, between the hours of 0700 and 1530 at (916) 351-2300 at least one business day prior to synchronizing the facility with the grid for testing. A report of conversation with the California ISO shall be provided electronically to the CPM one day before synchronizing the facility with the California transmission system for the first time.	one business day prior to synchronizing the facility with the grid for testing	Not Started - EPC/IP	N/A	N/A				
Transmission System Engineering	TSE-05	The project owner shall provide copies of the California ISO letter to the CPM when it is sent to the California ISO one week prior to initial synchronization with the grid. The project owner shall contact the California ISO Outage Coordination Department, Monday through Friday, between the hours of 0700 and 1530 at (916) 351-2300 at least one business day prior to synchronizing the facility with the grid for testing. A report of conversation with the California ISO shall be provided electronically to the CPM one day before synchronizing the facility with the California transmission system for the first time.	one business day prior to synchronizing the facility with the California transmission system for the first time	Not Started - EPC/IP	N/A	N/A				
Transmission System Engineering	TSE-06	Within 60 days after the first synchronization of the project, the project owner shall transmit to the CPM and DCBO: a. “As built” engineering description(s) and one-line drawings of the electrical portion of the facilities signed and sealed by the registered electrical engineer in charge. A statement attesting to conformance with CPUC GO-95 or NESC, Title 8, California Code of Regulations, Articles 35, 36, and 37 of the “High Voltage Electric Safety Orders,” and applicable interconnection standards, NEC, related industry standards. b. An “as built” engineering description of the transmission facilities' mechanical, structural, and civil portion signed and sealed by the registered engineer in responsible charge or acceptable alternative verification. “As built,” drawings of the electrical, mechanical, structural, and civil portion of the transmission facilities shall be maintained at the power plant and made available, if requested, for CPM audit as outlined in the “Compliance Monitoring Plan.”	Within 60 days after the first synchronization	Not Started - EPC	N/A	N/A				
Visual Resources	VIS-01	... e. The project owner shall supply a description of the condition (status) of the exterior surface coatings, colors, finishes, and materials for the large/major buildings, equipment, structures, and others as needed for the reporting year in the Annual Compliance Report. The report shall include: 1. The condition of the exterior surfaces of buildings, equipment, and structures at the end of the reporting year. 2. A listing of maintenance activities performed during the reporting year. 3. A tentative time schedule for maintenance activities for the upcoming year.	Annual	In Progress - Rincon	N/A	N/A	Director of Planning and Development Services for the County of Fresno			

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Visual Resources	VIS-01	a. The project owner shall submit an exterior surface coating, color, finish and materials plan to the CPM for approval and simultaneously to the Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase coating, color, finish and materials with a vendor. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. b. If the CPM determines that the exterior surface coating, color, finish, and materials plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. c. The project owner shall notify the CPM that exterior surface coatings, colors, and finishes of all listed buildings, equipment, and structures that has been completed are ready for inspection. With this notification, the applicant shall supply to the CPM one set of color photographs showing the project from the Key Views evaluated for the project certification, and individual color photographs showing the completed exterior surface coatings, colors, finishes, and materials for the following: the clarifiers, control room, cooling tower, maintenance building, thickener, and any other building, equipment, and structure as requested by the CPM. Color photographs may be electronically filed or manually filed on electronic media. d. Exterior surface coatings, colors, finishes, and materials shall be installed/applied (completed) on the exterior surfaces of the large/major buildings, equipment, and structures prior to the start of commercial operation. e. The project owner shall supply a description of the condition (status) of the exterior surface coatings, colors, finishes, and materials for the large/major buildings, equipment, structures, and others as needed for the reporting year in the Annual Compliance Report. The report shall include: 1. The condition of the exterior surfaces of buildings, equipment, and structures at the end of the reporting year. 2. A listing of maintenance activities performed during the reporting year. 3. A tentative time schedule for maintenance activities for the upcoming year.	60 days prior to executing a contract to purchase coating, color, finish and materials with a vendor	Submitted - CEC Review	N/A	10/21/2025	Director of Planning and Development Services for the County of Fresno	2/20/2026		

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Visual Resources	VIS-01	a. The project owner shall submit an exterior surface coating, color, finish and materials plan to the CPM for approval and simultaneously to the Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase coating, color, finish and materials with a vendor. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. b. If the CPM determines that the exterior surface coating, color, finish, and materials plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. c. The project owner shall notify the CPM that exterior surface coatings, colors, and finishes of all listed buildings, equipment, and structures that has been completed are ready for inspection. With this notification, the applicant shall supply to the CPM one set of color photographs showing the project from the Key Views evaluated for the project certification, and individual color photographs showing the completed exterior surface coatings, colors, finishes, and materials for the following: the clarifiers, control room, cooling tower, maintenance building, thickener, and any other building, equipment, and structure as requested by the CPM. Color photographs may be electronically filed or manually filed on electronic media. d. Exterior surface coatings, colors, finishes, and materials shall be installed/applied (completed) on the exterior surfaces of the large/major buildings, equipment, and structures prior to the start of commercial operation. e. The project owner shall supply a description of the condition (status) of the exterior surface coatings, colors, finishes, and materials for the large/major buildings, equipment, structures, and others as needed for the reporting year in the Annual Compliance Report. The report shall include: 1. The condition of the exterior surfaces of buildings, equipment, and structures at the end of the reporting year. 2. A listing of maintenance activities performed during the reporting year. 3. A tentative time schedule for maintenance activities for the upcoming year.	Following completion of exterior surface coatings, colors, and finishings on applicable buildings, equipment, etc.	In Progress - IP	N/A	N/A	Director of Planning and Development Services for the County of Fresno			

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Visual Resources	VIS-02	a. The project owner shall submit a light pollution control plan to the CPM for approval and simultaneously to the Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase permanent outdoor luminaires for the project. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. b. If the CPM determines the light pollution control plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. c. The project owner shall notify the CPM when the installation of the luminaires has been completed and are ready for inspection. After inspection if the CPM requires a modification to a luminaire(s) (e.g., design, installation, location), the project owner shall have 30 days after receiving the notification to complete the modification and request a follow-up inspection. d. If a light and glare complaint is filed with the project owner within 48 hours of receiving the complaint, the project owner shall supply the CPM with a completed complaint resolution form report as specified in the Compliance Conditions, a proposal to resolve the complaint and time schedule for resolution. The project owner shall notify the CPM within 48 hours after completing/resolving the complaint.	60 days prior to executing a contract to purchase permanent outdoor luminaires for the project; inspection after installation	No Action Needed	N/A	N/A	Director of Planning and Development Services for the County of Fresno			
Visual Resources	VIS-02	a. The project owner shall submit a light pollution control plan to the CPM for approval and simultaneously to the Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase permanent outdoor luminaires for the project. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. b. If the CPM determines the light pollution control plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. c. The project owner shall notify the CPM when the installation of the luminaires has been completed and are ready for inspection. After inspection if the CPM requires a modification to a luminaire(s) (e.g., design, installation, location), the project owner shall have 30 days after receiving the notification to complete the modification and request a follow-up inspection. d. If a light and glare complaint is filed with the project owner within 48 hours of receiving the complaint, the project owner shall supply the CPM with a completed complaint resolution form report as specified in the Compliance Conditions, a proposal to resolve the complaint and time schedule for resolution. The project owner shall notify the CPM within 48 hours after completing/resolving the complaint.	60 days prior to executing a contract to purchase permanent outdoor luminaires for the project; inspection after installation	Submitted - CEC Review	N/A	9/26/2025 - BAAH 10/8/2025 - Darden	Director of Planning and Development Services for the County of Fresno	2/20/2026	BAAH - 10/24/2025	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTF Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Visual Resources	VIS-02	a. The project owner shall submit a light pollution control plan to the CPM for approval and simultaneously to the Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase permanent outdoor luminaires for the project. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. b. If the CPM determines the light pollution control plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. c. The project owner shall notify the CPM when the installation of the luminaires has been completed and are ready for inspection. After inspection if the CPM requires a modification to a luminaire(s) (e.g., design, installation, location), the project owner shall have 30 days after receiving the notification to complete the modification and request a follow-up inspection. d. If a light and glare complaint is filed with the project owner within 48 hours of receiving the complaint, the project owner shall supply the CPM with a completed complaint resolution form report as specified in the Compliance Conditions, a proposal to resolve the complaint and time schedule for resolution. The project owner shall notify the CPM within 48 hours after completing/resolving the complaint.	When the installation of the luminaires has been completed and are ready for inspection.	In Progress - EPC	N/A	N/A	Director of Planning and Development Services for the County of Fresno			
Visual Resources	VIS-03	a. The project owner shall submit a plan locating the support structures adjacent to I-5 for approval to the CPM, Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to siting the structures. b. The project owner shall submit an exterior surface coating, color, finish and materials plan for the utility structures crossing I-5 for approval to the CPM, Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase coating, color, finish and materials with a vendor. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. c. If the CPM determines that the exterior surface coating, color, finish, and materials plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. d. The project owner shall notify the CPM that exterior surface coatings, colors, and finishes of the structures has been completed are ready for inspection. With this notification, the applicant shall supply to the CPM one set of color photographs showing the project from the Key Views evaluated for the project certification, and individual color photographs showing the completed exterior surface coatings, colors, finishes, and materials as requested by the CPM. Color photographs may be electronically filed or manually filed on electronic media. e. Exterior surface coatings, colors, finishes, and materials shall be installed/applied (completed) on the exterior surfaces of the structures prior to the start of commercial operation.	60 days prior to siting the structures	Submitted - CEC Review	N/A	10/22/2025	Director of Planning and Development Services for the County of Fresno	2/20/2026		

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Visual Resources	VIS-03	a. The project owner shall submit a plan locating the support structures adjacent to I-5 for approval to the CPM, Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to siting the structures. b. The project owner shall submit an exterior surface coating, color, finish and materials plan for the utility structures crossing I-5 for approval to the CPM, Director of Planning and Development Services for the County of Fresno for review and comment sixty (60) days prior to executing a contract to purchase coating, color, finish and materials with a vendor. The CPM shall provide the Director of Planning and Development Services at least 30 days to review the plan and provide comments to the applicant and the CPM. c. If the CPM determines that the exterior surface coating, color, finish, and materials plan requires a revision, the project owner shall provide to the CPM a plan with the specified revision(s) for approval by the CPM before any action or activity with the vendor is executed. Any revision to the plan must be approved by the CPM. d. The project owner shall notify the CPM that exterior surface coatings, colors, and finishes of the structures has been completed are ready for inspection. With this notification, the applicant shall supply to the CPM one set of color photographs showing the project from the Key Views evaluated for the project certification, and individual color photographs showing the completed exterior surface coatings, colors, finishes, and materials as requested by the CPM. Color photographs may be electronically filed or manually filed on electronic media. e. Exterior surface coatings, colors, finishes, and materials shall be installed/applied (completed) on the exterior surfaces of the structures prior to the start of commercial operation.	Following completion of exterior surface coatings, colors, and finishings on applicable buildings, equipment, etc.	In Progress - EPC	N/A	N/A	Director of Planning and Development Services for the County of Fresno			
Solid Waste Management	Waste-01	No less than 30 days prior to the start of site mobilization, the project owner shall submit the Construction Waste Management Plan to the CPM for approval. The Operation Waste Management Plan shall be submitted to the CPM no less than 30 days prior to the start of project operation for approval. The project owner shall submit any required revisions within 20 days of notification by the CPM. In the Annual Compliance Reports, the project owner shall document the actual waste management methods used during the year compared to the planned management methods.	30 days prior to the start of operation	Not Started - EPC	N/A	N/A				
Solid Waste Management	Waste-01	No less than 30 days prior to the start of site mobilization, the project owner shall submit the Construction Waste Management Plan to the CPM for approval. The Operation Waste Management Plan shall be submitted to the CPM no less than 30 days prior to the start of project operation for approval. The project owner shall submit any required revisions within 20 days of notification by the CPM. In the Annual Compliance Reports, the project owner shall document the actual waste management methods used during the year compared to the planned management methods.	30 days prior to the start of site mobilization	Ongoing - EPC	N/A	N/A				
Solid Waste Management	Waste-01	No less than 30 days prior to the start of site mobilization, the project owner shall submit the Construction Waste Management Plan to the CPM for approval. The Operation Waste Management Plan shall be submitted to the CPM no less than 30 days prior to the start of project operation for approval. The project owner shall submit any required revisions within 20 days of notification by the CPM. In the Annual Compliance Reports, the project owner shall document the actual waste management methods used during the year compared to the planned management methods.	30 days prior to the start of site mobilization	CEC Approved	N/A	10/31/2025 12/10/2025 1/30/2026			4/21/2026	

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Water Resources	WATER-01	At least thirty (30) days prior to site mobilization, the project owner shall submit to the Compliance Project Manager (CPM) proof that the construction permit was granted and that a waste discharge identification number (WDID) was issued by the SWRCB. Within ten (10) days of its mailing or receipt, the project owner shall submit to the CPM any correspondence between the project owner and the SWRCB or the Central Valley Regional Water Quality Control Board (CVRWQCB) concerning the CGP. This information shall include the NOI, any updates to the construction SWPPP, and the notice of termination. The project owner shall notify the CPM in writing of any reported non-compliance and include these in the annual compliance report. Any monitoring documentation associated with the SWPPP shall be included in the annual compliance report.	30 days prior to site mobilization	Completed	N/A	11/19/2025			N/A	
Water Resources	WATER-02	At least thirty (30) days prior to commencement of project operation, the project owner shall submit a copy of the Operation DESCP to the CPM for review and approval. The project owner shall notify the CPM in writing of any reported non-compliance instances and include these in the annual compliance report. Any monitoring documentation associated with the DESCP shall be included in the annual compliance report.	30 days prior to operation	Not Started - EPC	N/A	N/A				
Water Resources	WATER-03	No later than thirty (30) days prior to start of construction, the project owner shall submit a plan to install underground wiring to PV panels in compliance with Ordinance 15.48.080 (A)(2)(a) to the CPM for review and approval and to Fresno County for review.	30 days prior to construction	Submitted - CEC Review	N/A	10/27/2025 1/12/2026	Fresno County	1/8/2026		1/9/2026
Water Resources	WATER-04	No later than ninety (90) days prior to project operation, the project owner shall submit to the CPM evidence that the septic system design has been reviewed and commented on by FCPWPD and also has been approved by the chief building official (CBO). No later than 60 days prior to project operation, the project owner shall submit the operations and maintenance manual to the FCPWPD for review and comment. No later than 30 days prior to project operation, the project owner shall submit the operations and maintenance manual to the CPM for review and approval. The submittal shall include copies of any agency comments the project owner has received. The wastewater system shall be monitored following either the general standards adopted in SWRCB’s OWTS regulations or the procedures outlined in the CPM-approved operations and maintenance manual. Any testing results or correspondence exchanged between the project owner and the California Department of Health Services or the SCEHD during operations shall be provided to the CPM in the annual compliance report.	90 days prior to operation	Not Started - EPC	N/A	N/A				
Water Resources	WATER-05	At a frequency determined by the CPM, the project owner shall keep the CPM apprised of all aspects of production well installation. The project owner shall provide the CPM with all information required for to obtain a FCDPH well installation permit. The project owner shall file a well completion report to DWR for the extraction well. Any testing results or correspondence exchanged between the project owner and the California Department of Health Services or the FCDPH during operations shall be provided to the CPM in the annual compliance report. All results and diagrams associated with groundwater production well installation shall be included in the annual compliance report.	Prior to well construction	In Progress - EPC/IP	N/A	N/A				
Water Resources	WATER-06	During project construction, the monthly compliance report shall include a summary of monthly water use. The project’s annual compliance report shall include a monthly and annual summary of water use identifying construction or operations and water source.	N/A	Ongoing - EPC	N/A	N/A				
Water Resources	WATER-06	During project construction, the monthly compliance report shall include a summary of monthly water use. The project’s annual compliance report shall include a monthly and annual summary of water use identifying construction or operations and water source.	N/A	Ongoing - EPC	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Worker Safety and Fire Protection	Worker Safety-01	At least 90 days prior to the start of construction, the project owner shall submit to the CPM for review and approval a copy of the Project Construction and Safety and Health Program. The project owner shall provide to the CPM a copy of letters from the FCFPD detailing resolved comments on the Construction Fire Prevention Plan, the Emergency Action Plan, and Emergency Response Plan.	At least 90 days prior to the start of construction	CEC Approved	N/A	8/22/2025 10/20/2025 - BAAH 10/24/2025 - BAAH 11/4/2025 - Darden 11/21/2025- Darden 1/21/2026	FCFPD	12/11/2025	BAAH - 10/24/2025 Darden - 04/21/2026	1/21/2026
Worker Safety and Fire Protection	Worker Safety-02	At least 30 days prior to the start of commissioning, the project owner shall submit to the CPM for review and approval a copy of the Project Operations and Maintenance Safety and Health Program. The project owner shall provide a copy to the CPM of letters from the FCFPD detailing the resolved comments on the Operations Fire Prevention Plan, Fire Protection System Impairment Program, and Emergency Action Plan.	At least 30 days prior to the start of commissioning	Not Started - EPC	N/A	N/A				
Worker Safety and Fire Protection	Worker Safety-03	At least 30 days prior to the start of site mobilization, the project owner shall submit to the CPM the name and contact information of the CSS. The contact information of any replacement CSS shall be submitted to CPM within one business day. The CSS shall submit in the Monthly Compliance Report (MCR) a monthly safety inspection report.	30 days prior to the start of site mobilization	CEC Approved	N/A	7/21/2025			8/15/2025	
Worker Safety and Fire Protection	Worker Safety-03	At least 30 days prior to the start of site mobilization, the project owner shall submit to the CPM the name and contact information of the CSS. The contact information of any replacement CSS shall be submitted to CPM within one business day. The CSS shall submit in the Monthly Compliance Report (MCR) a monthly safety inspection report.	in the MCR	Ongoing - EPC	N/A	N/A				
Worker Safety and Fire Protection	Worker Safety-04	At least 60 days prior to the start of construction, the project owner shall provide proof of its agreement to fund the Safety Monitor services to the CPM for review and approval.	At least 60 days prior to the start of construction	CEC Approved	N/A	10/15/2025			11/18/2025	
Worker Safety and Fire Protection	Worker Safety-05	At least 60 days prior to the start of construction, the project owner shall submit the SAP to the CPM for review and approval. At least 30 days prior to the planned use of the well water, the project owner shall submit the laboratory findings to the CPM for review and approval of the use of the well water.	At least 30 days prior to planned use of the well water	Submitted - CEC Review	N/A	12/18/2025 1/29/2026				
Worker Safety and Fire Protection	Worker Safety-05	At least 60 days prior to the start of construction, the project owner shall submit the SAP to the CPM for review and approval. At least 30 days prior to the planned use of the well water, the project owner shall submit the laboratory findings to the CPM for review and approval of the use of the well water.	At least 60 days prior to the start of construction (SAP)	Submitted - CEC Review	N/A	11/5/2025 11/24/2025				
Worker Safety and Fire Protection	Worker Safety-06	At least 60 days prior to the start of construction, the project owner shall provide the procedure(s) with the standard checklist to the CPM for review and approval.	At least 60 days prior to the start of construction	CEC Approved	N/A	9/9/2025 11/4/2025			11/17/2025	
Worker Safety and Fire Protection	Worker Safety-07	At least 60 days prior to the start of construction, the project owner shall provide all the information required above (with the exception of k) to the FCFPD for review and comment, to the CPM for review and approval, and to the DCBO for plan check approval and construction inspection. Within 10 days of an incident at the BESS facility (including but not limited to fire, malfunction, leak, or thermal runaway of any cell, module, or unit) the project owner shall notify the CPM that a Root Cause Analysis (RCA) is being prepared. The project owner shall work with the CPM to determine a submission date for the completed RCA. The RCA shall be submitted to the FCFPD for review and comment, and to the CPM for review and approval.	Within 10 days of an incident at the BESS facility (including but not limited to fire, malfunction, leak, or thermal runaway of any cell, module, or unit	No Action Needed	N/A	N/A				

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Worker Safety and Fire Protection	Worker Safety-07	At least 60 days prior to the start of construction, the project owner shall provide all the information required above (with the exception of k) to the FCFPD for review and comment, to the CPM for review and approval, and to the DCBO for plan check approval and construction inspection. Within 10 days of an incident at the BESS facility (including but not limited to fire, malfunction, leak, or thermal runaway of any cell, module, or unit) the project owner shall notify the CPM that a Root Cause Analysis (RCA) is being prepared. The project owner shall work with the CPM to determine a submission date for the completed RCA. The RCA shall be submitted to the FCFPD for review and comment, and to the CPM for review and approval.	At least 60 days prior to the start of construction	Submitted - DCBO Review	3/5/2026	10/17/2025 3/11/2026	FCFPD	3/9/2026		
Worker Safety and Fire Protection	Worker Safety-08	The project owner shall ensure that the project adheres to all applicable provisions of NFPA 855. At least 90 days prior to the start of construction of the BESS, the project owner shall provide all system specifications and design drawings to the FCFPD for review and comment, to the CPM for review and approval, and to the DCBO for plan check approval and construction inspection.	At least 90 days prior to the start of construction of the BESS	Submitted - DCBO Review	2/20/2026	3/3/2026	FCFPCD	3/3/2026		
Worker Safety and Fire Protection	Worker Safety-09	The project owner shall ensure that the project adheres to all applicable provisions of NFPA 850. At least 90 days prior to the start of construction of the fire protection system, the project owner shall provide all fire protection system specifications and drawings to the FCFPD for review and comment, to the CPM for review and approval, and to the DCBO for plan check approval and construction inspection.	At least 90 days prior to the start of construction of the fire protection system	In Progress - Addressing DCBO Comments	10/31/2025	N/A	FCFPCD			
Worker Safety and Fire Protection	Worker Safety-10	At least 30 days prior to the start of site mobilization, the project owner shall submit to the CPM proof that a portable AED is available to be made available on site as soon as physically possible along with a copy of the training and maintenance program for review and approval.	At least 30 days prior to the start of site mobilization	CEC Approved	N/A	9/19/2025 11/4/2025			BAAH - 10/22/2025 Darden - 11/17/2025	
Worker Safety and Fire Protection	Worker Safety-11	At least 60 days prior to the commencement of site mobilization, the VF Prevention and Response Plan shall be provided to the CPM for review and approval.	At least 60 days prior to site mobilization	CEC Approved	N/A	8/20/2025 9/26/2025 10/02/2025 10/22/2025			BAAH - 10/22/2025 Darden - 11/17/2025	
Worker Safety and Fire Protection	Worker Safety-12	a. No more than 30 days after certification, the project owner shall provide to the CPM for review and approval the schedule for reaching agreement on funding prior to site mobilization. b. At least 30 days prior to the start of site mobilization, or as soon as practicable thereafter, the project owner shall provide to the CPM for review and approval either: 1. A copy of the agreement with the FCFPD or 2. A copy of the arbiter’s decision. c. If the agreement or arbiter’s decision submitted 30 days prior to site mobilization is limited to funding during construction, then, provided the property tax exclusion still applies, the project owner must provide to the CPM for review and approval an agreement or arbiter’s decision to cover the remaining period of the project at least 30 days prior to the completion of construction. d. Upon approval of the agreement or arbiter’s decision by the CPM, the project owner shall commence payment of the initial funding and annual funding. If the agreement or arbiter's decision is provided later than 30 days prior to the start of site mobilization, funding will be made retroactive to cover from the start date of site mobilization.	30 days after certification	CEC Approved	N/A	7/11/2025		11/18/2025		

Technical Resource	Cond. #	Verification/Action/Submittal	Timing (prior to)	FNTP Compliance Status for CPM	Submitted to DCBO	Submitted to CPM	Other Agencies to Submit to?	Date Submitted to Other Agencies	Date Approved by CPM	Date Approved by Other Agencies
Worker Safety and Fire Protection	Worker Safety-12	a. No more than 30 days after certification, the project owner shall provide to the CPM for review and approval the schedule for reaching agreement on funding prior to site mobilization. b. At least 30 days prior to the start of site mobilization, or as soon as practicable thereafter, the project owner shall provide to the CPM for review and approval either: 1. A copy of the agreement with the FCFPD or 2. A copy of the arbiter’s decision. c. If the agreement or arbiter’s decision submitted 30 days prior to site mobilization is limited to funding during construction, then, provided the property tax exclusion still applies, the project owner must provide to the CPM for review and approval an agreement or arbiter’s decision to cover the remaining period of the project at least 30 days prior to the completion of construction. d. Upon approval of the agreement or arbiter’s decision by the CPM, the project owner shall commence payment of the initial funding and annual funding. If the agreement or arbiter's decision is provided later than 30 days prior to the start of site mobilization, funding will be made retroactive to cover from the start date of site mobilization.	At least 30 days prior to the start of site mobilization	CEC Approved	N/A	10/21/2025			4/21/2026	

Appendix E

DCBO Approval of Drainage Structures, Grading Plan, Erosion and Sediment Control Plan,
Soils Report (CIVIL-1)

June 8, 2026



Mr. Joe Douglas
Compliance Project Manager
California Energy Commission
Energy Facilities Siting Division
1516 Ninth Street, MS 2000
Sacramento, CA 95814-5512

Darden Clean Energy Project (DCEP) – ACCEPTANCE
WC³ Permit No.: CIVIL-1-01-REV

Re: Plan Review: Drainage Structures, Grading Plan, Erosion and Sediment Control Plan, Soils Report Rev
Address: Darden Clean Energy Project, Fresno County, CA

Dear Mr. Douglas:

On behalf of the California Energy Commission, West Coast Code Consultants, Inc. (WC³) has reviewed the documents, listed on the attached sheet, as they relate to the stated subject above. Documents appear to be in compliance with Condition CIVIL-1, established by the California Energy Commission (CEC) Commission Decision (23-OPT-02), dated June 2025, and have been accepted as part of the construction documents.

Accepted submittals have been stamped and signed by WC³ and uploaded to the WC³ project portal. Any changes to the design professionals, in their area of responsible charge, must be submitted to the project portal for review and approval before said change takes effect.

Sincerely,

West Coast Code Consultants, Inc. (WC³)

Giyan A. Senaratne, S.E., P.E., LEED Ap.
Delegate Chief Building Official

Cc: Olivia Gastaldo, CEC Compliance Manager, Intersect Power (ogastaldo@ipxpower.com)

DOCUMENTS APPROVED FOR:

CIVIL-1-01-REV-IFC-Drainage Structures, Grading Plan, Erosion and Sediment Control Plan, Soils Report

File Type / Description	File Name
Plans	DARDEN III&IV CIVIL RUNNING SET IFC REV2 2026-02-26.pdf
Plans	DARDEN I&II CIVIL RUNNING SET IFC REV2 2026-02-20 REV.pdf
Plans	DARI-CV-C702 CIVIL DETAILS.pdf

Appendix F

DCBO Approval of Electrical Design Package and Studies (ELEC-1)

June 16, 2026



Mr. Joe Douglas
Compliance Project Manager
California Energy Commission
Energy Facilities Siting Division
1516 Ninth Street, MS 2000
Sacramento, CA 95814-5512

Darden Clean Energy Project (DCEP) – ACCEPTANCE
WC³ Permit No.: ELEC-1-02-REV

Re: Plan Review: IFC Darden I&II PV Electrical Design Package and Studies Rev
Address: Darden Clean Energy Project, Fresno County, CA

Dear Mr. Douglas:

On behalf of the California Energy Commission, West Coast Code Consultants, Inc. (WC³) has reviewed the documents, listed on the attached sheet, as they relate to the stated subject above. Documents appear to be in compliance with Condition ELEC-1, established by the California Energy Commission (CEC) Commission Decision (23-OPT-02), dated June 2025, and have been accepted as part of the construction documents.

Accepted submittals have been stamped and signed by WC³ and uploaded to the WC³ project portal. Any changes to the design professionals, in their area of responsible charge, must be submitted to the project portal for review and approval before said change takes effect.

Sincerely,

West Coast Code Consultants, Inc. (WC³)

Giyan A. Senaratne, S.E., P.E., LEED Ap.
Delegate Chief Building Official

Cc: Olivia Gastaldo, CEC Compliance Manager, Intersect Power (ogastaldo@ipxpower.com)

DOCUMENTS APPROVED FOR:

ELEC-1-02-REV-IFC Darden I&II PV Electrical Design Package and Studies

File Type / Description	File Name
Plans	24103-01 _ - MORTENSON _ - DARDEN _1 _ - _IFC_REV.2 _ - EE _ - 20260410.pdf
Parasitic Load Memo	Darden _ - Parasitic Load Memorandum _ - 20260204.pdf
AC Lost and Reactive Power Study	24103R-RP _ - DardenI&II _ - _AC Loss & Reactive Power Study _ - IFC_Rev1.pdf
Temporary Overvoltage Study	24103R-TOV _ - Darden I- IV _Temporary Overvoltage Study _ - IFC _ - Rev1.pdf

Appendix G

DCBO Approval of Structural Package Revision (STRUC-1)

June 5, 2026



Mr. Joe Douglas
Compliance Project Manager
California Energy Commission
Energy Facilities Siting Division
1516 Ninth Street, MS 2000
Sacramento, CA 95814-5512

Darden Clean Energy Project (DCEP) – ACCEPTANCE
WC³ Permit No.: STRUC-1-02-REV

Re: Plan Review: Darden I&II PV Structural Package Rev
Address: Darden Clean Energy Project, Fresno County, CA

Dear Mr. Douglas:

On behalf of the California Energy Commission, West Coast Code Consultants, Inc. (WC³) has reviewed the documents, listed on the attached sheet, as they relate to the stated subject above. Documents appear to be in compliance with Condition STRUC-1, established by the California Energy Commission (CEC) Commission Decision (23-OPT-02), dated June 2025, and have been accepted as part of the construction documents.

Accepted submittals have been stamped and signed by WC³ and uploaded to the WC³ project portal. Any changes to the design professionals, in their area of responsible charge, must be submitted to the project portal for review and approval before said change takes effect.

Sincerely,

West Coast Code Consultants, Inc. (WC³)

A handwritten signature in blue ink, appearing to read "Giyan A. Senaratne", with a long, horizontal, wavy line extending from the end of the signature.

Giyan A. Senaratne, S.E., P.E., LEED Ap.
Delegate Chief Building Official

Cc: Olivia Gastaldo, CEC Compliance Manager, Intersect Power (ogastaldo@ipxpower.com)

DOCUMENTS APPROVED FOR:

Darden I&II PV Structural Package Rev

File Type / Description	File Name
Plans	DARDEN-I-and-II---IFC-REV-2---SE-PV-SHEETS---RESUBMISSION.pdf
Structural Calculations	24103---DARDEN-I-IV---PV---IFC-REV2-RESUBMITTAL---STRUCTURAL-CALCULATIONS---NON-RACKING---20260413_SS.pdf
Structural Calculations	24103-01&02---Mortenson---Darden---IFC-REV2-SE-Racking-Foundation-Calculations---20260313_SS.pdf
Geotechnical Review Letter	60245030-Darden-Solar-Structural-Geo-Review-Letter-Rev.-3.pdf

Appendix H

Darden Equipment List – June 2026 (SWITCH-GHG-01 / AQ-SC-5)

Date	Equipment Number	Type	Model or Serial Number	Engine Family	EIN #	< 6 Days on site	<50 HP	Engine Tier	Owner	Maint Letter/ Rcrds on file	Days expected on site
12/8/2025	N/A	Ford Tractor	8970	Genesis/456 ci	N/A	No	No	N/A	LangStraat	Yes	29
12/8/2025	N/A	12 K Forklift	JLG-604210015738	N/A	N/A	No	No	N/A	Sun Belt	Yes	29
12/8/2025	N/A	John Deere Tractor 9520R	1RW9520RCFP017000	JJDXL13.5310	N/A	No	No	4	LangStraat	Yes	29
12/8/2025	N/A	John Deere Tractor 9R 640	1RW9640DKNA080178	N/A	N/A	No	No	4	LangStraat	Yes	29
12/8/2025	N/A	John Deere Tractor 8R 370	1RW8370DHC206591	N/A	N/A	No	No	4	LangStraat	Yes	29
12/8/2025	N/A	John Deere Tractor 9620RX	1RW9620RAJP806120	N/A	N/A	No	No	4	LangStraat	Yes	29
12/8/2025	N/A	John Deere Tractor 9560R	1RW8956RTPCP6004378	N/A	N/A	No	No	4	LangStraat	Yes	29
12/8/2025	N/A	John Deere Tractor 9620RX	1RW9620RJPK807717	N/A	N/A	No	No	4	LangStraat	Yes	29
12/8/2025	N/A	John Deere Tractor 9R 640	1RW9640DLNA080110	N/A	N/A	No	No	4	LangStraat	Yes	29
12/8/2025	N/A	John Deere Tractor 9560 RT	1RW9560RUCP901799	N/A	N/A	No	No	5	LangStraat	Yes	29
12/9/2025	N/A	4,000 Gal Water Truck	1FVHCYD25PHNZ0216	N/A	N/A	No	No	4	LangStraat	Yes	287
12/9/2025	2020034	4,000 Gal Water Truck	HV K400	N/A	N/A	No	No	4	QuinnCAT	Yes	28
12/10/2025	AV444400019	Water Truck	KENWORTH T270	LCEXH0408BAT	N/A	No	No	N/A	Sunbelt	Yes	27
12/10/2025	W5515	Pickup Truck	F350	KFMXH06.7P4A	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	10594776	Skid steer loader	BOBCAT T770	NGMXD4045VV	AG4X58	No	No	4	Sunbelt	Yes	27
12/10/2025	10678170	Skid steer loader	BOBCAT T776	NGMXD4045VV	SU5F46	No	No	4	Sunbelt	Yes	27
12/10/2025	W3084	Dump Truck	7400SBA	HCEXH0540LAX	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	W5808	Framer	F550	MGMXD06.78VV	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	W5387	Framer	F550	CFMXH06.7B23	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	W5730	Framer	F550	KFMXH06.7P4A	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	W5695	Framer	F550	KFMXH06.7P4A	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	W2129	Trailer - Dump	N/A	N/A	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	W2178	Trailer - Dump	N/A	N/A	N/A	No	No	N/A	Wilson	Yes	27
12/10/2025	W5675	Pickup Truck	F250	KFMXH06.7P4A	N/A	No	No	N/A	Wilson	Yes	27
12/17/2025	N/A	4X4 UTV	599167	Nasdf	N/A	No	Yes	N/A	Equipment Share	Yes	279
12/17/2025	N/A	Light Tower	471766	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	279
12/17/2025	N/A	Chipper	BC 1500	NFMXD4045AA	N/A	No	No	4	Sunbelt	Yes	20
1/5/2026	1001558	5K Forklift	501-20TC	N/A	N/A	No	No	N/A	Sunbelt	Yes	356
1/7/2026	2021379	Shepsfoot Roller Paver	P5600876/ CP56B	LPKXL04.4MU1	CH7D65	No	No	4	QuinnCAT	Yes	358
1/7/2026	2023540	Smooth Drum Roller	RFL00304	NPXKL03.6FX1	KR7S47	No	No	4	QuinnCAT	Yes	358
1/7/2026	2200146	Skip Loader	H6L00469	NPXKL03.6FW1	KT8F69	No	No	4	QuinnCAT	Yes	358
1/7/2026	388798	12K Forklift	Skytrak/0160129416	PCEXL03.8AAC	EH3J94	No	No	4	Equipment Share	Yes	358
1/8/2026	N/A	150 Motor Grader	EB502035	PCPXL09.3HTF	N/A	No	No	4	Mortenson	Yes	357
1/9/2026	N/A	Chipper	BC 1000 XL	NFMXD4045AA	N/A	No	No	4	Vermeer	Yes	356
1/12/2026	AG-946-03	John Deere AG Tractor	9460R	N/A	JV6W54	No	No	4	I-5 Rentals	Yes	353
1/12/2026	AG-946-02	John Deere AG Tractor	9460R	N/A	VL9A57	No	No	4	I-5 Rentals	Yes	353
1/13/2026	2021723	Backhoe 420	C3.6	MPKXL03.6FX1	RX5T74	No	No	4	QuinnCAT	Yes	352
1/13/2026	HR0000892	CAT D6 Dozer	HNK01080/ C9.3B	NCPXL09.3NTF	JJ6D48	No	No	4	QuinnCAT	Yes	352
1/14/2026	2500193	Skid steer Loader	KR405378	RPKXL02.8FM1	NK5J87	No	No	4	QuinnCAT	Yes	351
1/14/2026	HR0001080	CAT D6 Dozer	WH510308/ C9.3B	RCPXL09.3NTF	FB9V56	No	No	4	QuinnCAT	Yes	351
1/16/2026	2-0011405	Dodge Flatbed 2500	3C6UR5HL5RG127247	N/A	N/A	No	No	N/A	PTR	Yes	349
1/20/2026	HR0001022	140 Motor Grader	EB301097	PCPXL09.3HTF	WH8S45	No	No	4	QuinnCAT	Yes	345
1/20/2026	SC 804	CAT scraper 627K	T4F12170	N/A	N/A	No	No	4	JS Cole	Yes	345
1/20/2026	SC 813	CAT scraper 627K	T4F12456	N/A	N/A	No	No	4	JS Cole	Yes	345
1/20/2026	SC 814	CAT scraper 627K	T4F13219	N/A	N/A	No	No	4	JS Cole	Yes	345
1/26/2026	27349	Light Tower	LTV6	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	339
1/27/2026	2200420	Shepsfoot Roller Paver	SXT00139/ CP11GC	NPXKL03.6FW1	KD8D49	No	No	4	QuinnCAT	Yes	338
2/2/2026	HR0000944	815 Roller	J5T00209	NPXKL07.0VM1	DP4D99	No	No	4	QuinnCAT	Yes	333
2/3/2026	2023371	4,000 Gal Water Truck	HV K400	N/A	N/A	No	No	5	QuinnCAT	Yes	332
2/3/2026	644333	4X4 UTV	4XAP4ED4778837855	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	332
2/5/2026	#17	Plow	8631-01	N/A	N/A	No	No	N/A	A&E	Yes	267
2/6/2026	2020039	4,000 Gal Water Truck	HV K400	N/A	N/A	No	No	4	QuinnCAT	Yes	329
2/6/2026	2022761	325 Excavator	TEL20004	MPKXL04.4SU1	XL3M79	No	No	4	QuinnCAT	Yes	10
2/6/2026	HR0001005	CAT D6 Dozer	JJ601134	PCPXL09.3HTF	Sv7H58	No	No	3	QuinnCAT	Yes	10
2/10/2026	2022681	84" Smooth Drum Roller	RFL00207	J3639457	AF4C94	No	No	4	QuinnCAT	Yes	325
2/13/2026	2021051	4,000 Gal Water Truck	HV K400	N/A	N/A	No	No	N/A	QuinnCAT	Yes	322
2/17/2026	2022724	D4 Dozer	CAT000D4LKWM00306	NCPXL09.3NTF	DY7H58	No	No	5	QuinnCAT	Yes	318
2/18/2026	399816	12K Forklift 8' forks	TH1256CD2020	25017858	KB6H99	No	No	4	Equipment Share	Yes	360
2/18/2026	HR0001002	623 Scraper	WYF00133	PCPXL12.5HTF	GA4X43	No	No	4	QuinnCAT	Yes	300
2/19/2026	641034	12K Forklift 8' forks	JCB5CR7GKS3537186	SJCBL04.4TA5	WH4K43	No	No	4	Equipment Share	Yes	7
2/20/2026	425624	10k Forklift	510.56	RJCBL04.4TA5	VT6V97	No	No	4	Equipment Share(Willscot)	Yes	80

2/23/2026	HR0001079	966 Loader	M7R10253	RCPXL09.3NTF	UR6P49	No	No	4	QuinnCAT	Yes	266
2/23/2026	HR0001067	8,000 Gal Water Truck 740	3T806422	RCPXL15.2HTF	KF6D94	No	No	4	QuinnCAT	Yes	260
2/24/2026	HR0001091	140 Grader	EB301438	SYE49934	RF6B38	No	No	4	QuinnCAT	Yes	200
2/24/2026	644325	4X4 UTV	4XAP4ED47T8840223	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	360
2/24/2026	644290	4X4 UTV	D26P4VDB4	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	360
2/24/2026	HR0001016	140 Grader	EB301096	PCPXL09.3HTF	YV8V97	No	No	4	QuinnCAT	Yes	200
2/24/2026	2200420	84" Padfoot roller	SXT00139/ CP11GC	NPXKL03.6FX1	KD8D49	No	No	4	QuinnCAT	Yes	200
2/25/2026	246988	Light Tower	ALMAND	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	300
2/25/2026	280202	150 KW Generator	QAS 175 Atlas Copco	N/A	N/A	No	No	N/A	Equipment Share	Yes	40
2/25/2026	239059	36KW Generator	Wacker Neuson G50	N/A	N/A	No	No	N/A	Equipment Share	Yes	300
2/25/2026	HR000113	140 Motor Grader	140 AWD	SCPXL09.3HTF	CS3H68	No	No	4	QuinnCAT	Yes	285
2/26/2026	2500444	315 Excavator	WKX50651	SPKXL03.6FX1	XC4S68	No	No	4	QuinnCAT	Yes	60
2/27/2026	2500441	Excavator	315	SPKXL03.6FX1	CE5X84	No	No	4	QuinnCAT	Yes	285
3/3/2026	200667	Tractor Loader	210	MYDXL03.3TKA	MF7A97	No	No	4	Equipment Share	Yes	300
3/3/2026	317754	Trencher	RTX450	PDZXL02.9021	DB5A99	No	No	4	Equipment Share	Yes	60
3/5/2026	HR0001008	623 Scraper	623	PCPXL12.5HTF	ME5S53	No	No	4	QuinnCAT	Yes	100
3/6/2026	641034	12K Forklift 8' forks	512-56	SJCBL04.4TA5	WH4K43	No	No	4	Equipment Share	Yes	300
3/6/2026	644022	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/9/2026	2200018	Smooth Drum Roller	CS11GC	MPKXL03.6FX1	YR6V85	No	No	4	QuinnCAT	Yes	100
3/10/2026	644334	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/10/2026	644295	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/10/2026	664010	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/10/2026	644394	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/11/2026	2023893	320 Excavator	320 GC	PPKXL04.4SU1	LY6H88	No	No	4	QuinnCAT	Yes	100
3/11/2026	2022996	Smooth Drum Roller	CS11GC	MPKXL03.6FX1	HX9L58	No	No	4	QuinnCAT	Yes	285
3/11/2026	HR0001048	150 Motor Grader	150 AWD	RCPXL09.3HTF	DF7M83	No	No	4	QuinnCAT	Yes	285
3/11/2026	664011	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/12/2026	2500437	308 Excavator	325	SPKXL02.8FL1	YH8K48	No	No	4	QuinnCAT	Yes	15
3/12/2026	HR0001125	D5 Dozer	D5	SPKXL07.0VL1	XR7R46	No	No	4	QuinnCAT	Yes	285
3/13/2026	2022699	325 Excavator	325	MPKXL04.4SU1	FS5B56	No	No	4	QuinnCAT	Yes	280
3/13/2026	2022777	325 Excavator	325	MPKXL04.4SU1	NF6F69	No	No	4	QuinnCAT	Yes	285
3/13/2026	623134	12K Forklift 8' forks	512-56	SJCBL04.4S09	5M5M85	No	No	4	Equipment Share	Yes	300
3/13/2026	664013	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/13/2026	2023372	4K Water Truck	Ledwell 4K WT	N/A	N/A	No	No	N/A	QuinnCAT	Yes	285
3/13/2026	2023373	4K Water Truck	Ledwell 4K WT	N/A	N/A	No	No	N/A	QuinnCAT	Yes	286
3/16/2026	281252	10k Forklift	GTH844	NDZXL02.9020	ST9M38	No	No	4	Equipment Share(Ecobridge)	Yes	80
3/16/2026	260621	Skid steer loader	svl97-2c	NKBXL03.8AMD	BL5J46	No	No	4	Equipment Share(Ecobridge)	Yes	80
3/16/2026	2023543	325 Excavator	325	NPXKL04.4SU1	CB6R35	No	No	4	QuinnCAT	Yes	280
3/16/2026	HR0000910	D5 Dozer	D5	NPXKL07.0VL4	SC4C33	No	No	4	QuinnCAT	Yes	285
3/17/2026	2600304	305 Excavator	305 CR	TPKXL02.2IW1	VL4B49	No	No	4	QuinnCAT	Yes	30
3/17/2026	2200711	26k Forklift	P120.10	NFPXL06.7FR1	BR8X47	No	No	4	QuinnCAT	Yes	12
3/17/2026	664009	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/18/2026	661881	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/19/2026	HR0000920	D5 Dozer	D5	NPXKL07.0VL4	FL4A55	No	No	4	QuinnCAT	Yes	285
3/20/2026	493797	12K Forklift 8' forks	512-56	RJCBL044S09	GM7L73	No	No	4	Equipment Share	Yes	300
3/23/2026	160148275	Telescopic Handler	1255	F3.8CM2450F156C	VX5Y33	No	No	T4F	Mortenson	Yes	415
3/23/2026	160148276	Telescopic Handler	1255	F3.8CM2450F156C	KP5G94	No	No	T4F	Mortenson	Yes	415
3/23/2026	160148277	Telescopic Handler	1255	F3.8CM2450F156C	LN5A69	No	No	T4F	Mortenson	Yes	415
3/23/2026	160148278	Telescopic Handler	1255	F3.8CM2450F156C	GX8E59	No	No	T4F	Mortenson	Yes	415
3/23/2026	160148279	Telescopic Handler	1255	F3.8CM2450F156C	BL7B33	No	No	T4F	Mortenson	Yes	415
3/23/2026	160148281	Telescopic Handler	1255	F3.8CM2450F156C	RM5B67	No	No	T4F	Mortenson	Yes	415
3/25/2026	664003	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/26/2026	2600307	Skid steer loader	275 XE	SPKXL03.6FX1	CK5J88	No	No	4	QuinnCAT	Yes	337
3/26/2026	2600308	Skid steer loader	275 XE	TPKXL03.6FX1	BV5Y46	No	No	4	QuinnCAT	Yes	285
3/26/2026	2600309	Skid Steer Loader	275 XE	TPKXL03.6FX1	EP7R64	No	No	4	QuinnCAT	Yes	285
3/26/2026	2600310	Skid Steer Loader	275 XE	TPKXL03.6FX2	LN6E83	No	No	4	QuinnCAT	Yes	285
3/26/2026	226388	14K Forklift 8'forks	3099291	NJCBL04.4S09	XG8J69	No	No	4	Equipment Share	Yes	300
3/26/2026	661783	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/27/2026	2500254	Skid steer loader	265	RPKXL02.8FM1	SM9V84	No	No	4	QuinnCAT	Yes	285
3/27/2026	2200033	Smooth Drum Roller	CS11GC	NPXKL03.6FX1	RX8Y33	No	No	4	QuinnCAT	Yes	285
3/27/2026	HR0001142	D5 Dozer	D5	SPKXL07.0VL4	FA4B63	No	No	4	QuinnCAT	Yes	285
3/27/2026	661887	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	HR0001104	Motor Grader	140 AWD	RCPXL09.3NTF	RH3R75	No	No	4	QuinnCAT	Yes	285
3/30/2026	661884	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400

3/30/2026	661768	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	661883	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	661886	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	661879	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	661885	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	644346	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	673296	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
3/30/2026	2022835	Excavators	325	MPKXL04.4SU1	GD7A33	No	No	T4F	QuinnCAT	Yes	125
3/31/2026	432834	12k Forklift 8' forks	512-56	RJCBL04.4TA5	SN4L37	No	No	4	Equipment Share	Yes	300
3/31/2026	661330	12k Forklift 8' forks	512-56	SJCBL04.4TA5	GC7X43	No	No	4	Equipment Share	Yes	300
3/31/2026	664014	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/1/2026	2025087	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	XN6T37	No	No	T4F	Mortenson	Yes	453
4/1/2026	2025058	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	AB3K75	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026056	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	FA5P64	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026018	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	LC9T44	No	No	T4F	Mortenson	Yes	453
4/1/2026	2025139	Drill Rig (Mobile)	HR Pro 1500	PYDXL02.1TDA	HD6W64	No	No	T4F	Mortenson	Yes	453
4/1/2026	20203255	Drill Rig (Mobile)	HRE5000	RHZXL02.0V50	AU7P97	No	No	T4F	Mortenson	Yes	453
4/1/2026	18411245	Drill Rig (Mobile)	HRE5000	RHZXL02.0V50	CP7P89	No	No	T4F	Mortenson	Yes	453
4/1/2026	19402255	Drill Rig (Mobile)	HRE5000	RHZXL02.0V50	WM8D88	No	No	T4F	Mortenson	Yes	453
4/1/2026	24011255	Drill Rig (Mobile)	HRE5000	SHZXL02.0V50	CG4F96	No	No	T4F	Mortenson	Yes	453
4/1/2026	19903255	Drill Rig (Mobile)	HRE5000	SHZXL02.0V50	PY7P88	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026041	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	HY4K76	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026070	Drill Rig (Mobile)	FEX 6m	RCPXL09.3HTF	EH4N47	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026042	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	JS5K77	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026043	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	UE5X88	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026054	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	VG4P86	No	No	T4F	Mortenson	Yes	453
4/1/2026	2026069	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	SK6V34	No	No	T4F	Mortenson	Yes	453
4/2/2026	644291	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/2/2026	664002	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/2/2026	661761	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/2/2026	664006	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/2/2026	644021	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/2/2026	644288	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/3/2026	2022700	Excavators	325	MPKXL04.4SU1	MJ9J79	No	No	T4F	QuinnCAT	Yes	125
4/6/2026	411699	Skip Loader	JD120	PYDXL03.3TKA	MY9X54	No	No	4	Equipment Share	Yes	95
4/6/2026	661765	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/8/2026	680661	12k Forklift	512-56 S2	TJCBL04.4TA5	GP3R97	No	No	4	Equipment Share	Yes	275
4/8/2026	HR0001157	Graders	140 AWD	RCPXL09.3HTF	VV8S95	No	No	T4F	QuinnCAT	Yes	200
4/9/2026	680172	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/9/2026	2021609	Excavators	325	LPKXL04.4SU1	LD8C48	No	No	T4F	QuinnCAT	Yes	95
4/9/2026	2021657	Excavators	325	LPKXL04.4SU1	GC5T83	No	No	T4F	QuinnCAT	Yes	95
4/9/2026	2022660	Pavers	CS11 GC	MPKXL03.6FX1	SK6A85	No	No	T4F	QuinnCAT	Yes	86
4/9/2026	2022685	Pavers	CS11 GC	MPKXL03.6FX1	RX9W36	No	No	T4F	QuinnCAT	Yes	86
4/9/2026	2022838	Excavators	325	MPKXL04.4SU1	RU8P38	No	No	T4F	QuinnCAT	Yes	125
4/10/2026	202503	Skip Loader	210EP	MYDLX03.TKA	EH6W94	No	No	4	Equipment Share	Yes	95
4/10/2026	681093	12k Forklift	512-56 S2	TJCBL04.4TA5	PC4U34	No	No	4	Equipment Share	Yes	275
4/10/2026	558014	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/10/2026	591461	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/10/2026	587309	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/10/2026	680173	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/10/2026	680195	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/10/2026	680201	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/10/2026	2021389	Backhoe	420ST	LPKXL03.6FX1	WC5X66	No	No	T4F	QuinnCAT	Yes	83
4/10/2026	2022665	Dozer	D3	MPKXL03.6FX1	PU7W47	No	No	T4F	QuinnCAT	Yes	75
4/10/2026	2022755	Excavators	325	MPKXL04.4SU1	HY9U57	No	No	T4F	QuinnCAT	Yes	125
4/10/2026	2022890	Excavators	325	MPKXL04.4SU1	AV9Y53	No	No	T4F	QuinnCAT	Yes	125
4/10/2026	2023538	Excavators	315 GC	NPKXL03.6FX1	ML3M84	No	No	T4F	QuinnCAT	Yes	100
4/10/2026	2023690	Excavators	325	NPKXL04.4SU1	AJ7A66	No	No	T4F	QuinnCAT	Yes	125
4/10/2026	2300239	Excavators	303.5	N/A	N/A	No	No	T4F	QuinnCAT	Yes	60
4/10/2026	2400234	17K Telehandler	1732	PDZXL03.6060	CK9J36	No	No	T4F	QuinnCAT	Yes	150
4/10/2026	2500031	Wheel Loader	950 GC	RPKXL07.0VM1	RY5R84	No	No	T4F	QuinnCAT	Yes	125
4/10/2026	2500037	Wheel Loader	950 GC	RPKXL07.0VM1	AW9L77	No	No	T4F	QuinnCAT	Yes	125
4/10/2026	2500038	Wheel Loader	950 GC	RPKXL07.0VM1	GL6F53	No	No	T4F	QuinnCAT	Yes	125
4/10/2026	2500379	Excavators	315	SPKXL03.6FX1	SE3B49	No	No	T4F	QuinnCAT	Yes	100

4/10/2026	2600229	Excavators	315	TPKXL03.6FX1	JB5F54	No	No	T4F	QuinnCAT	Yes	100
4/10/2026	2600357	Excavators	315 GC	TPKXL03.6FX1	VH8J63	No	No	T4F	QuinnCAT	Yes	100
4/10/2026	HR0001049	Motor Grader	140 AWD	RCPXL09.3HTF	EH3E54	No	No	T4F	QuinnCAT	Yes	200
4/10/2026	HR0001092	Motor Grader	150 AWD	RCPXL09.3HTF	RX4N43	No	No	T4F	QuinnCAT	Yes	200
4/11/2026	2023895	Excavators	325	PPKXL04.4SU1	TD7Y65	No	No	T4F	QuinnCAT	Yes	125
4/13/2026	573718	Skiploader	210G-EP	RYDXL03.3TKA	LM6A49	No	No	4	Equipment Share	Yes	275
4/13/2026	680525	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/13/2026	680518	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/13/2026	680177	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/13/2026	680174	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/13/2026	2023979	Excavators	325	PPKXL04.4SU1	CY3X58	No	No	T4F	QuinnCAT	Yes	125
4/13/2026	2300077	Excavators	315 GC	PPKXL03.6FX1	KW7X54	No	No	T4F	QuinnCAT	Yes	95
4/13/2026	2500270	Skid Steer Loaders	265	RPKXL02.8FM1	HN5S89	No	No	T4F	QuinnCAT	Yes	130
4/13/2026	2500271	Skid Steer Loaders	265	RPKXL02.8FM1	YN8R45	No	No	T4F	QuinnCAT	Yes	130
4/13/2026	2500294	Skid Steer Loaders	265	RPKXL02.8FM1	DT9E55	No	No	T4F	QuinnCAT	Yes	130
4/13/2026	2600366	Backhoes	430	MPKXL03.6FX1	RP5V39	No	No	T4F	QuinnCAT	Yes	95
4/14/2026	682692	12K Forklift	512-56	TJCBLO4.4TA5	EH7C76	No	No	4	Equipment Share	Yes	275
4/14/2026	HR0001123	Rubber Tired Loaders	966	SCPXL09.3NTF	BA5G99	No	No	T4F	QuinnCAT	Yes	225
4/14/2026	HR0001150	Rubber Tired Loaders	966	SCPXL09.3NTF	RD6E58	No	No	T4F	QuinnCAT	Yes	175
4/15/2026	682433	12K Forklift	512-56	TJCBLO4.4TA5	LU9J65	No	No	4	Equipment Share	Yes	275
4/15/2026	680659	12K Forklift	512-56	TJCBLO4.4TA5	680659	No	No	4	Equipment Share	Yes	275
4/15/2026	650659	TL12 Track 6' Forks	TL12V-2	SKBXL03.8C5D	LC3C67	No	No	4	Equipment Share	Yes	275
4/15/2026	644292	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/15/2026	644344	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/15/2026	680188	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/15/2026	2023896	Excavators	325	PPKXL04.4SU1	BG5J45	No	No	T4F	QuinnCAT	Yes	125
4/15/2026	2023897	Excavators	325	PPKXL04.4SU1	NJ5J54	No	No	T4F	QuinnCAT	Yes	125
4/15/2026	2200042	Excavators	325	NPKXL04.4SU1	YT3A45	No	No	T4F	QuinnCAT	Yes	125
4/15/2026	2200138	Excavators	320 GC	NPKXL04.4SU1	PT3W47	No	No	T4F	QuinnCAT	Yes	95
4/15/2026	HR0001060	Excavators	325	RPKXL04.4SU1	LK4G35	No	No	T4F	QuinnCAT	Yes	95
4/15/2026	HR0001145	Motor Grader	150 AWD	SCPXL09.3HTF	VB3G74	No	No	T4F	QuinnCAT	Yes	150
4/15/2026	HR0001148	Motor Grader	140 AWD	SCPXL09.3HTF	BH5G64	No	No	T4F	QuinnCAT	Yes	150
4/15/2026	R8Y06705	Skid Steer Loaders	275	TPKXL03.6FX1	GL9K55	No	No	T4F	Mortenson	Yes	415
4/15/2026	R8Y06711	Skid Steer Loaders	275	TPKXL03.6FX1	XJ3E76	No	No	T4F	Mortenson	Yes	415
4/15/2026	R8Y06058	Skid Steer Loaders	275	RCPXL09.3HTF	DG3N44	No	No	T4F	Mortenson	Yes	415
4/15/2026	R8Y06053	Skid Steer Loaders	275	TPKXL03.6FX1	SL4F98	No	No	T4F	Mortenson	Yes	415
4/15/2026	EB510209	Graders	150	SCPXL09.3HTF	DK4U56	No	No	T4F	Mortenson	Yes	150
4/16/2026	682689	12K Forklift	512-56	TJCBLO4.4TA5	MC9K87	No	No	4	Equipment Share	Yes	275
4/16/2026	2023898	Excavators	325	PPKXL04.4SU1	LC3A84	No	No	T4F	QuinnCAT	Yes	125
4/16/2026	2023978	Excavators	325	PPKXL04.4SU1	PH7S85	No	No	T4F	QuinnCAT	Yes	125
4/16/2026	2400916	Dozer	D2	PPKXL03.6FX1	FG3G53	No	No	T4F	QuinnCAT	Yes	125
4/16/2026	2401335	Skid Steer Loaders	289D3	PKBXL03.3EKD	WS9W66	No	No	T4F	QuinnCAT	Yes	125
4/16/2026	HR0000912	Dozer	D5	NPKXL07.0VL4	TP7D97	No	No	T4F	QuinnCAT	Yes	125
4/16/2026	HR0000995	Dozer	D5	PPKXL07.0VL4	NN8F97	No	No	T4F	QuinnCAT	Yes	125
4/16/2026	HR0001155	Excavators	335	TPKXL07.0VM1	NP3K54	No	No	T4F	QuinnCAT	Yes	155
4/16/2026	HR0001156	Excavators	335	TPKXL07.0VM1	ET8L99	No	No	T4F	QuinnCAT	Yes	155
4/17/2026	2500359	Compactor	CP12	RPKXL04.4MU1	YB3R78	No	No	T4F	QuinnCAT	Yes	125
4/20/2026	302258	Skiploader	210ELP	NYDXL03.3TKA	SG9P54	No	No	4	Equipment Share	Yes	275
4/20/2026	596391	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/20/2026	455952	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/20/2026	592033	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/20/2026	676830	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/20/2026	539368	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/20/2026	686407	4X4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/22/2026	682690	12k Forklift	512-56 S2	TJCBLO4.4TA5	LT6T54	No	No	4	Equipment Share	Yes	275
4/22/2026	650663	TL12 Track 6' Forks	TL12V-2	SKBXL03.8C5D	AW5A97	No	No	4	Equipment Share	Yes	275
4/22/2026	680178	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/22/2026	680205	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/22/2026	680176	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/22/2026	680514	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/22/2026	687483	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/23/2026	682693	12k Forklift	512-56 S2	TJCBLO4.4TA5	NL4X84	No	No	4	Equipment Share	Yes	275
4/23/2026	682694	12k Forklift	512-56 S2	TJCBLO4.4TA5	AU6D68	No	No	4	Equipment Share	Yes	275
4/23/2026	650658	TL12 Track 6' Forks	TL12V-2	SKBXL03.8C5D	SH9Y45	No	No	4	Equipment Share	Yes	275

4/23/2026	681108	12K Forlift	TL12V-2	SKBXL03.8C5D	YD5A57	No	No	4	Equipment Share	Yes	275
4/23/2026	682691	12k Forklift	512-56 S2	TJCBL04.4TA5	NS8P49	No	No	4	Equipment Share	Yes	275
4/24/2026	688962	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/27/2026	690051	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/27/2026	690057	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/27/2026	2021658	Excavators	325	LPKXL04.4SU1	UN5W35	No	No	T4F	QuinnCAT	Yes	95
4/27/2026	2021660	Excavators	325	LPKXL04.4SU1	FV6L56	No	No	T4F	QuinnCAT	Yes	95
4/27/2026	2023657	Excavators	315 GC	NPKXL03.6FX1	RH4S75	No	No	T4F	QuinnCAT	Yes	100
4/27/2026	2300079	Excavators	315GC	PPKXL03.6FX1	EG5T54	No	No	T4F	QuinnCAT	Yes	95
4/27/2026	2400908	Excavators	305 CR	RPKXL02.2IW1	LG4N48	No	No	T4F	QuinnCAT	Yes	90
4/27/2026	2500439	Excavators	315	SPKXL03.6FX1	HD4U45	No	No	T4F	QuinnCAT	Yes	100
4/27/2026	2500443	Excavators	315	SPKXL03.6FX1	NR9L36	No	No	T4F	QuinnCAT	Yes	100
4/29/2026	688952	4x4 UTV	Pro XD	N/A	N/A	No	Yes	N/A	Equipment Share	Yes	400
4/30/2026	36373	Trencher 6"cut	DITCH WITCH	KDZXL03.9021	GU3G73	No	No	4	Equipment Share	Yes	275
5/1/2026	650661	Skid Steer Loaders	TL12V2-CR	SKBXL03.8C5D	KSN1297	No	No	T4F	Equipment Share	Yes	430
5/1/2026	2026055	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	KK7B44	No	No	T4F	Mortenson	Yes	453
5/1/2026	2026044	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	DG6W34	No	No	T4F	Mortenson	Yes	453
5/1/2026	2026030	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	TX7J56	No	No	T4F	Mortenson	Yes	453
5/1/2026	2026032	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	ML8J44	No	No	T4F	Mortenson	Yes	453
5/1/2026	2026031	Drill Rig (Mobile)	HD Pro1500	RCPXL09.3HTF	FT3U54	No	No	T4F	Mortenson	Yes	453
5/1/2026	2026045	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	JV4X79	No	No	T4F	Mortenson	Yes	453
5/1/2026	2026033	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	JF3J45	No	No	T4F	Mortenson	Yes	453
5/4/2026	688955	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	688951	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	690059	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	690049	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	690050	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	690058	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	690054	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	688965	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	688964	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/4/2026	688953	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/5/2026	2600549	Telescopic Handler	TH1255	SPKXL03.6FX1	BJ8L55	No	No	T4F	QuinnCAT	Yes	100
5/5/2026	688967	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/5/2026	690055	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/5/2026	688959	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/5/2026	693611	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/5/2026	688960	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/5/2026	688958	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/5/2026	690052	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/7/2026	688957	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/7/2026	688956	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/7/2026	692954	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/7/2026	693667	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/8/2026	HR0001109	Excavators	335	SPKXL07.0VM1	HR3C99	No	No	T4F	QuinnCAT	Yes	430
5/8/2026	HR0001116	Rubber Tired Loaders	966	RCPXL09.3NTF	KK8B78	No	No	T4F	QuinnCAT	Yes	430
5/8/2026	HR0001120	Scraper	623	SCPXL12.5HTF	AL4Y38	No	No	T4F	QuinnCAT	Yes	430
5/11/2026	603151	45' Art Boom	Z-45 XC	SDZXL02.9021	13333070	No	No	T4F	Equipment Share	Yes	89
5/11/2026	523348	Art Boom	Z-45 XC	SDZXL02.9021	13274386	No	Yes	T4F	Equipment Share	Yes	430
5/11/2026	16616	Tractors/Loaders/Backhoes	210LEP	MYDXL03.3TKA	CH4E33TB03095	No	No	T4F	Equipment Share	Yes	430
5/11/2026	HR0001091	Graders	140 AWD	SCPXL09.3HTF	RF6B38	No	No	T4F	QuinnCAT	Yes	430
5/11/2026	HR0001130	Graders	140 AWD	SCPXL09.3HTF	CS3H68	No	No	T4F	QuinnCAT	Yes	430
5/11/2026	2024201	Drill Rig	HD Pro 1500	PYDXL02.1TDA	XD6W33	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024199	Drill Rig	HD Pro 1500	PYDXL02.1TDA	VH7K77	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024175	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	BL7J64	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024185	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	HX6A84	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024186	Drill Rig	HD Pro 1500	PYDXL02.1TDA	WC4A49	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024177	Drill Rig	HD Pro 1500	PYDXL02.1TDA	XR6B58	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024198	Drill Rig	HD Pro 1500	PYDXL02.1TDA	PH7D76	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024197	Drill Rig	HD Pro 1500	PYDXL02.1TDA	SH4K38	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024180	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	YL8T94	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024179	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	PN7U45	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024171	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	UL4H76	No	No	T4F	Mortenson	Yes	413
5/11/2026	XEC01062	Crawler Tractors	D6XE	RCPXL09.3NTF	CL5G48	No	No	T4F	Mortenson	Yes	413

5/11/2026	EB502035	Graders	150	RCPXL09.3HTF	HL6A83	No	No	T4F	Mortenson	Yes	150
5/11/2026	2024174	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	HB7H66	No	No	T4F	Mortenson	Yes	150
5/11/2026	2024176	Drill Rig	HD Pro 1500	PYDXL02.1TDA	JY8X45	No	No	T4F	Mortenson	Yes	150
5/11/2026	2024167	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	WN6L37	No	No	T4F	Mortenson	Yes	413
5/11/2026	2024200	Drill Rig (Mobile)	HD Pro 1500	PYDXL02.1TDA	TK4Y55	No	No	T4F	Mortenson	Yes	413
5/11/2026	2026057	Drill Rig (Mobile)	HD Pro 1500	RCPXL09.3HTF	NK5J76	No	No	T4F	Mortenson	Yes	413
5/11/2026	693648	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	693669	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	693661	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	692960	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	693643	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	692958	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	693700	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	693699	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/11/2026	693668	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/13/2026	2600458	Skid Steer Loaders	275	TPKXL03.6FX1	AM9R67	No	No	T4F	QuinnCAT	Yes	233
5/18/2026	692961	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/18/2026	692959	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/18/2026	692962	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/20/2026	2200141	Excavators	325	NPXKL04.4SU1	MY3F68	No	No	T4F	QuinnCAT	Yes	275
5/20/2026	2500456	Excavators	320GC	RPKXL04.4SU1	TR5U75	No	No	T4F	QuinnCAT	Yes	275
5/20/2026	2600400	Excavators	320 GC	TPKXL04.4.SU1	AX3G35	No	No	T4F	QuinnCAT	Yes	275
5/20/2026	695652	Telescopic Handler	12054	SCEZL03.8AAC	222749212	No	No	T4F	Equipment Share	Yes	430
5/20/2026	700477	Telescopic Handler	12054	SCFXL03.8AAC	22749194	No	No	T4F	Equipment Share	Yes	430
5/20/2026	HR0001134	Excavators	335	TPKXL07.0VM1	VS9H54	No	No	T4F	QuinnCAT	Yes	430
5/22/2026	2600455	Skid Steer Loaders	275	TPKXL03.6FX1	UH8X54	No	No	T4F	QuinnCAT	Yes	400
5/22/2026	2600456	Skid Steer Loaders	275	TPKXL03.6FX1	UJ9H89	No	No	T4F	QuinnCAT	Yes	400
5/22/2026	2600457	Skid Steer Loaders	275	TPKXL03.6FX1	HE7D74	No	No	T4F	QuinnCAT	Yes	400
5/25/2026	693694	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/26/2026	692956	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/27/2026	693647	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/27/2026	692964	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/27/2026	688954	4x4 UTV	Gator RTV-X	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/27/2026	693688	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/28/2026	2023818	12K Forklift	TL1255	NPXKL03.6FX1	GM3D33	No	No	T4F	QuinnCAT	Yes	275
5/28/2026	693632	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
5/29/2026	692963	Telescopic Handler	TL12V2-CR	SKBXL03.8C5D	KSW3726	No	No	T4F	Equipment Share	Yes	430
5/29/2026	661360	Telescopic Handler	510-56	SJCBL04.4S09	SJ320/42326 U36744	No	No	T4F	Equipment Share	Yes	430
5/29/2026	692957	4x4 UTV	Pro XD	NA	NA	No	Yes	NA	Equipment Share	Yes	450
6/18/2026	711916	Telescopic Handler	505-20TC	TKHXL02.5TCR	5604001940	No	Yes	T4F	Equipment Share	Yes	228
6/18/2026	510823	Telescopic Handler	G5-18A	RDZXL02.9020	13224537	No	No	T4F	Equipment Share	Yes	228
6/10/2026	567091	Forklift	506-36	SJCBL04.4TA5	SL320/41533U13107	No	No	T4F	Equipment Share	Yes	236
6/17/2026	553977	Telescopic Handler	519	RDZXL02.2111	13236509	No	No	T4F	Equipment Share	Yes	236
5/29/2026	251975	Tractor/Loader/Backhoe	210EL	NYDXL03.3TKA	CH4E33TB04702	No	No	T4F	Equipment Share	Yes	187
6/5/2026	702813	Telescopic Handler	12054	TCEXL03.8AAC	22751358	No	No	T4F	Equipment Share	Yes	228
5/27/2026	711487	Telescopic Handler	12054	TCEXL03.8AAC	2275946	No	No	T4F	Equipment Share	Yes	199
6/17/2026	721548	Tractor/Loader/Backhoe	210G-EP	SYDXL03.3TKA	CH4E33TB06836	No	No	T4F	Equipment Share	Yes	186
5/25/2026	688300	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSS1862	No	No	T4F	Equipment Share	Yes	409
5/25/2026	682963	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSW3726	No	No	T4F	Equipment Share	Yes	427
5/25/2026	699169	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSW2322	No	No	T4F	Equipment Share	Yes	409
5/25/2026	699163	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KTC0933	No	No	T4F	Equipment Share	Yes	418
6/19/2026	718365	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSY2008	No	No	T4F	Equipment Share	Yes	402
6/19/2026	643507	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	ZSC0796	No	No	T4F	Equipment Share	Yes	402
6/1/2026	699160	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSY4707	No	No	T4F	Equipment Share	Yes	402
6/19/2026	716592	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSU5637	No	No	T4F	Equipment Share	Yes	402
6/19/2026	719968	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSW2217	No	No	T4F	Equipment Share	Yes	402
6/19/2026	699173	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSY4116	No	No	T4F	Equipment Share	Yes	402
5/25/2026	699154	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSW4832	No	No	T4F	Equipment Share	Yes	434
5/25/2026	699165	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSY3740	No	No	T4F	Equipment Share	Yes	434
6/24/2026	643511	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSNB1352	No	No	T4F	Equipment Share	Yes	413
6/19/2026	682695	Telescopic Handler	512-56 S2	444 TA4-55-1.1	SL320/41533 U01547	No	No	T4F	Equipment Share	Yes	423
6/12/2026	682969	Skid Steer Loader	TL12V2-CR	SKBXL03.8C5D	KSS4670	No	No	T4F	Equipment Share	Yes	385
6/17/2026	695284	Telescopic Handler	505-20-TC	TKHXL02.5TCR	5532301130	No	No	T4F	Equipment Share	Yes	423
6/18/2026	696977	Excavator	410P	TJDXL04.5317	PE4045U240889	No	No	T4F	Equipment Share	Yes	434

6/22/2026	700476	Telescopic Handler	12054	SCEXL03.8AAC	22749155	No	No	T4F	Equipment Share	Yes	332
6/22/2026	584204	Telescopic Handler	12054	SCEXL038AAC	27708229	No	No	T4F	Equipment Share	Yes	424
6/23/2026	674996	Telescopic Handler	512-56S S2	TJCBL04.4S09	SJ320/40919U040672	No	No	T4F	Equipment Share	Yes	231
6/29/2026	462104	Telescopic Handler	510-56	RJCBL04.4TA5	SL320/42325 U28067	No	No	T4F	Equipment Share	Yes	97
6/30/2026	729552	Skid Steer Loaders	TL12V2-CRH	TKBXL03.8C5D	V3800-CR-TI-DV3	No	No	T4F	Equipment Share	Yes	402
6/22/2026	180826	Telescopic Handler	TL1255D	JPKXL04.4MT1	GT7R69	No	No	T4F	QuinnCAT	Yes	2
6/24/2026	2022659	Pavers	CS11 GC	MPKXL03.6FX1	XY5P83	No	No	T4F	QuinnCAT	Yes	358
6/24/2026	2400813	Excavators	305	PPKXL02.2W1	MJ3W93	No	Yes	T4F	QuinnCAT	Yes	285
6/17/2026	2400968	Skid Steer Loaders	299D3 XE	PKBXL03.8C5D	CG4V48	No	No	T4F	QuinnCAT	Yes	285
6/24/2026	2401246	Telescopic Handler	TL1255	RPKXL03.6FX1	CN9B87	No	No	T4F	QuinnCAT	Yes	423
6/11/2026	2600499	Excavators	308 CR	TPKXL02.8FL1	NC7U38	No	No	T4F	QuinnCAT	Yes	285
6/17/2026	HR0001007	Excavators	335	PPKXL07.0VM1	CV5P96	No	No	T4F	QuinnCAT	Yes	285
6/29/2026	HR0001137	Rubber Tired Loaders	950	SPKXL07.0VM1	XW9M68	No	No	T4F	QuinnCAT	Yes	285
6/29/2026	HR0001144	Rubber Tired Loaders	950	TPKXL07.0VM1	AF5J47	No	No	T4F	QuinnCAT	Yes	285
6/17/2026	HR0001170	Rubber Tired Loaders	966	SCPXL09.3NTF	RA7J69	No	No	T4F	QuinnCAT	Yes	285
6/29/2026	HR0001173	Excavator	335	TPKXL07.0VM1	SD9P97	No	No	T4F	QuinnCAT	Yes	285
6/29/2026	HR0001177	Excavator	335	TPKXL07.0VM1	AL8J85	No	No	T4F	QuinnCAT	Yes	285

Appendix I

Darden Hazardous Waste Manifest (SWITCH WASTE-1)

FSE

SK SHIP# 248515680



009389319SKS

Form Approved OMB No. 2050-0039

* Please print or type.

UNIFORM HAZARDOUS WASTE MANIFEST		1. Generator ID Number CAR000401430	2. Page 1 of 1	3. Emergency Response Phone 1-800-468-1760	4. Manifest Tracking Number 009389319 SKS	
5. Generator's Name and Mailing Address Mortenson Construction 23796 West Davis Avenue CANTUA CREEK 509-675-2153				Generator's Site Address (if different than mailing address) CA 93608-0000		
6. Transporter 1 Company Name SAFETY-KLEEN SYSTEMS INC				U.S. EPA ID Number TXR000081205		
7. Transporter 2 Company Name CLEAN HARBORS ENV SERVICES INC				U.S. EPA ID Number MAD039322250		
8. Designated Facility Name and Site Address CLEAN HARBORS OF WILMINGTON 1737 EAST DENNI STREET WILMINGTON, CA 90744 310-835-9998				U.S. EPA ID Number CAD044429835		
Facility's Phone						
GENERATOR	9a. HM	9b. U.S. DOT Description (including Proper Shipping Name, Hazard Class, ID Number and Packing Group (if any))	10. Containers No. Type		11. Total Quantity	12. Unit Wt./Vol.
		1. NONE, NON-RCRA HAZARDOUS WASTE, LIQUIDS, (GREASE), #A-A		DM		P
		2. NONE, NON-RCRA HAZARDOUS WASTE, LIQUIDS, (OIL, DIRT, SAND, ABSORBENTS AND OR DIESEL FUEL), #A-A	005	DM	1,000	P
		3. NONE, NON-RCRA HAZARDOUS WASTE LIQUIDS, (OIL SLUDGE AND WATER), #A-A	004	DM	400	P
		4.				
13. Waste Codes 352						
14. Special Handling Instructions and Additional Information TSD:W1 99973596 M042683 CSG: 2602640699						
24H EMERGENCY#800-468-1760-CH/SK/TFI-Contract retained by generator confers agency authority on initial transporter to add or substitute additional transporters on generator's behalf.						
15. GENERATOR'S/OFFEROR'S CERTIFICATION: I hereby declare that the contents of this consignment are fully and accurately described above by the proper shipping name, and are classified, packaged, marked and labeled/placarded, and are in all respects in proper condition for transport according to applicable international and national governmental regulations. If export shipment and I am the Primary Exporter, I certify that the contents of this consignment conform to the terms of the attached EPA Acknowledgment of Consent. I certify that the waste minimization statement identified in 40 CFR 262.27(a) (if I am a large quantity generator) or (b) (if I am a small quantity generator) is true.						
Generator's Offeror's Printed/Typed Name Kaylee ANGUS		Signature <i>Kaylee Angus</i>		Month Day Year 05 20 26		
16. International Shipments ☐ Import to U.S. ☐ Export from U.S. Port of entry/exit: _____ Date leaving U.S. _____						
17. Transporter Acknowledgment of Receipt of Materials						
Transporter 1 Printed/Typed Name Antonio Guerrero		Signature <i>Antonio Guerrero</i>		Month Day Year 05 20 26		
Transporter 2 Printed/Typed Name MZCHAS S. Cam		Signature <i>MZCHAS S. Cam</i>		Month Day Year 05 26 26		
18. Discrepancy						
18a. Discrepancy Indication Space ☐ Quantity ☐ Type ☐ Residue ☐ Partial Rejection ☐ Full Rejection						
Manifest Reference Number						
18b. Alternate Facility (or Generator) U.S. EPA ID Number						
Facility's Phone						
18c. Signature of Alternate Facility (or Generator) Month Day Year						
19. Hazardous Waste Report Management Method Codes (i.e., codes for hazardous waste treatment, disposal, and recycling systems)						
20. Designated Facility Owner/Operator Certification of receipt of hazardous materials covered by the manifest except as noted in Item 18a						
Printed/Typed Name Graciela Gomez		Signature <i>Graciela Gomez</i>		Month Day Year 16 01 26		


Appendix J

Darden Safety Report (Worker Safety-3)

Worker Safety

Worker Safety-3: Darden Clean Energy Project Safety Report – June 2026

- Monthly Safety Inspection Report:

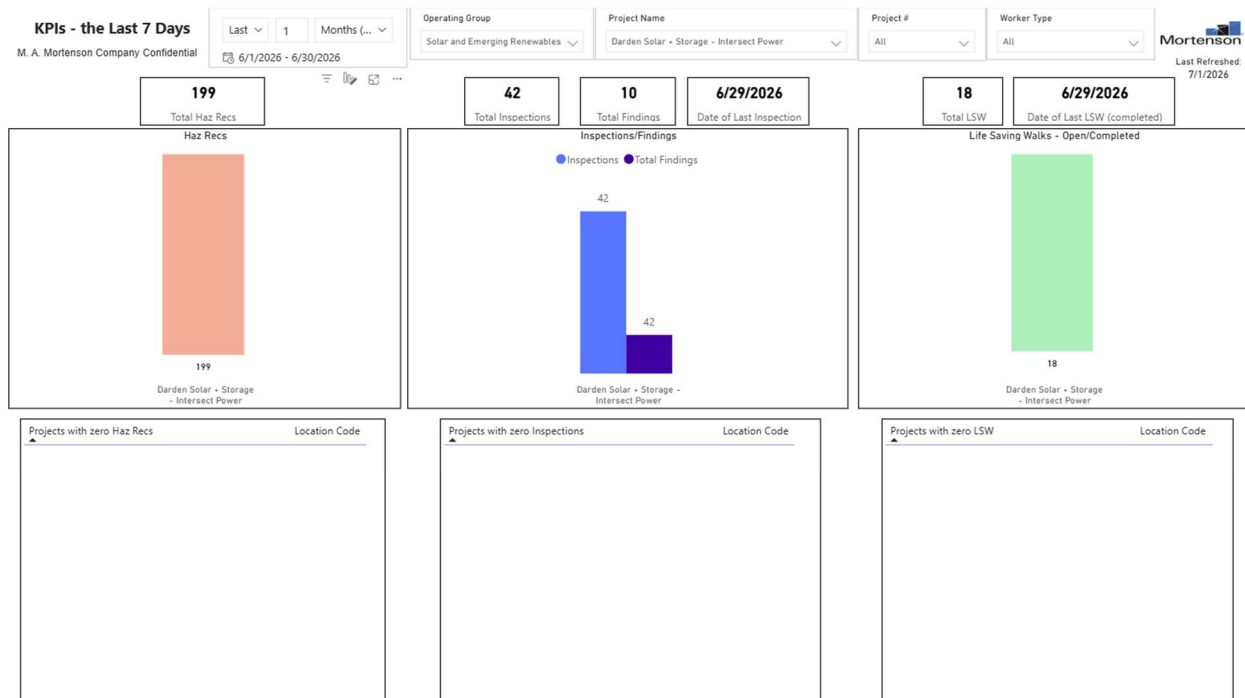

Monthly Safety Summary – Darden Solar + Storage (June 2026)

Project Overview

- Orientations – 61
- Mortenson Craft Onboarded – 335
- Trainings – 32
- Safety Inspections – 42
- Life Saving Walks - 18
- Total Hazard Recognitions - 199

Appendix K

DCBO Approval of Minor Revisions to IFC Gen Tie Design Package (TSE-4)

June 22, 2026



Mr. Joe Douglas
Compliance Project Manager
California Energy Commission
Energy Facilities Siting Division
1516 Ninth Street, MS 2000
Sacramento, CA 95814-5512

Darden Clean Energy Project (DCEP) – ACCEPTANCE
WC³ Permit No.: N/A

Re: Plan Review: [projdesc]
Address: Darden Clean Energy Project, Fresno County, CA

Dear Mr. Douglas:

On behalf of the California Energy Commission, West Coast Code Consultants, Inc. (WC³) has reviewed the documents, listed on the attached sheet, as they relate to the stated subject above. Documents appear to be in compliance with the California Energy Commission (CEC) Commission Decision (23-OPT-02), dated June 2025, and have been accepted as part of the construction documents.

Accepted submittals have been stamped and signed by WC³ and uploaded to the WC³ project portal. Any changes to the design professionals, in their area of responsible charge, must be submitted to the project portal for review and approval before said change takes effect.

Sincerely,

West Coast Code Consultants, Inc. (WC³)

A handwritten signature in blue ink, appearing to read "Giyan A. Senaratne", with a long, horizontal, wavy line extending from the end of the signature.

Giyan A. Senaratne, S.E., P.E., LEED Ap.
Delegate Chief Building Official

Cc: Olivia Gastaldo, CEC Compliance Manager, Intersect Power (ogastaldo@ipxpower.com)

DOCUMENTS APPROVED FOR:

Minor Revisions IFC Gen Tie Design Package

File Type / Description	File Name
Phasing Diagram	DAR-T-205.01.pdf
Foundation Detail Drawing Structure Schedule	DAR-T-700.02.pdf
Drawing Index	DAR-G.00.01.pdf
Sabre Customer Approval	26-570903_CUSTOMER APPROVAL_rev A_6-1-26 reduced size.pdf
Cut Sheets	Gen-Tie Material Cutsheets Combined 5.7.2026.pdf

Appendix L

DCBO Approval of Solar Canopy Plans

July 6, 2026



Mr. Joe Douglas
Compliance Project Manager
California Energy Commission
Energy Facilities Siting Division
1516 Ninth Street, MS 2000
Sacramento, CA 95814-5512

Darden Clean Energy Project (DCEP) – ACCEPTANCE
WC³ Permit No.: N/A

Re: Plan Review: Solar Canopy Plans
Address: Darden Clean Energy Project, Fresno County, CA

Dear Mr. Douglas:

On behalf of the California Energy Commission, West Coast Code Consultants, Inc. (WC³) has reviewed the documents, listed on the attached sheet, as they relate to the stated subject above. Documents appear to be in compliance with the California Energy Commission (CEC) Commission Decision (23-OPT-02), dated June 2025, and have been accepted as part of the construction documents.

Accepted submittals have been stamped and signed by WC³ and uploaded to the WC³ project portal. Any changes to the design professionals, in their area of responsible charge, must be submitted to the project portal for review and approval before said change takes effect.

Sincerely,

West Coast Code Consultants, Inc. (WC³)

A handwritten signature in blue ink, appearing to read "Giyan A. Senaratne", with a long horizontal flourish extending to the right.

Giyan A. Senaratne, S.E., P.E., LEED Ap.
Delegate Chief Building Official

Cc: Olivia Gastaldo, CEC Compliance Manager, Intersect Power (ogastaldo@ipxpower.com)

DOCUMENTS APPROVED FOR:

Solar Canopy Plans

File Type / Description	File Name
Solar Canopy Plans	Solar Canopy Plans.pdf

Appendix M

Department of Parks and Recreation Archaeological Reports

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
PRIMARY RECORD

Primary #:
HRI #:
Trinomial:
NRHP Status Code:

Other Listings

Review Code:

Reviewer:

Date:

Page 1 of 3

*Resource Name or #: D-MP-ISO1

P1. Other Identifier: Darden-Monitoring Phase-Isolate-1

***P2. Location:** ☒ Not for Publication ☐ Unrestricted

***a. County:** Fresno County

and
* **b. USGS 7.5' Quad:** Westside, Calif. **Date:** 1956 **T** 17S **R** 16E; NW ¼ of NE ¼ of Sec 12 **M.D.B.M.**
c. Address: N/A **City:** Cantua Creek **Zip:** 93608
d. UTM: **Zone:** 11S **214593 mE / 4040915 mN**
e. Other Locational Data: From the intersection of West Clarkson Avenue and South San Mateo Avenue, head east on West Clarkson Avenue for 2.7 miles. Curve right to continue onto South Amador Avenue for 1.3 miles and curve right to take West Elkhorn Avenue for 0.6 miles to South Sonoma Avenue and proceed south for 0.8 miles. Turn left onto West Davis Avenue and proceed east for 3.5 miles. The resource is located approximately 663 feet south of West Davis Avenue.
Elevation: 204 ft. AMSL

***P3a. Description:** D-MP-ISO1 is an obsidian bifacially flaked core. The isolated artifact measures approximately 6 centimeters (cm) in length by 4.5 cm in width, with a thickness of 4 cm (Photo 1 and Photo 2). The isolate is located on a flat valley agricultural land with light brown silty loam sediment present. Isolated finds typically do not qualify for listing in the National Register of Historic Places (NRHP) or the California Register of Historical Resources as their data potential is exhausted during the initial recording. Furthermore, per agreement with the California Energy Commission and the Tachi Yokut Tribe, the isolate was transferred to the Tachi Yokut Tribe for final disposition following the completion of documentation.

***P3b. Resource Attributes:** Prehistoric: AP16 - Other: Isolate

***P4. Resources Present:** ☐ Building; ☐ Structure; ☐ Object; ☐ Site; ☐ District; ☐ Element of District; ☒ Other

P5a. Photo



P5b. Description of Photo:

Photo 1. D-MP-ISO1, Side A, Plan View

***P6. Date Constructed/Age and Sources:**

☐ Historic ☒ Prehistoric ☐ Both

***P7. Owner and Address:**

IPX Power
9450 SW Gemini Drive PMB #68743
Beaverton, Oregon 97008-1705

***P8. Recorded by:**

Rincon Consultants
2060 Knoll Avenue
Ventura, CA 93003

***P9. Date Recorded:** June 3, 2026

***P10. Survey Type:** Construction
Monitoring

***P11. Report Citation:** Rincon Consultants, Inc. (TBD) Cultural and Tribal Cultural Resources Monitoring Report for the Darden Clean Energy Project. To be filed with CEC and SSJVIC.

***Attachments:** ☐ NONE; ☒ Location Map; ☐ Sketch Map; ☒ Continuation Sheet; ☐ Building, Structure, and Object Record; ☐ Archaeological Record; ☐ District Record; ☐ Linear Feature Record; ☐ Milling Station Record; ☐ Rock Art Record; ☐ Artifact Record; ☐ Photograph Record; ☐ Other (List):

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
LOCATION MAP

Primary #:
HRI #:
Trinomial:


Page 2 of 3

*Resource Name or #: D-MP-ISO1

*Map Name: *Westside, Calif.*

*Scale: 1:24,000

*Date of Map: 1956

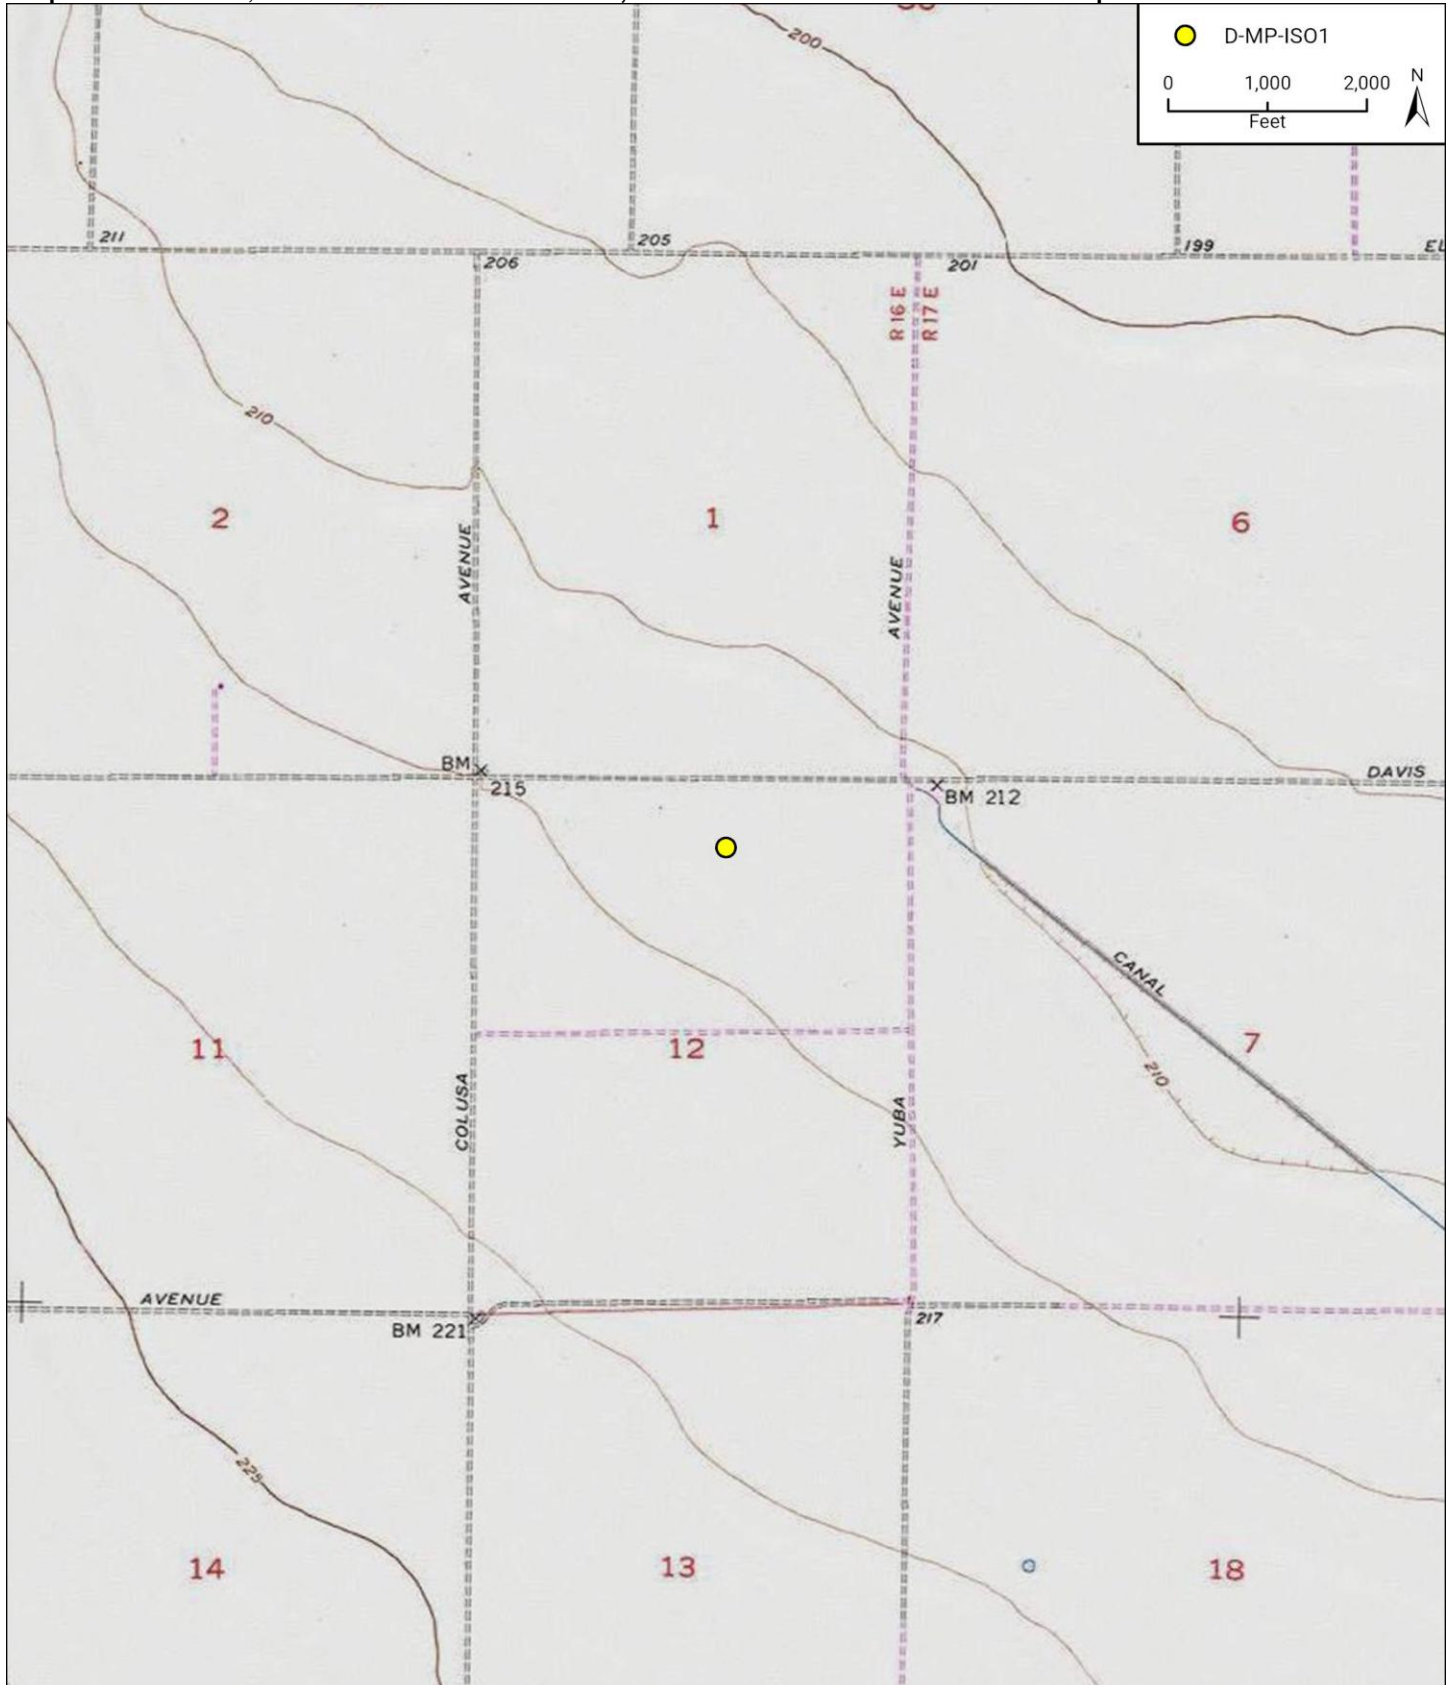

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
CONTINUATION SHEET

Primary #:

HRI #:

Trinomial:

Page 3 of 3

*Resource Name or #: D-MP-ISO1

Recorded by: Rincon Consultants, Inc.

Date: 7/9/2026

■ Continuation □ Update

P5a. Photographs: continued



Photo 2. D-MP-ISO1, Side B, Plan View

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
PRIMARY RECORD

Primary #:
HRI #:
Trinomial:
NRHP Status Code:

Other Listings

Review Code:

Reviewer:

Date:

Page 1 of 3

*Resource Name or #: D-MP-ISO2

P1. Other Identifier: Darden-Monitoring Phase-Isolate-2

*P2. Location: ☒ Not for Publication ☐ Unrestricted

*a. County: Fresno County

and
* b. USGS 7.5' Quad: *Westside, Calif.* Date: 1956 T 17S R 16E; SE ¼ of SE ¼ of Sec 21 M.D.B.M.
c. Address: N/A City: Cantua Creek Zip: 93608
d. UTM's: Zone: 11S 210440 mE / 4036657 mN
e. Other Locational Data: From the intersection of West Clarkson Avenue and South San Mateo Avenue, head east on West Clarkson Avenue for 2.7 miles. Curve right to continue onto South Amador Avenue for 1.3 miles and curve right to take West Elkhorn Avenue for 0.6 miles to South Sonoma Avenue and proceed south for 3.8 miles. Turn left onto West Mount Whitney Avenue and proceed east for 1 mile. Turn left onto South Napa Avenue and proceed north for 0.2 miles. The resource is located approximately 46 feet west of South Napa Avenue.
Elevation: 244 ft. AMSL

*P3a. Description: D-MP-ISO2 consists of one isolated ground stone (Artifact A: Photo 1 through Photo 3) and one modified stone (Artifact B Photo 4 and Photo 5). The isolated ground stone measures 15 centimeters (cm) in length by 14 cm in width, with a thickness of 8 cm. The modified stone measures 14.5 cm in length by 10 cm in width with a thickness of 5.5 cm at one end and 2.5 cm at the other. The artifacts were identified three meters apart, located on a flat valley agricultural land with light brown silty loam sediment present. Isolated finds are typically ineligible for listing in the National Register of Historic Places (NRHP) and/or the California Register of Historical Resources (CRHR) as their data potential is exhausted during the initial recording. Furthermore, per agreement with the California Energy Commission and the Tachi Yokut Tribe, the isolate was transferred to the Tachi Yokut Tribe for final disposition following the completion of documentation.

*P3b. Resource Attributes: Prehistoric: AP16 - Other: Isolate

*P4. Resources Present: ☐ Building; ☐ Structure; ☐ Object; ☐ Site; ☐ District; ☐ Element of District; ☒ Other

P5a.



P5b. Description of Photo:

Photo 1. D-MP-ISO2, Artifact A, Side A, Plan View

*P6. Date Constructed/Age and Sources:

☐ Historic ☒ Prehistoric ☐ Both

*P7. Owner and Address:

IPX Power
9450 SW Gemini Drive PMB #68743
Beaverton, Oregon 97008-1705

*P8. Recorded by:

Rincon Consultants
2060 Knoll Avenue
Ventura, CA 93003

*P9. Date Recorded: June 17, 2026

*P10. Survey Type: Construction
Monitoring

*P11. Report Citation: Rincon Consultants, Inc. (TBD) Cultural and Tribal Cultural Resources Monitoring Report for the Darden Clean Energy Project. To be filed with CEC and SSJVIC.

*Attachments: ☐ NONE; ☒ Location Map; ☐ Sketch Map; ☒ Continuation Sheet; ☐ Building, Structure, and Object Record; ☐ Archaeological Record; ☐ District Record; ☐ Linear Feature Record; ☐ Milling Station Record; ☐ Rock Art Record; ☐ Artifact Record; ☐ Photograph Record; ☐ Other (List):

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
LOCATION MAP

Primary #:
HRI #:
Trinomial:


Page 2 of 3

*Resource Name or #: D-MP-ISO2

*Map Name: *Westside, Calif.*

*Scale: 1:24,000

*Date of Map: 1956

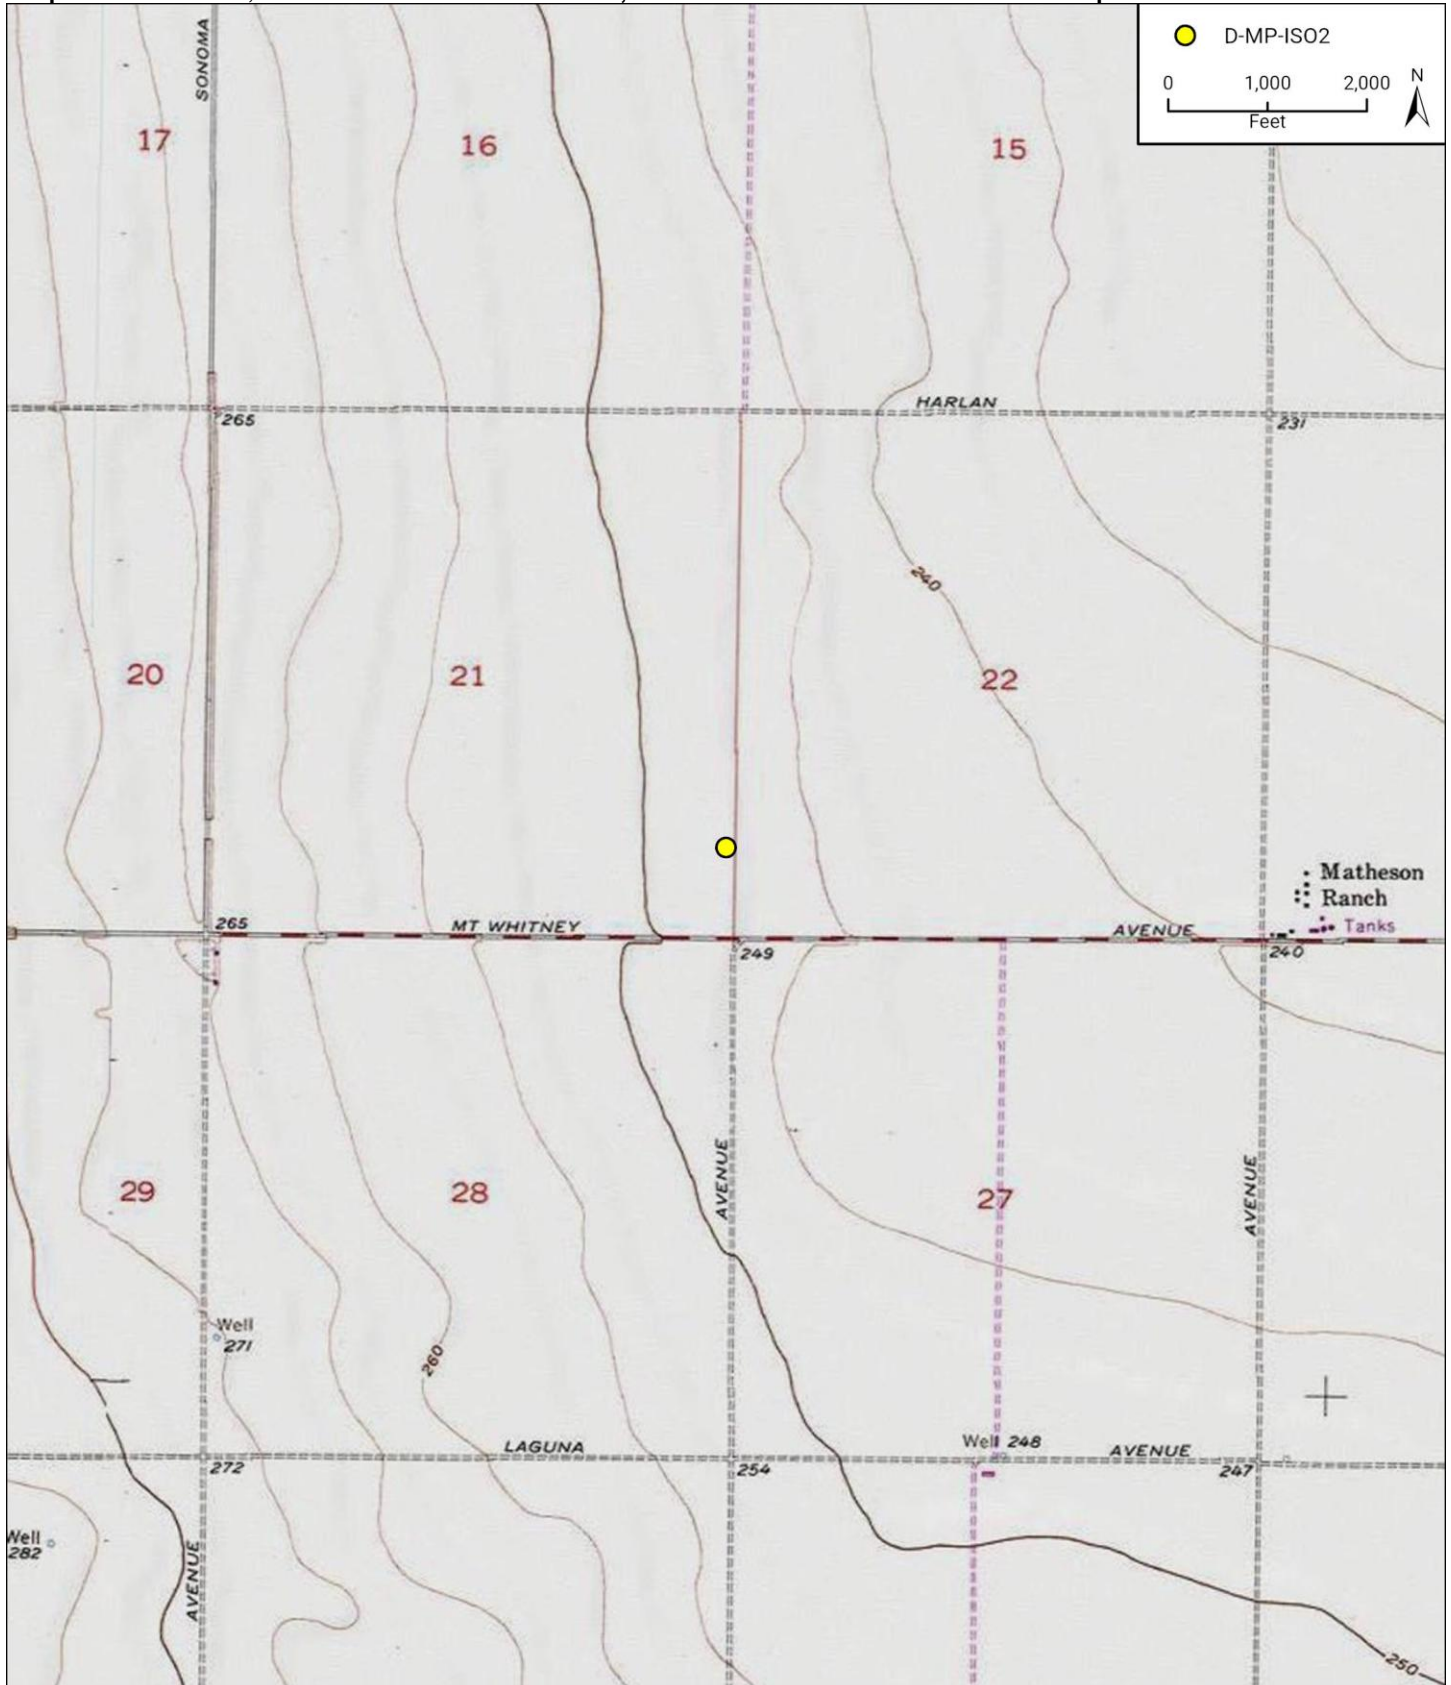

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
CONTINUATION SHEET

Primary #:

HRI #:

Trinomial:

Page 3 of 3

*Resource Name or #: D-MP-ISO2

Recorded by: Rincon Consultants, Inc.

Date: 7/9/2026

☒ Continuation ☐ Update

P5a. Photographs: continued



Photo 2. D-MP-ISO2, Artifact A, Side B, Plan View



Photo 3. D-MP-ISO2, Artifact A, Possible Modified Margin, Plan View



Photo 4. D-MP-ISO2, Artifact B, Side A, Plan View



Photo 5. D-MP-ISO2, Artifact B, Side B, Plan View

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
PRIMARY RECORD

Primary #:
HRI #:
Trinomial:
NRHP Status Code:

Other Listings

Review Code:

Reviewer:

Date:

Page 1 of 5

*Resource Name or #: D-MP-S1

P1. Other Identifier: Darden-Monitoring Phase-Site 1

***P2. Location:** ☒ Not for Publication ☐ Unrestricted

***a. County:** Fresno

and

*** b. USGS 7.5' Quad:** Westside, Calif. **Date:** 1956 **T** 17S; **R** 16E; NW ¼ of NE ¼ of Sec 12 **M.D.B.M.**

c. Address: **City:** Cantua Creek **Zip:** 93608

d. UTM's: **Zone:** 11S **214498 mE / 4040905 mN**

e. Other Locational Data: From the intersection of West Clarkson Avenue and South San Mateo Avenue, head east on West Clarkson Avenue for 2.7 miles. Curve right to continue onto South Amador Avenue for 1.3 miles and curve right to take West Elkhorn Avenue for 0.6 miles to South Sonoma Avenue and proceed south for 0.8 miles. Turn left onto West Davis Avenue and proceed east for 3.4 miles. The resource is located approximately 730 feet south of West Davis Avenue.

Elevation: 203 ft. AMSL

***P3a. Description:** D-MP-S1 is a sparse scatter comprised of 10 fragments of obsidian (Photo 1 through Photo 4). The scatter measures 39 meters (128.5 feet) north to south and 29 meters (94 feet) east to west. The fragments are of low-quality material with inclusions. Cortex is noted on several of the artifacts indicating that these items had not been prepared for flaking. One fragment appears to contain flaking which may be the result of mechanical equipment associated with the use of the area as an agriculture field. Obsidian is not natural to the area, therefore its presence is the result of human agency. However, considering the quality of material (many noted inclusions), lack of platform preparation for flaking, and lack of association with other artifacts, it is unclear if the artifacts were transported prehistorically or more recently.

***P3b. Resource Attributes:** Prehistoric: AP2 - Lithic scatter

***P4. Resources Present:** ☐ Building; ☐ Structure; ☐ Object; ☒ Site; ☐ District; ☐ Element of District; ☐ Other

P5a. Photo 1



P5b. Description of Photo:

Photo 1. D-MP-S1, View North

***P6. Date Constructed/Age and Sources:**

☐ Historic ☒ Prehistoric ☐ Both

***P7. Owner and Address:**

IPX Power
9450 SW Gemini Drive PMB #68743
Beaverton, Oregon 97008-1705

***P8. Recorded by:**

Rincon Consultants
2060 Knoll Drive
Ventura, CA 93003

***P9. Date Recorded:** June 4, 2026

***P10. Survey Type:** Construction
Monitoring

***P11. Report Citation:** Rincon Consultants, Inc. (TBD) Cultural and Tribal Cultural Resources Monitoring Report for the Darden Clean Energy Project. To be filed with CEC and SSJVIC.

***Attachments:** ☐ NONE; ☒ Location Map; ☒ Sketch Map; ☒ Continuation Sheet; ☐ Building, Structure, and Object Record; ☒ Archaeological Record; ☐ District Record; ☐ Linear Feature Record; ☐ Milling Station Record; ☐ Rock Art Record; ☐ Artifact Record; ☐ Photograph Record; ☐ Other (List):

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
LOCATION MAP

Primary #:
HRI #:
Trinomial:


Page 2 of 5

*Resource Name or #: D-MP-S1

*Map Name: Westside, Calif.

*Scale: 1:24,000

*Date of Map: 1956

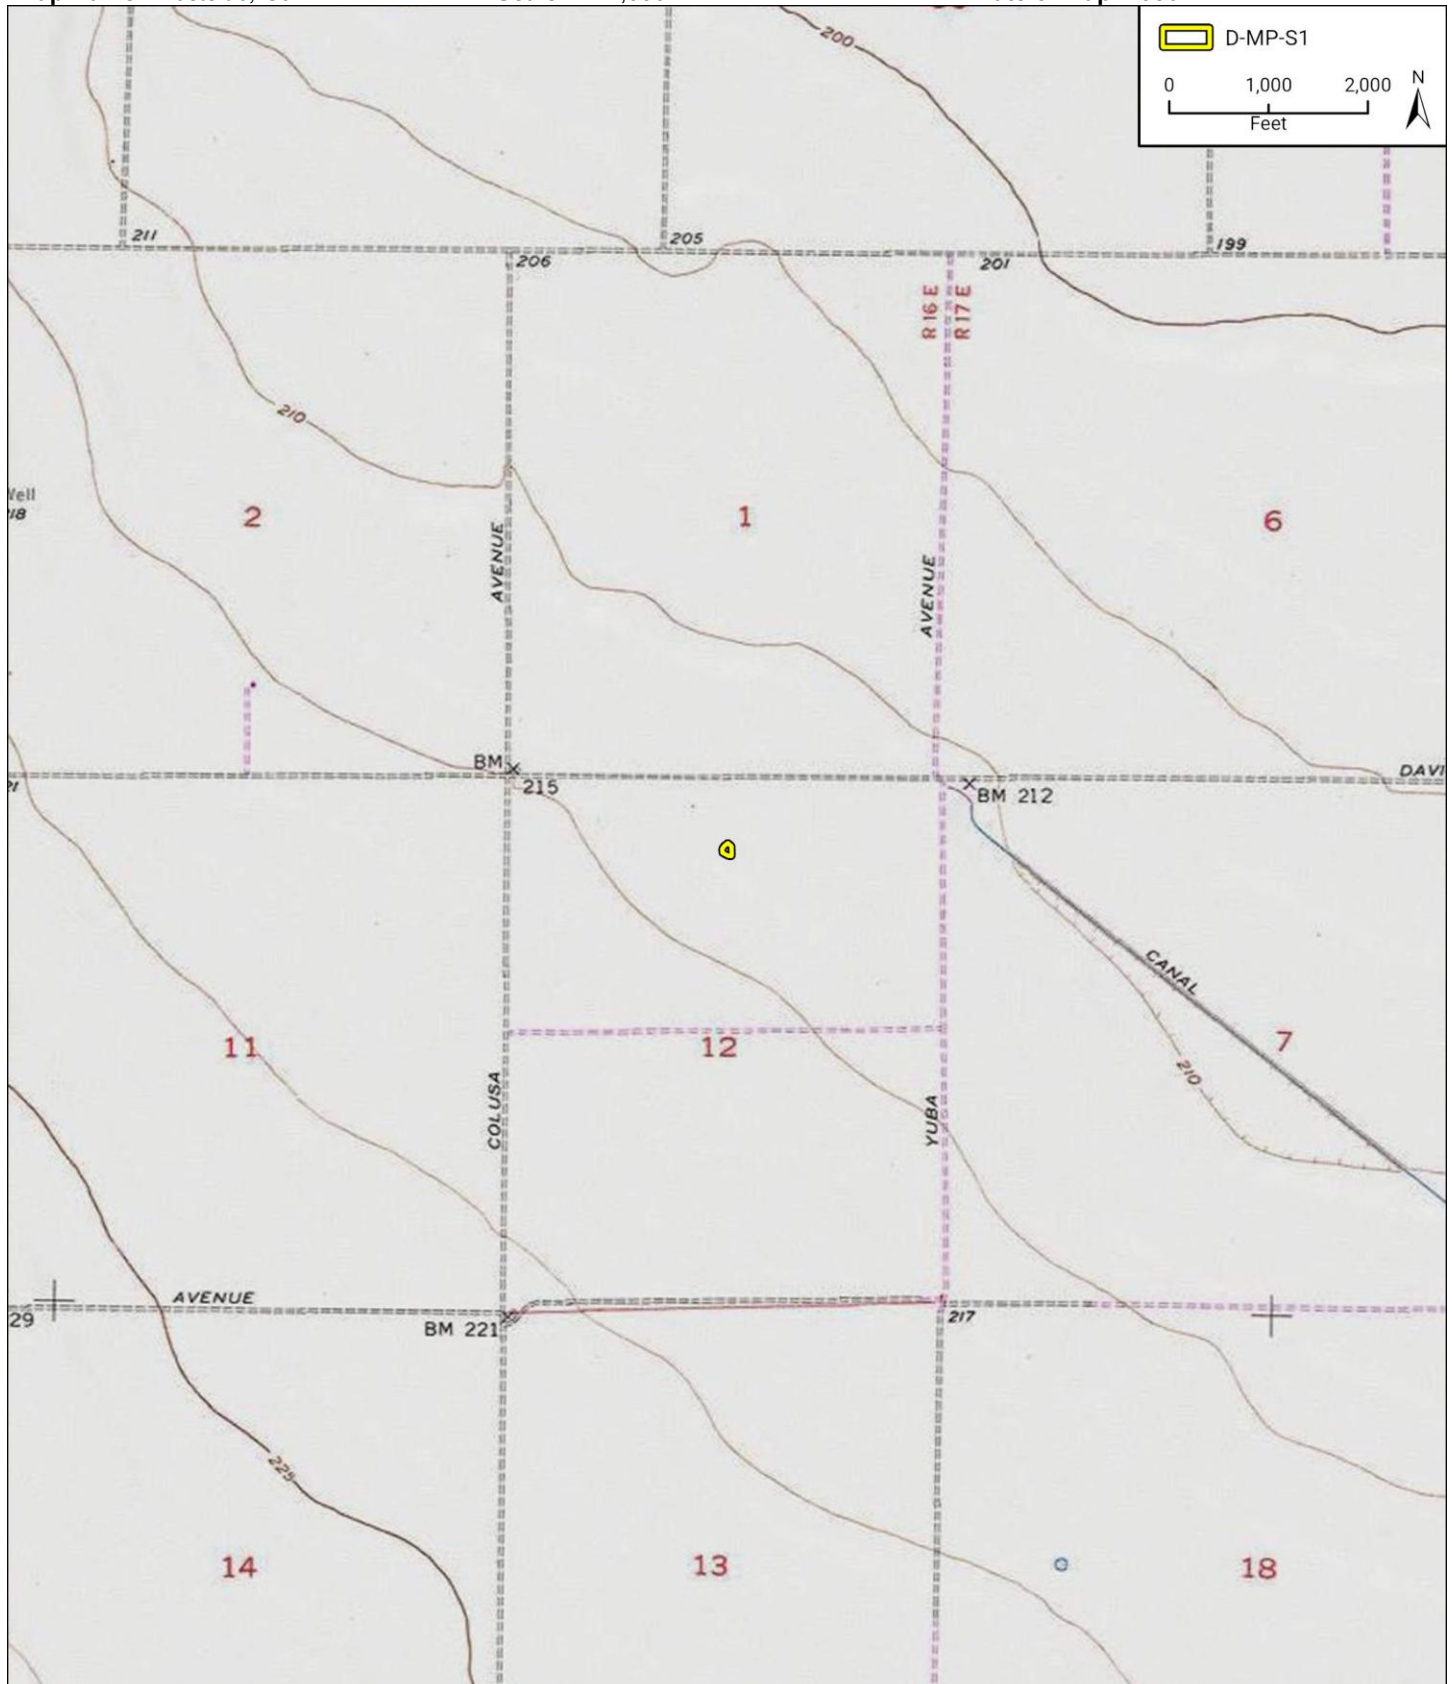

State of California — The Resources Agency
DEPARTMENT OF PARKS AND RECREATION
ARCHAEOLOGICAL SITE RECORD

Primary #:
HRI #:
Trinomial:

Page 3 of 5

*Resource Name or #: D-MP-S1

*A1. Dimensions: **a. Length:** 128.5 ft (North-South) **b. Width:** 94 ft (East-West)
Method of Measurement: ☐ Paced ☐ Taped ☐ Visual Estimate ☒ GPS
Method of Determination: ☒ Artifacts ☐ Features ☐ Soil ☐ Vegetation ☐ Topography ☐ Cut Bank
 ☐ Animal Burrow ☐ Excavation ☐ Property Boundary ☐ Other (Explain):

Reliability of Determination: ☒ High ☐ Medium ☐ Low

Limitations (Check any that apply): ☐ Restricted access ☐ Paved/built over ☐ Site limits incompletely defined
 ☒ Disturbances ☐ Vegetation ☐ Other (Explain):

A2. Depth: **Subsurface Elements:** ☐ Yes ☐ No ☒ Unknown Method of Determination:

*A3. Human Remains Potential: ☐ Yes ☐ No ☐ Possible ☒ Unknown

*A4. Site Contains Features: ☐ Yes ☒ No

*A5. Cultural Constituents: D-MP-S1 contains 10 fragments of obsidian with inclusions.

*A6. Were Specimens Collected? ☒ No ☐ Yes

*A7. Site Condition: ☐ Good ☐ Fair ☒ Poor

Disturbances Present? ☒ Yes ☐ No

Describe Disturbance(s): Disturbances observed include past agricultural activity, active construction and trenching

*A8. Nearest Water: The California Aqueduct is approximately 7 miles to the west.

*A9. Elevation: 203 feet AMSL

A10. Environmental Setting: D-MP-S1 is situated on flat valley agricultural land. Sediments within the resource boundary are comprised of a layer of silty loam fill.

A11. Historical Information:

*A12. Age: ☐ Prehistoric ☐ Protohistoric ☐ 1542-1769 ☐ 1769-1848 ☐ 1848-1880 ☐ 1880-1914 ☐ 1914-1945
 ☐ Post 1945 ☒ Undetermined

A13. Interpretations:

A14. Remarks: Initial observations of the obsidian fragments indicate the material is low quality with inclusions making it an undesirable candidate for the creation of tools. Per agreement with the California Energy Commission and the Tachi Yokut Tribe, the isolate was transferred to the Tachi Yokut Tribe for final disposition following the completion of documentation.


A15. References:

A16. Photographs: See Continuation Sheet
 Original Media/Negatives Kept at: Rincon Consultants, Inc. 2060 Knoll Drive, Ventura, California 93003

*A17. Form Prepared by: Andrea Ogaz

Date: 7/9/2026

Affiliation and Address: Rincon Consultants, Inc. 2060 Knoll Drive, Ventura, California 93003

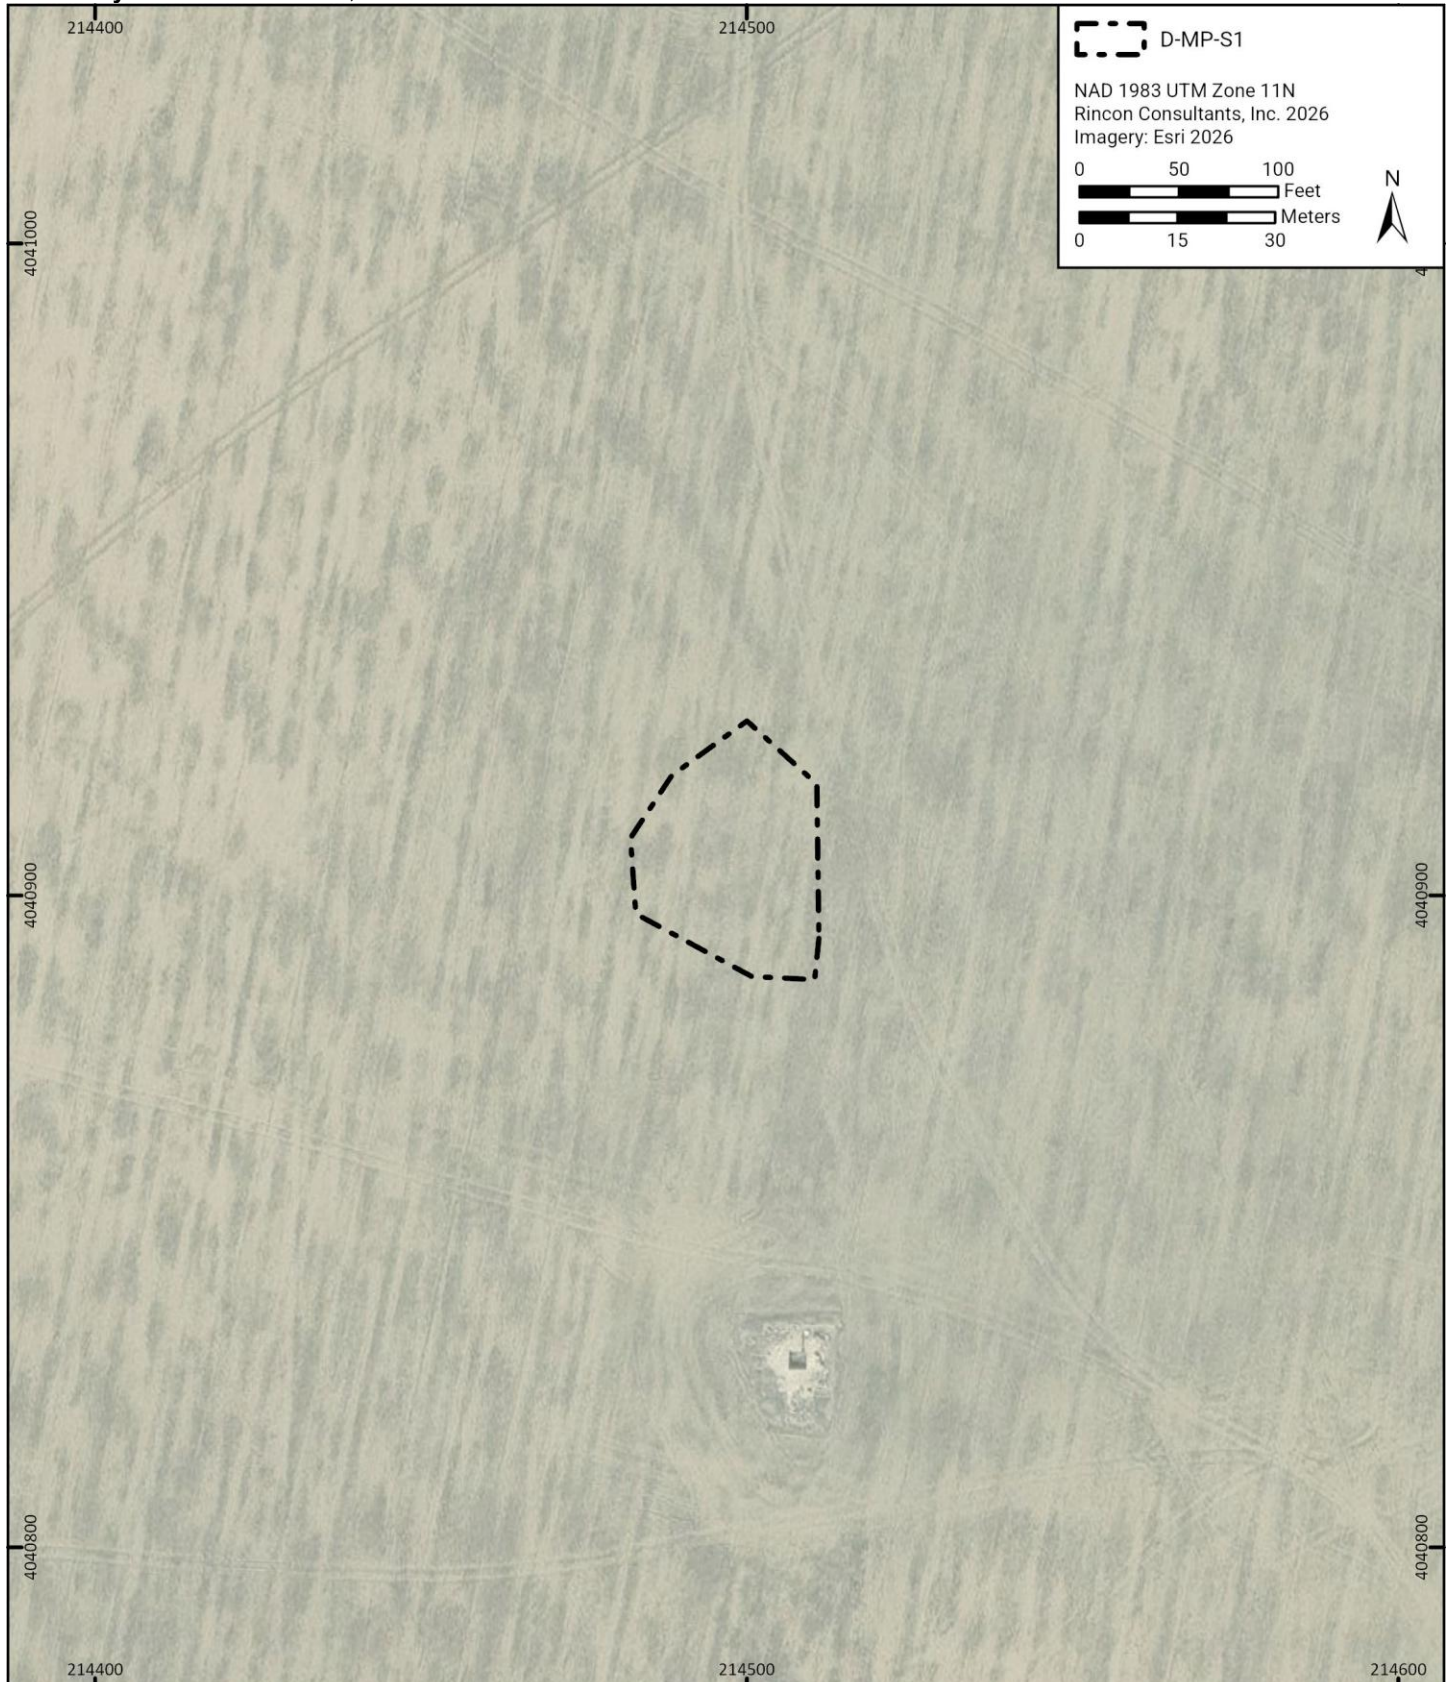

A16. Photographs: continued



Photo 2. Sample of Fragmented Obsidian, Plan View

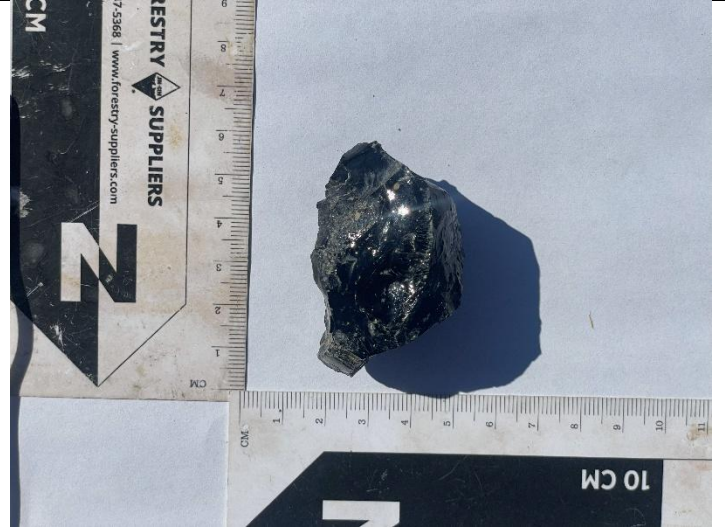


Photo 3. Sample of Fragmented Obsidian with Possible Flaking from Mechanical Equipment, Plan View



Photo 4. Sample of Fragmented Obsidian, Plan View
